



October Shut Day 01 Day Shift – Morning

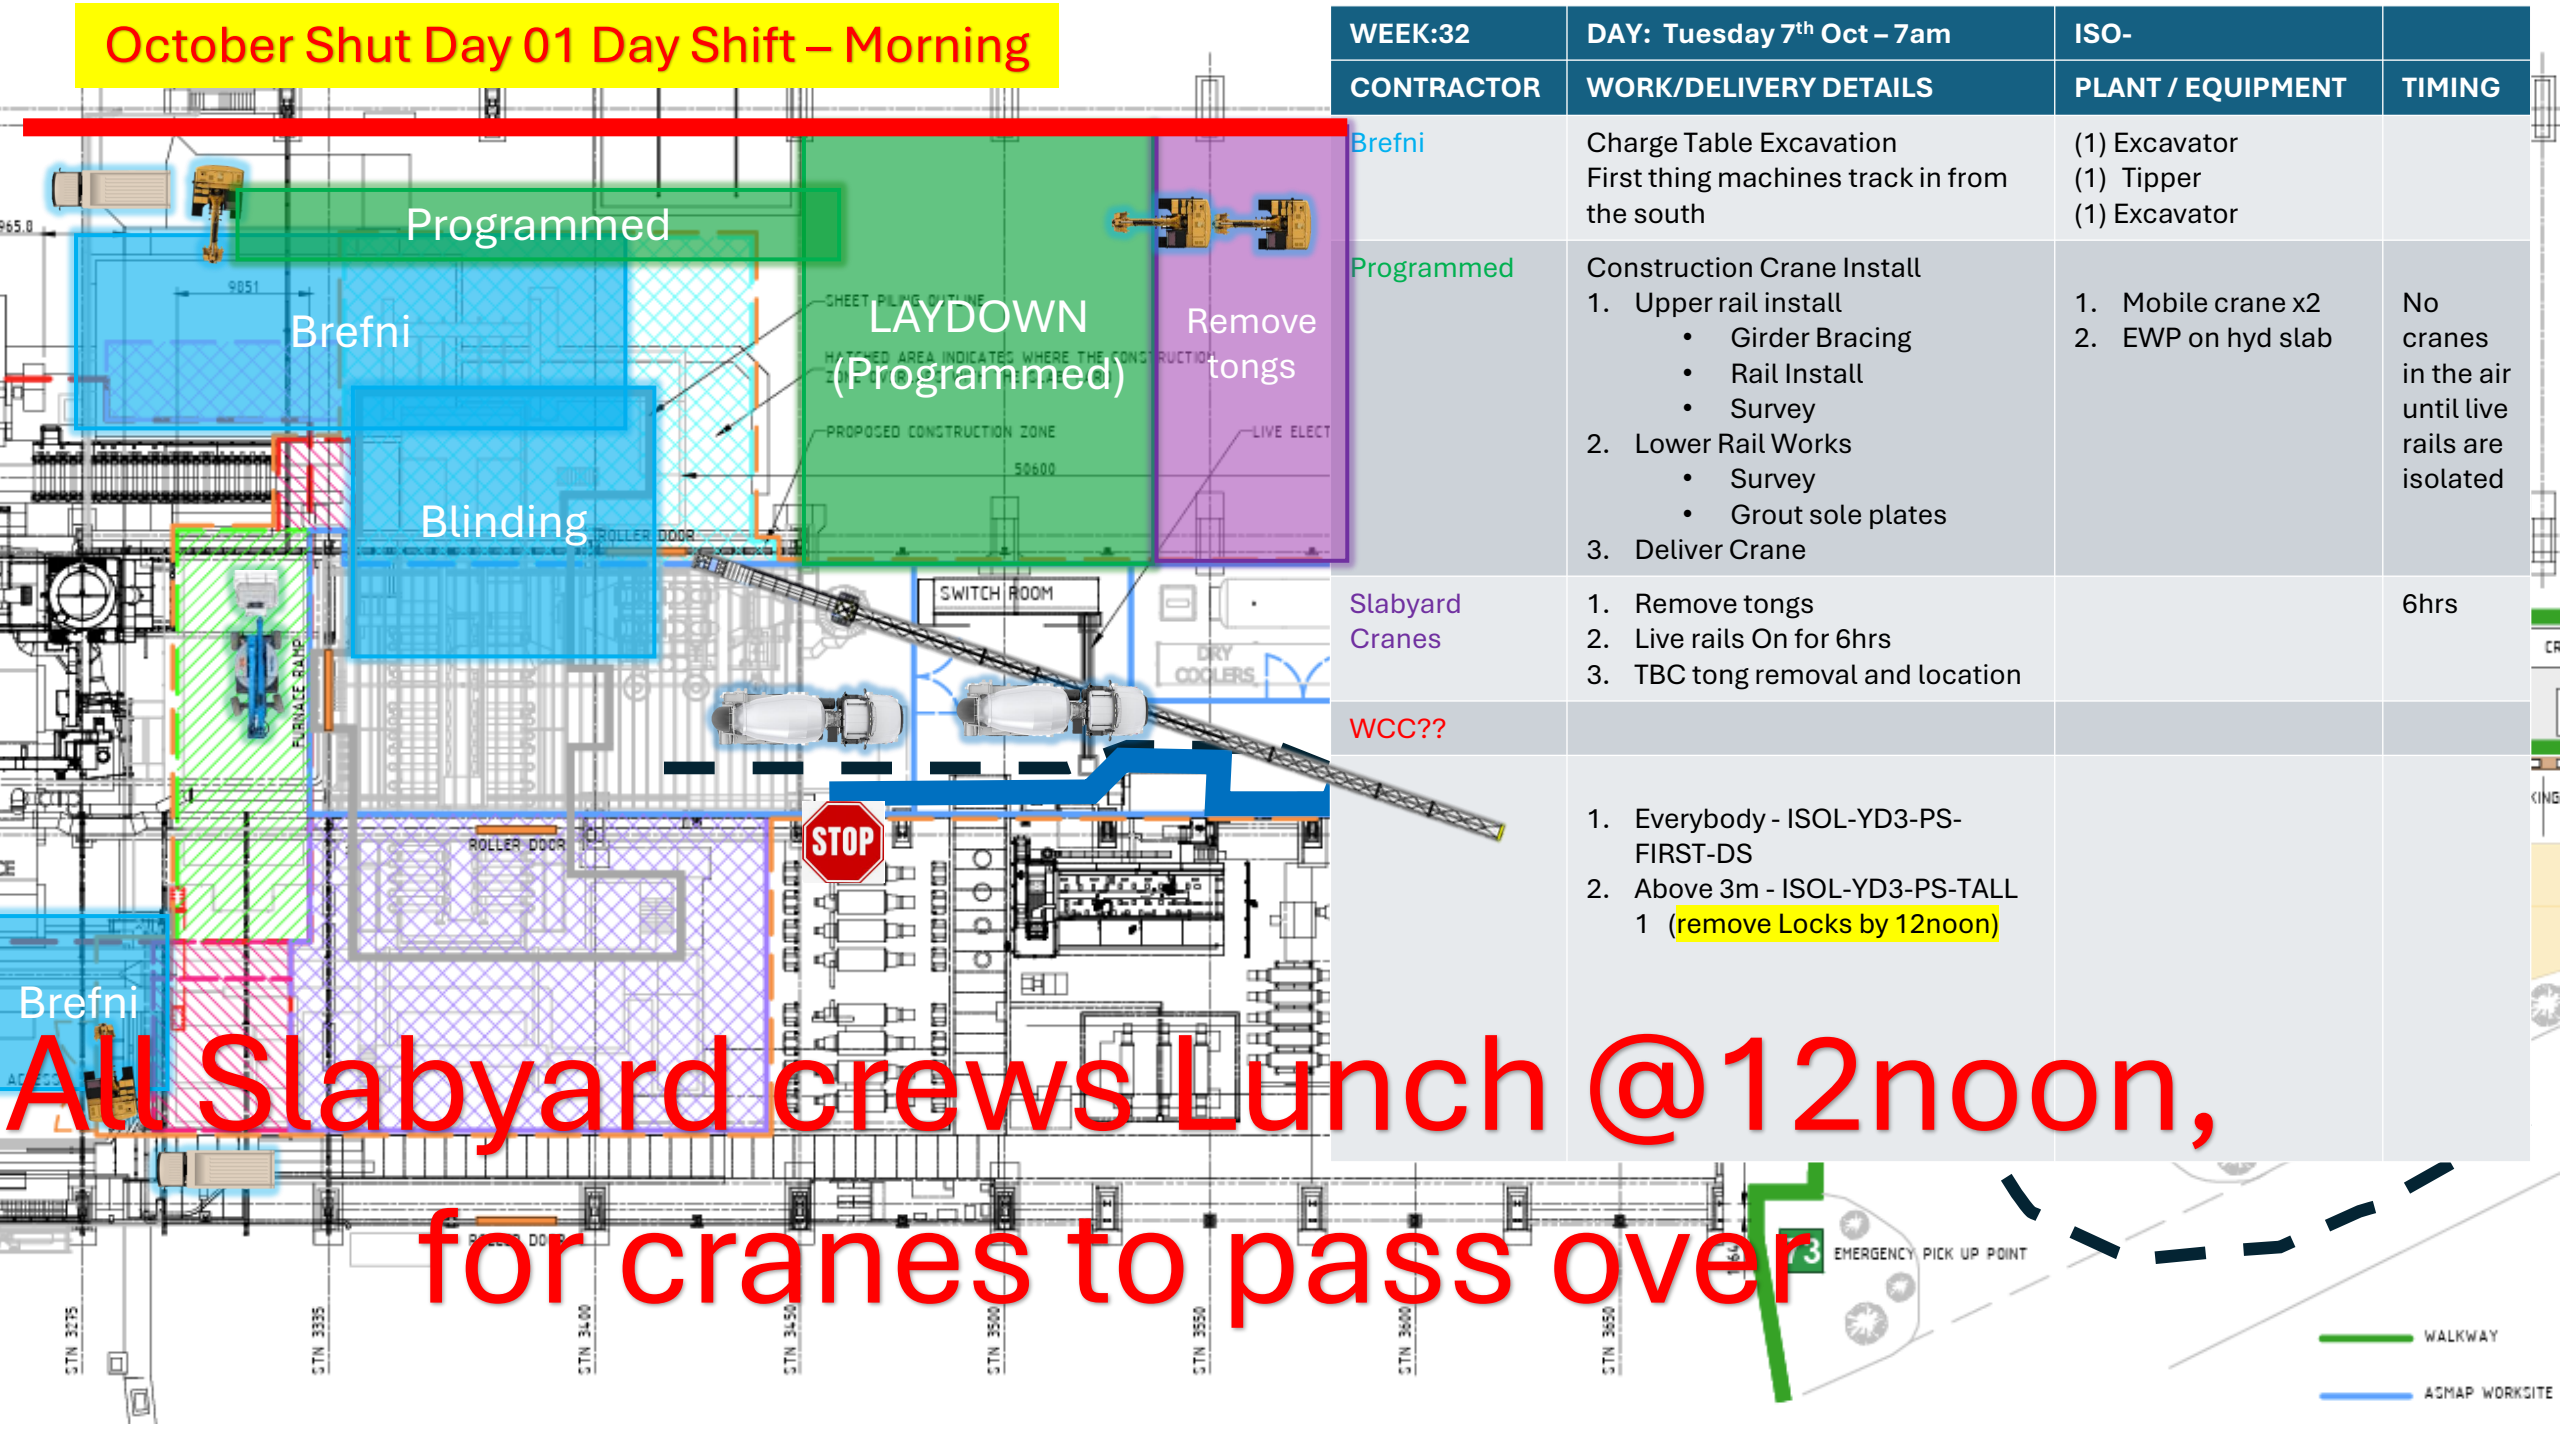

WEEK:32	DAY: Tuesday 7 th Oct – 7am	ISO-	
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation First thing machines track in from the south	(1) Excavator (1) Tipper (1) Excavator	
Programmed	Construction Crane Install 1. Upper rail install - Girder Bracing - Rail Install - Survey 2. Lower Rail Works - Survey - Grout sole plates 3. Deliver Crane	1. Mobile crane x2 2. EWP on hyd slab	No cranes in the air until live rails are isolated
Slabyard Cranes	1. Remove tongs 2. Live rails On for 6hrs 3. TBC tong removal and location		6hrs
WCC??	1. Everybody - ISOL-YD3-PS-FIRST-DS 2. Above 3m - ISOL-YD3-PS-TALL 1 (remove Locks by 12noon)		

All Slabyard crews Lunch @12noon,
for cranes to pass over


October Shut Day 01 Day Shift - Afternoon

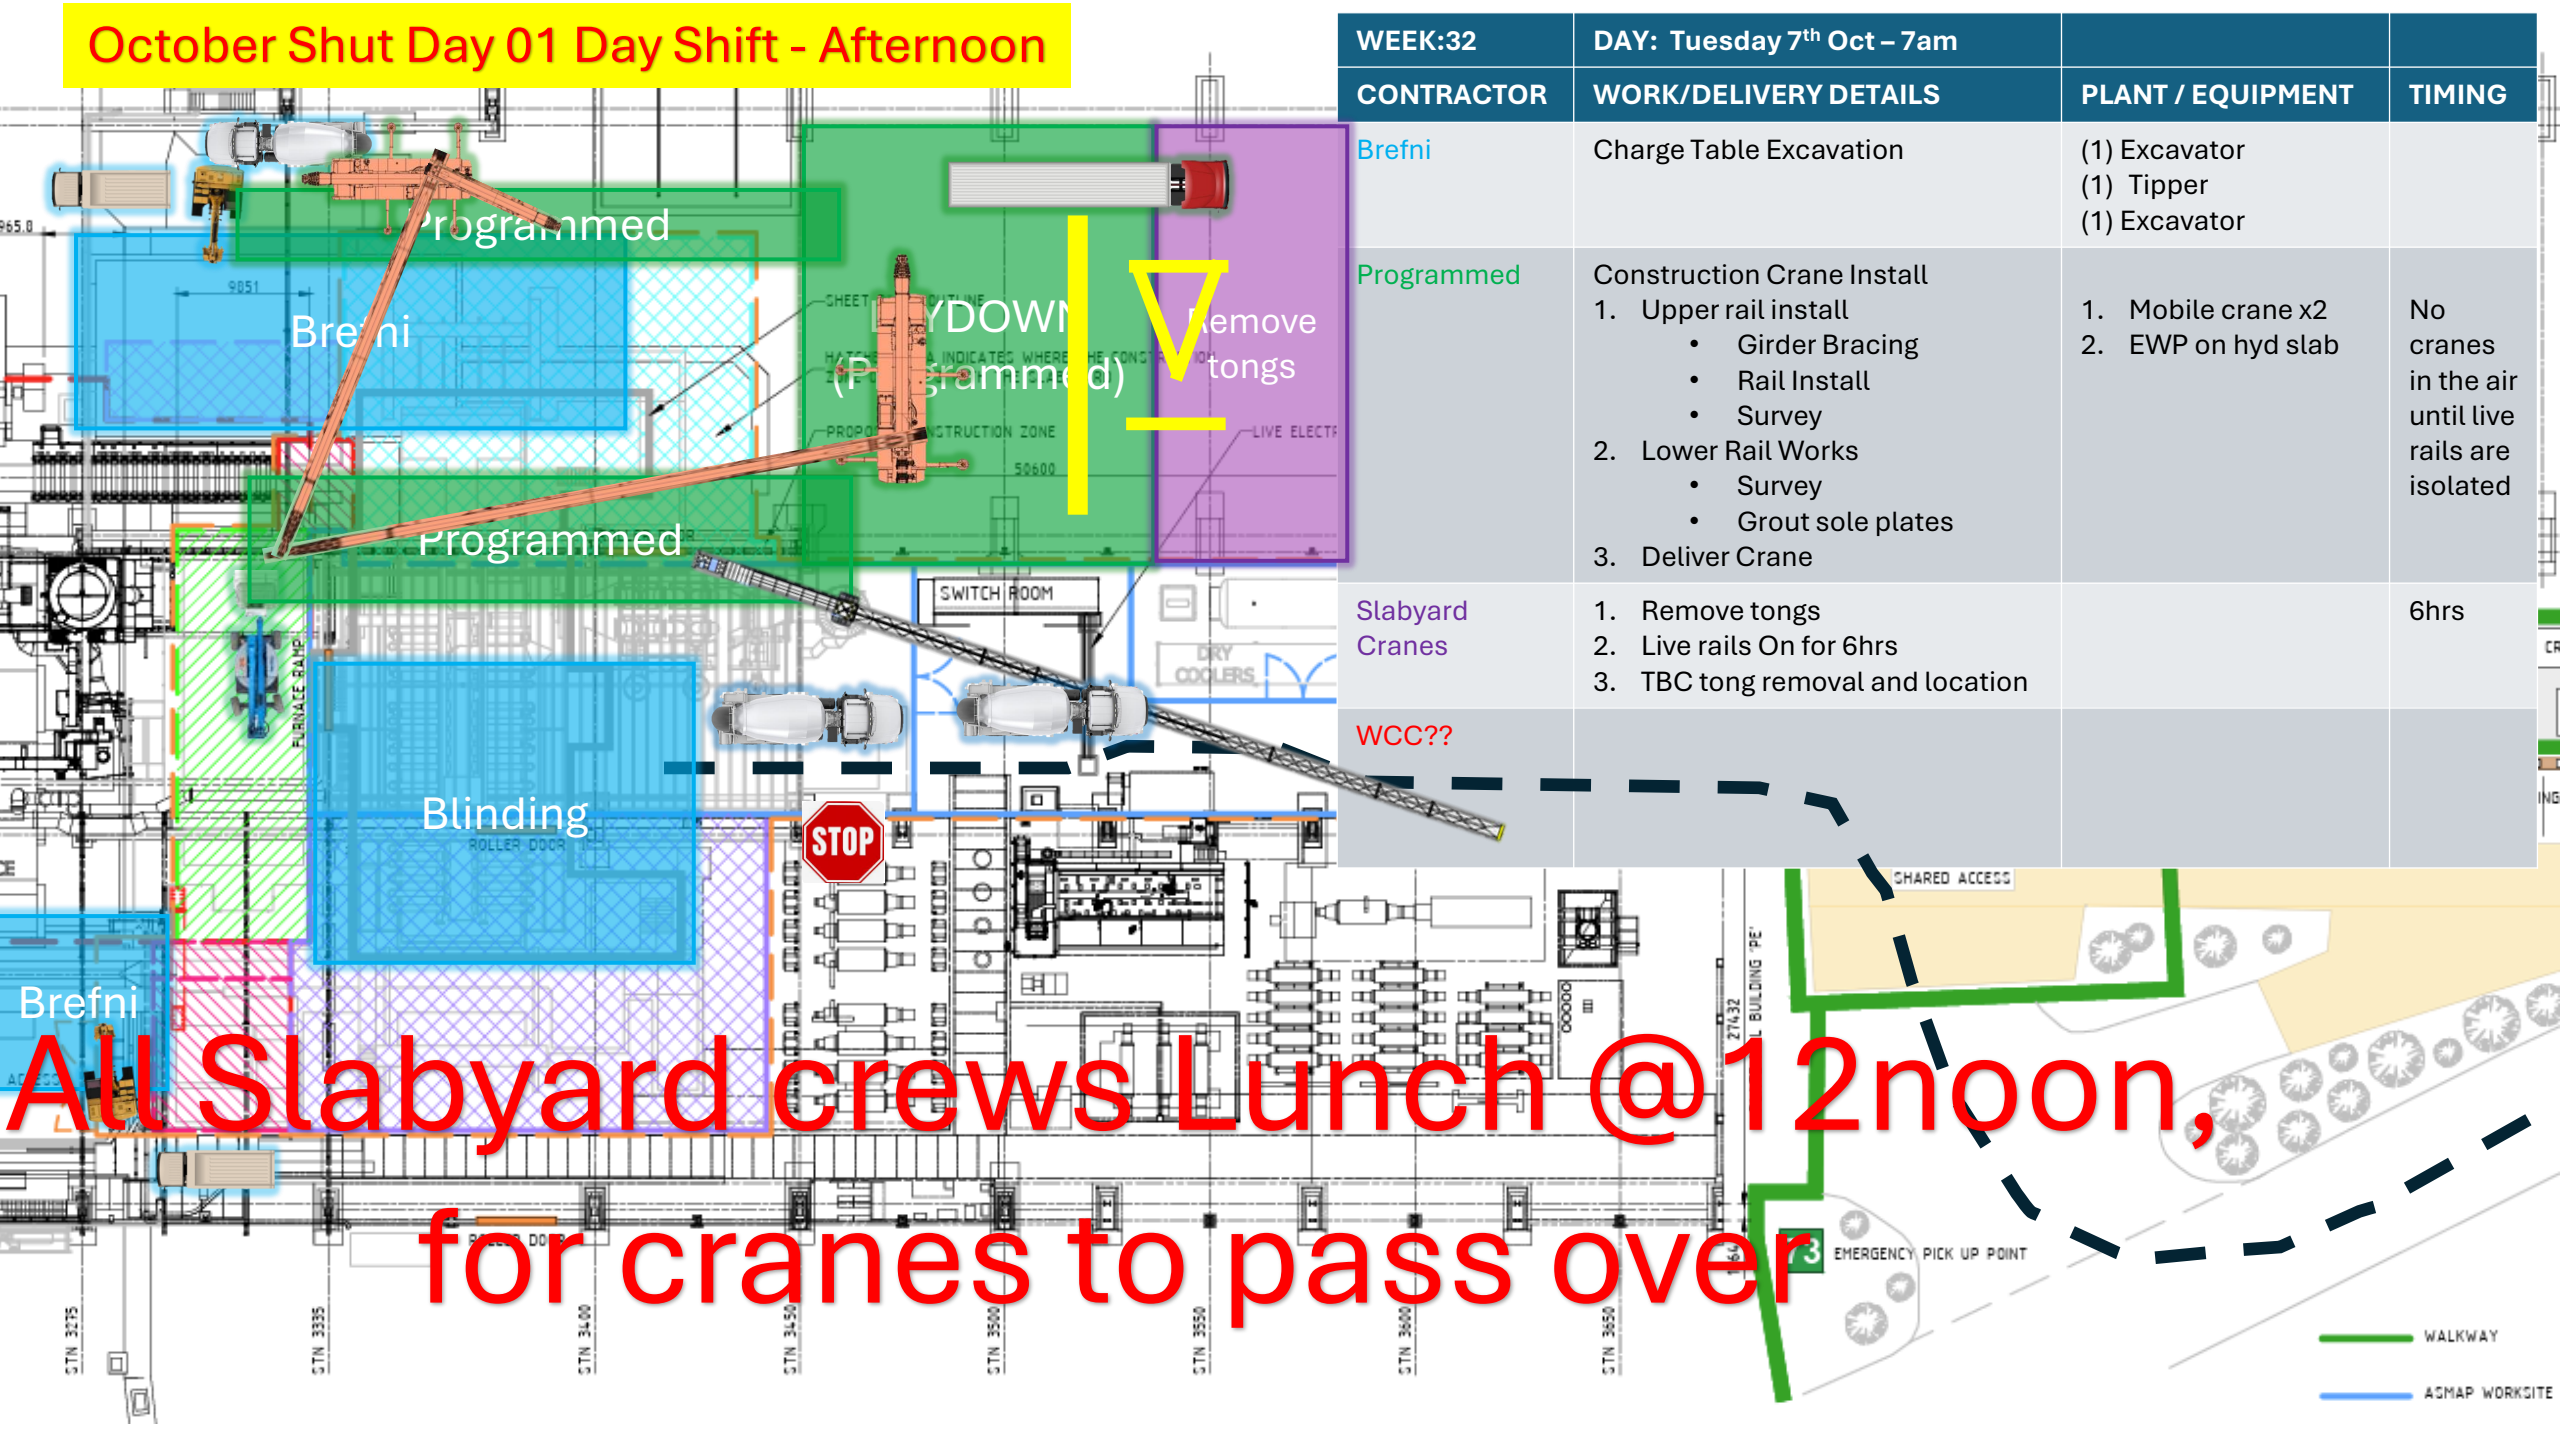

WEEK:32	DAY: Tuesday 7 th Oct – 7am		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation	(1) Excavator (1) Tipper (1) Excavator	
Programmed	Construction Crane Install 1. Upper rail install - Girder Bracing - Rail Install - Survey 2. Lower Rail Works - Survey - Grout sole plates 3. Deliver Crane	1. Mobile crane x2 2. EWP on hyd slab	No cranes in the air until live rails are isolated
Slabyard Cranes	1. Remove tongs 2. Live rails On for 6hrs 3. TBC tong removal and location		6hrs
WCC??			


All Slabyard crews Lunch @ 12noon,
for cranes to pass over

October Shut Day 01 Night Shift

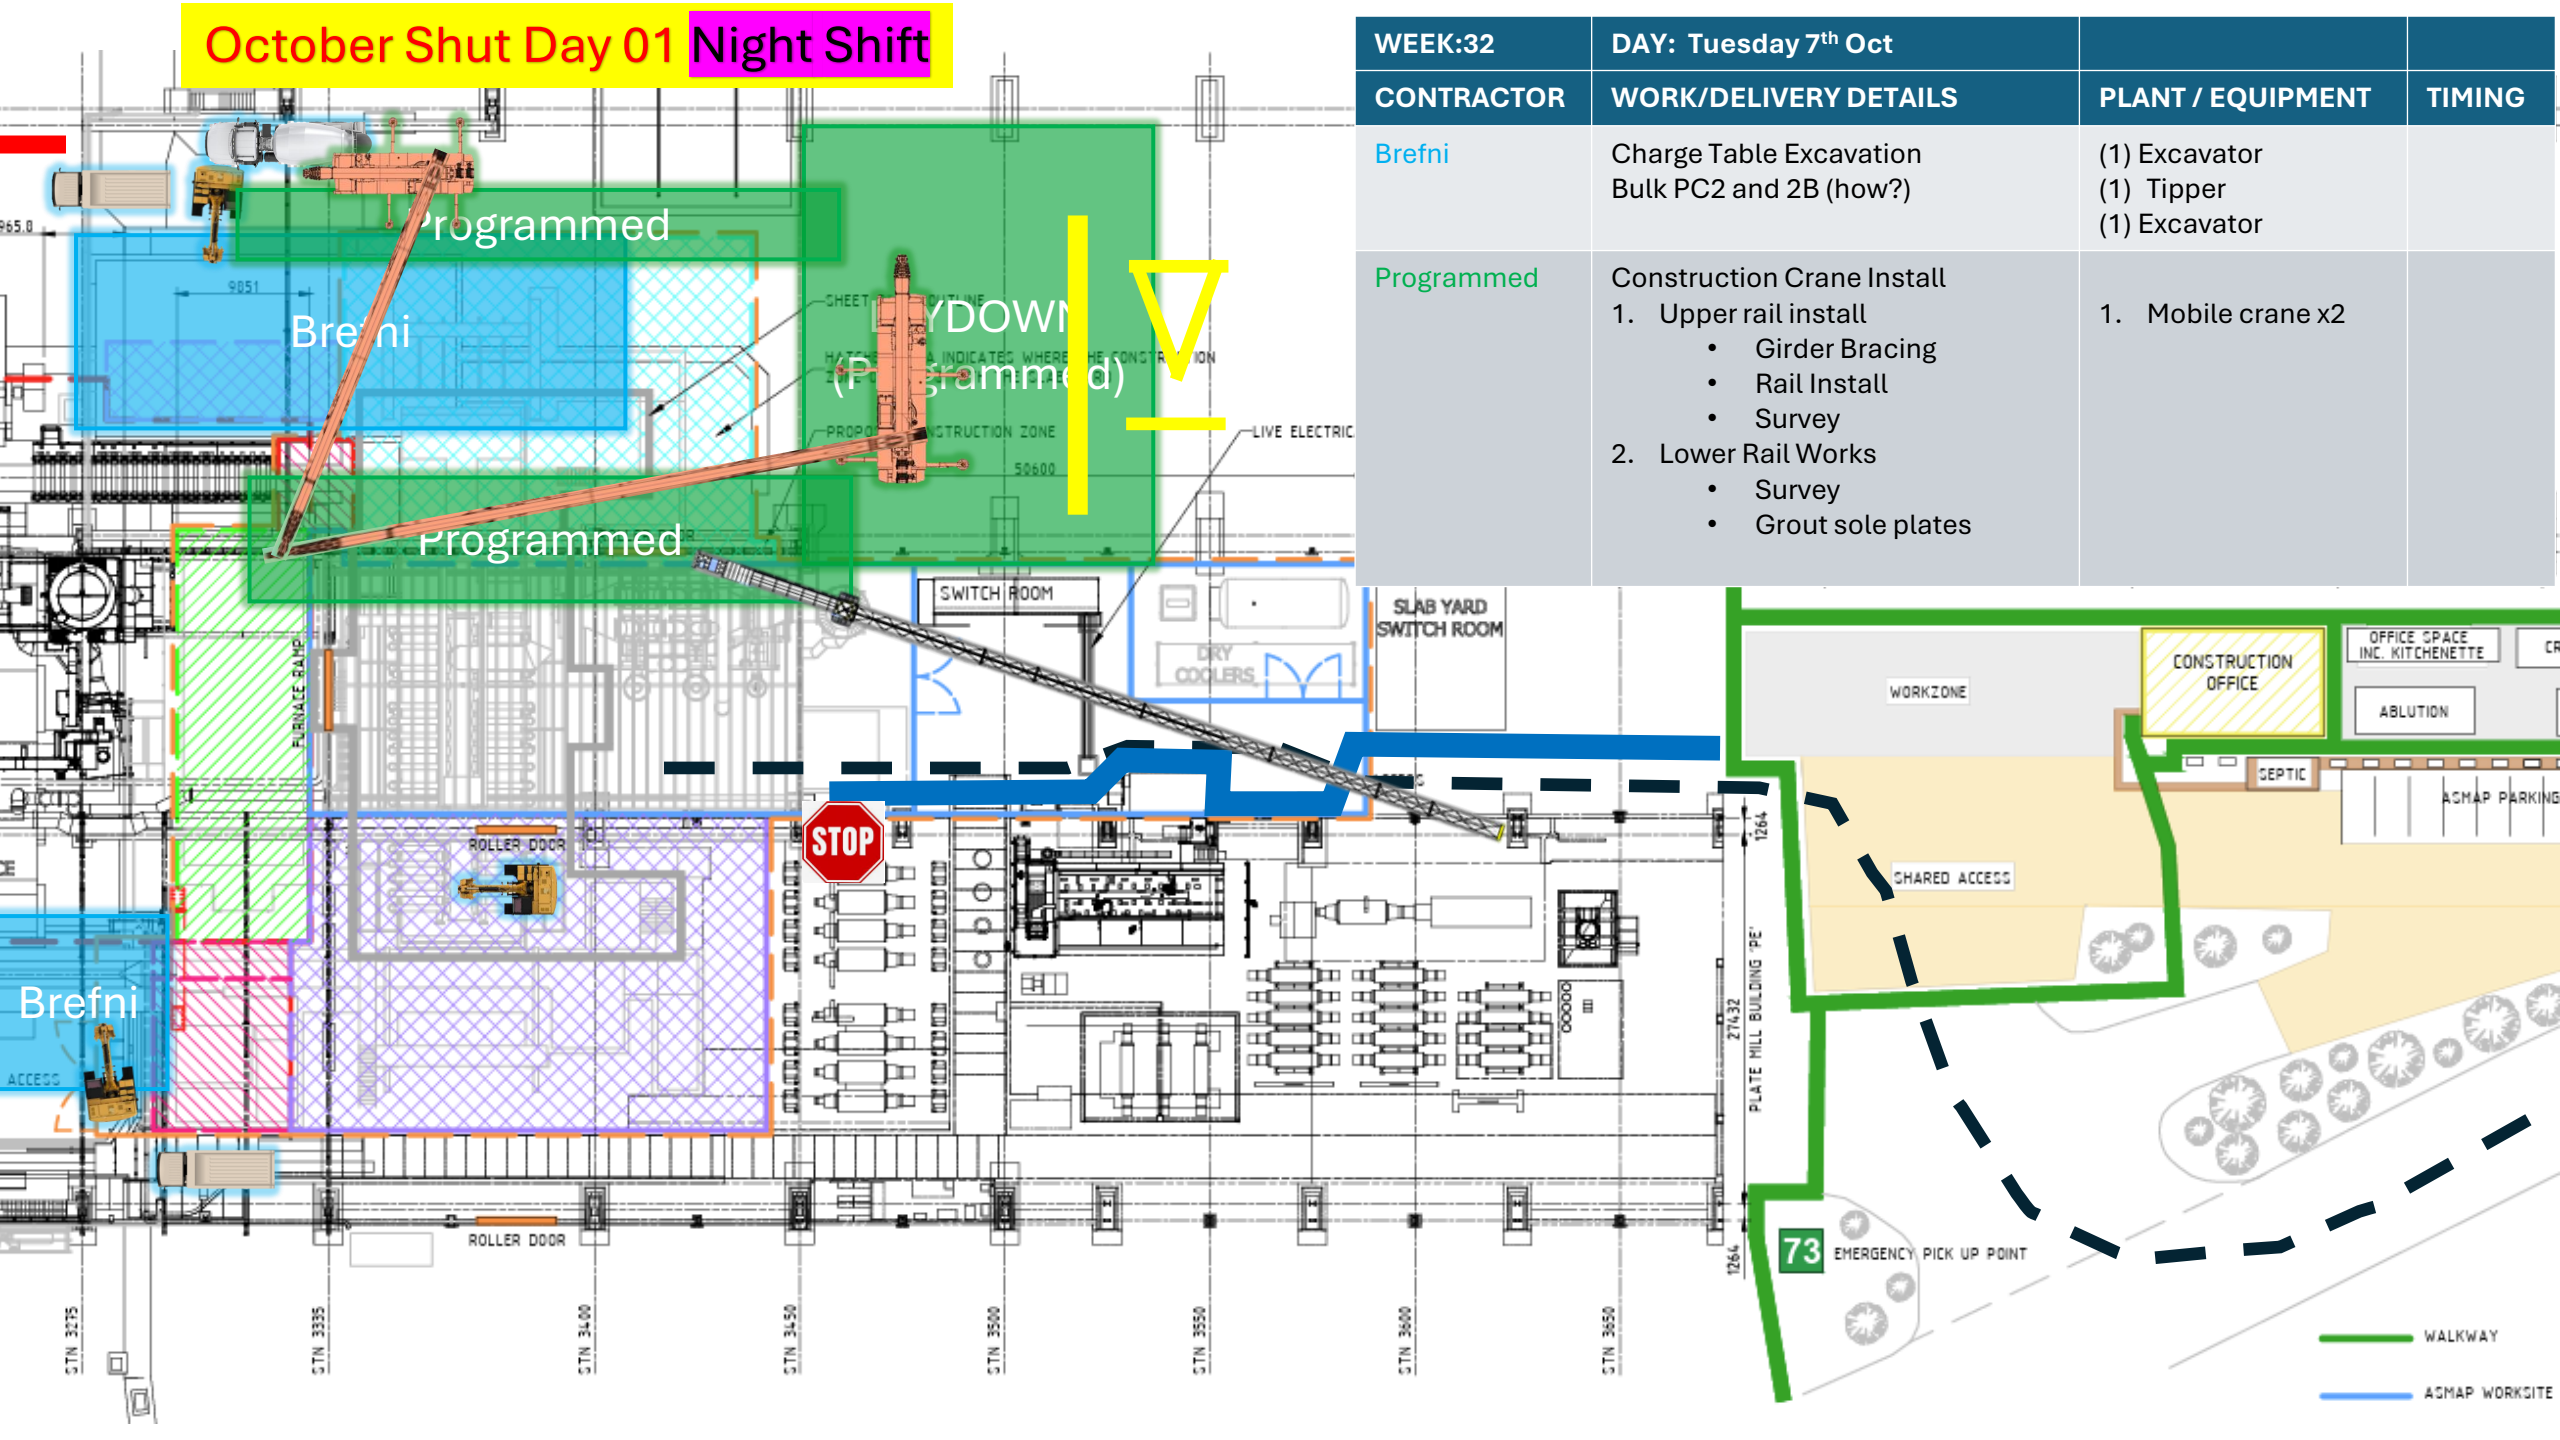


WEEK:32	DAY: Tuesday 7 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation Bulk PC2 and 2B (how?)	(1) Excavator (1) Tipper (1) Excavator	
Programmed	Construction Crane Install 1. Upper rail install - Girder Bracing - Rail Install - Survey 2. Lower Rail Works - Survey - Grout sole plates	1. Mobile crane x2	

October Shut Day 02 Day Shift

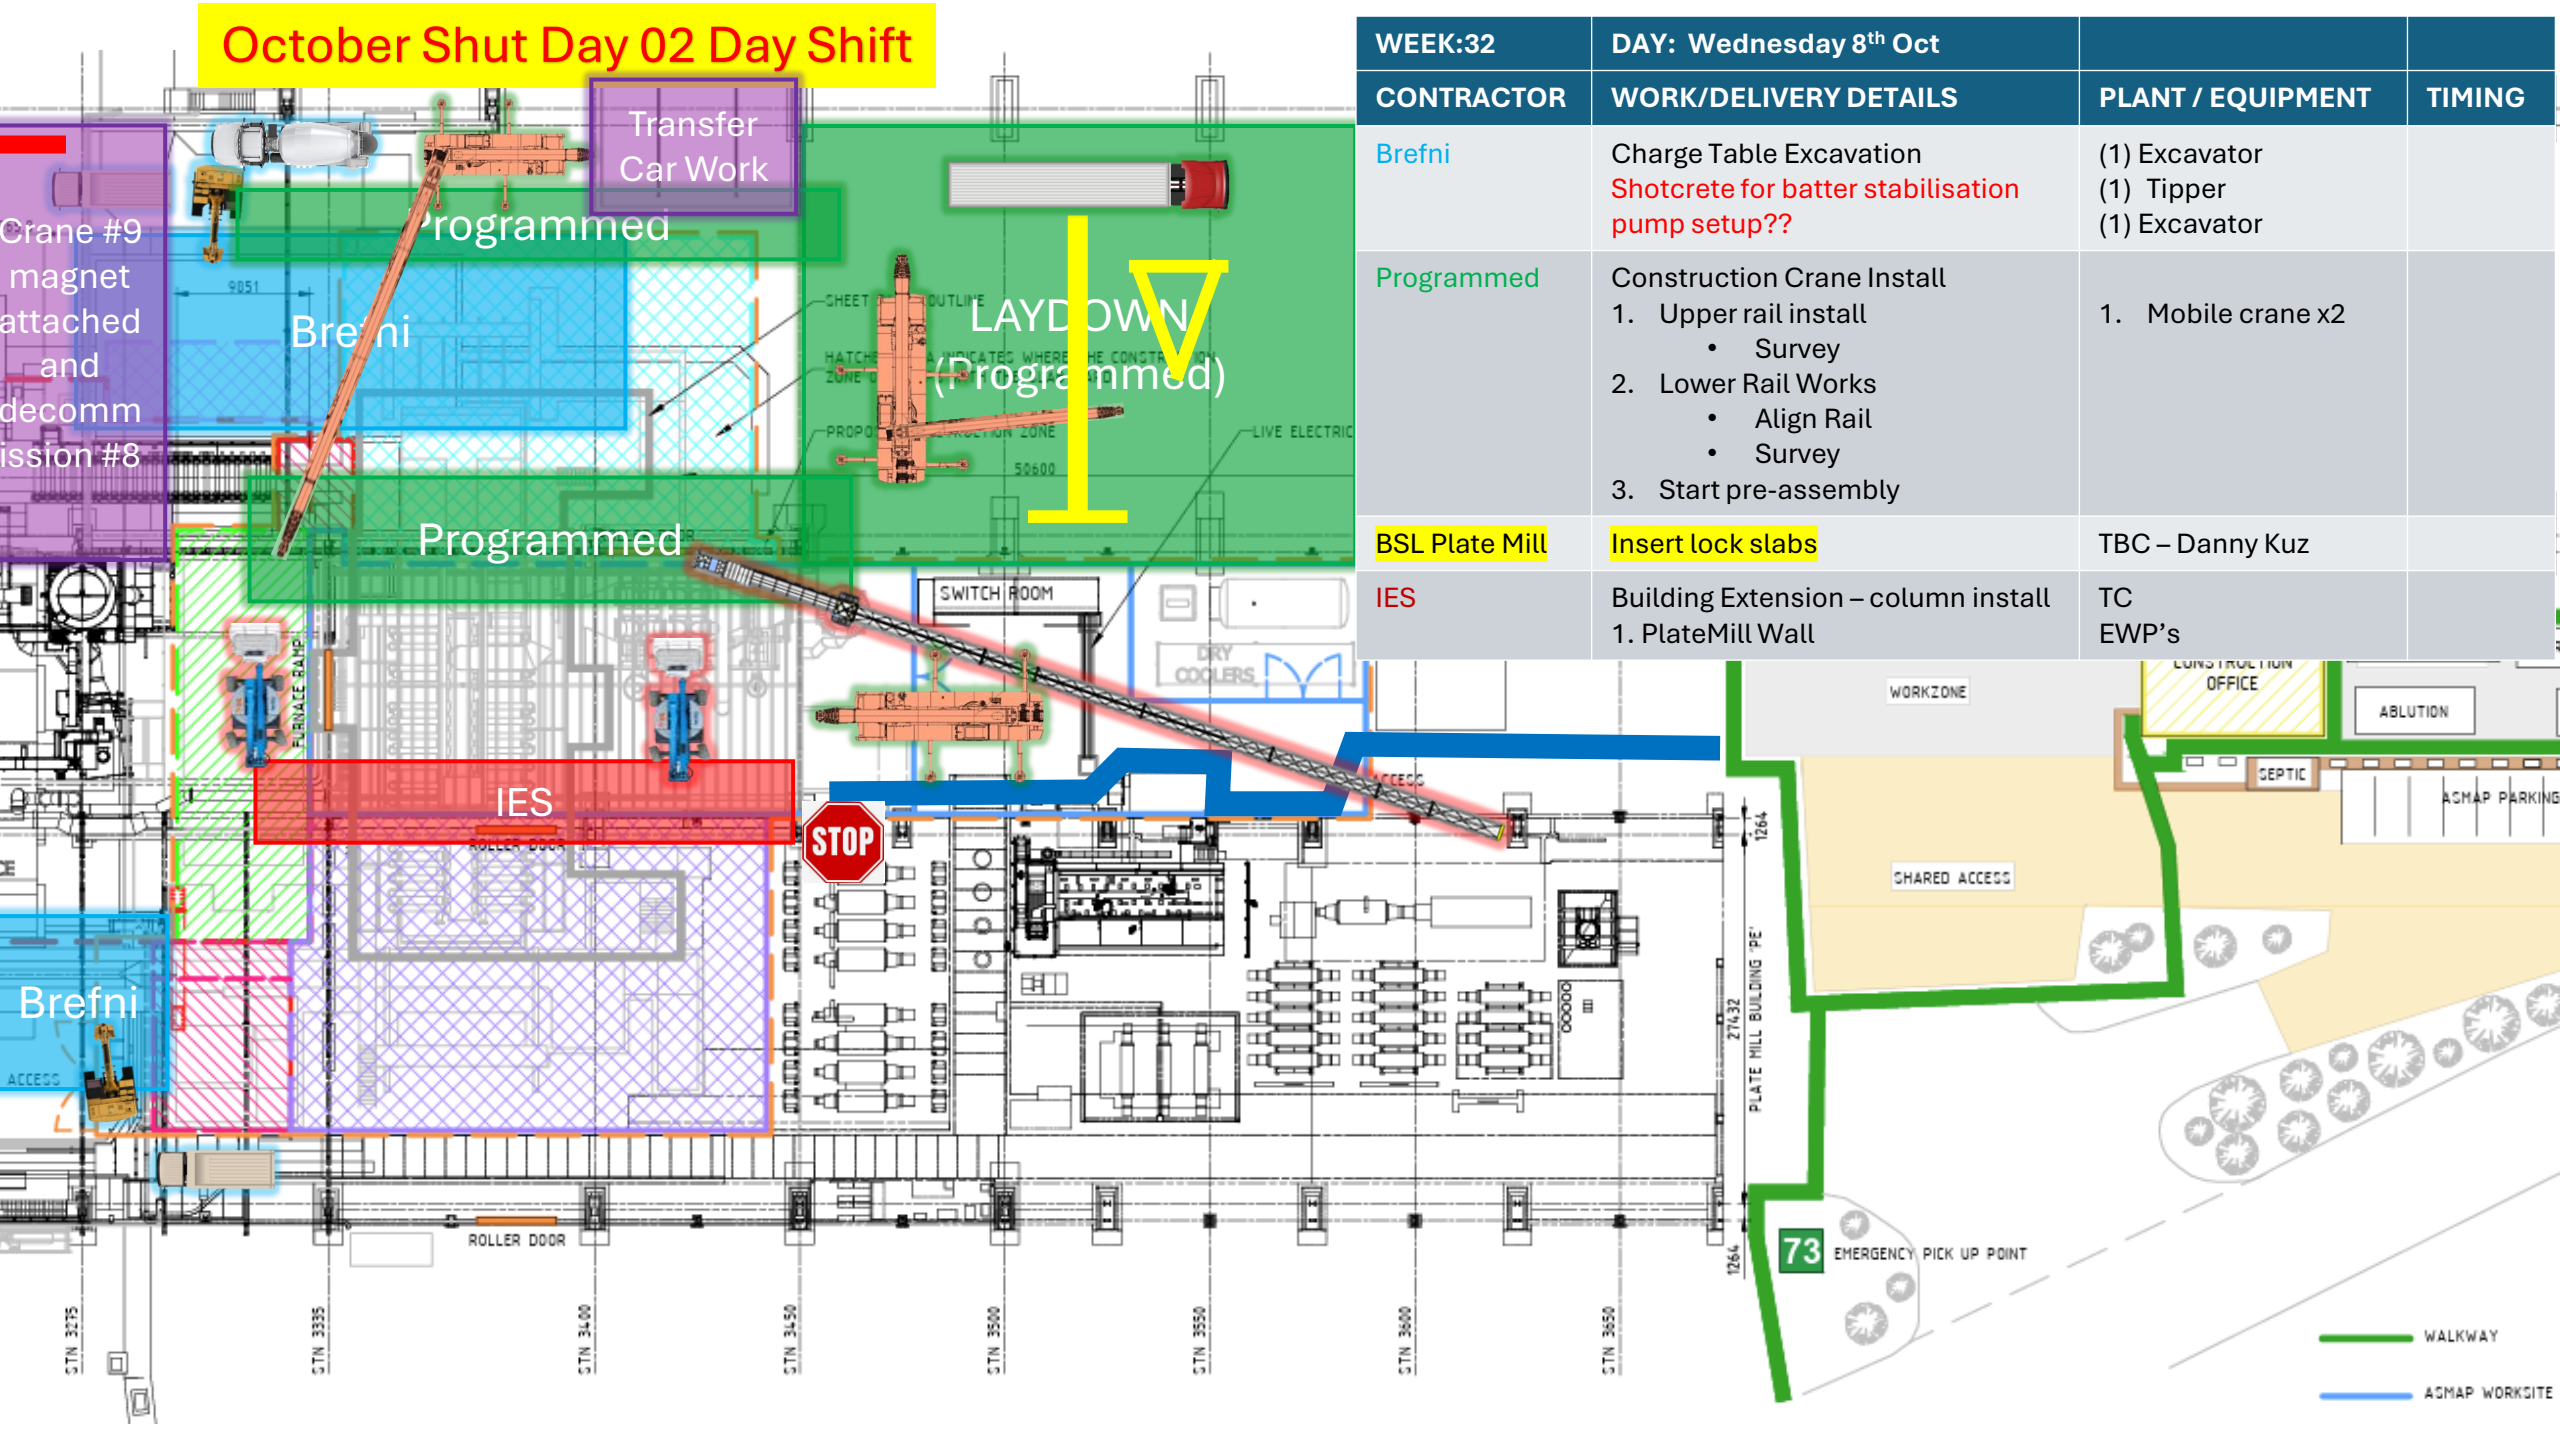


WEEK:32	DAY: Wednesday 8 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation Shotcrete for batter stabilisation pump setup??	(1) Excavator (1) Tipper (1) Excavator	
Programmed	Construction Crane Install 1. Upper rail install • Survey 2. Lower Rail Works • Align Rail • Survey 3. Start pre-assembly	1. Mobile crane x2	
BSL Plate Mill	Insert lock slabs	TBC – Danny Kuz	
IES	Building Extension – column install 1. PlateMill Wall	TC EWP's	

October Shut Day 02 Night Shift

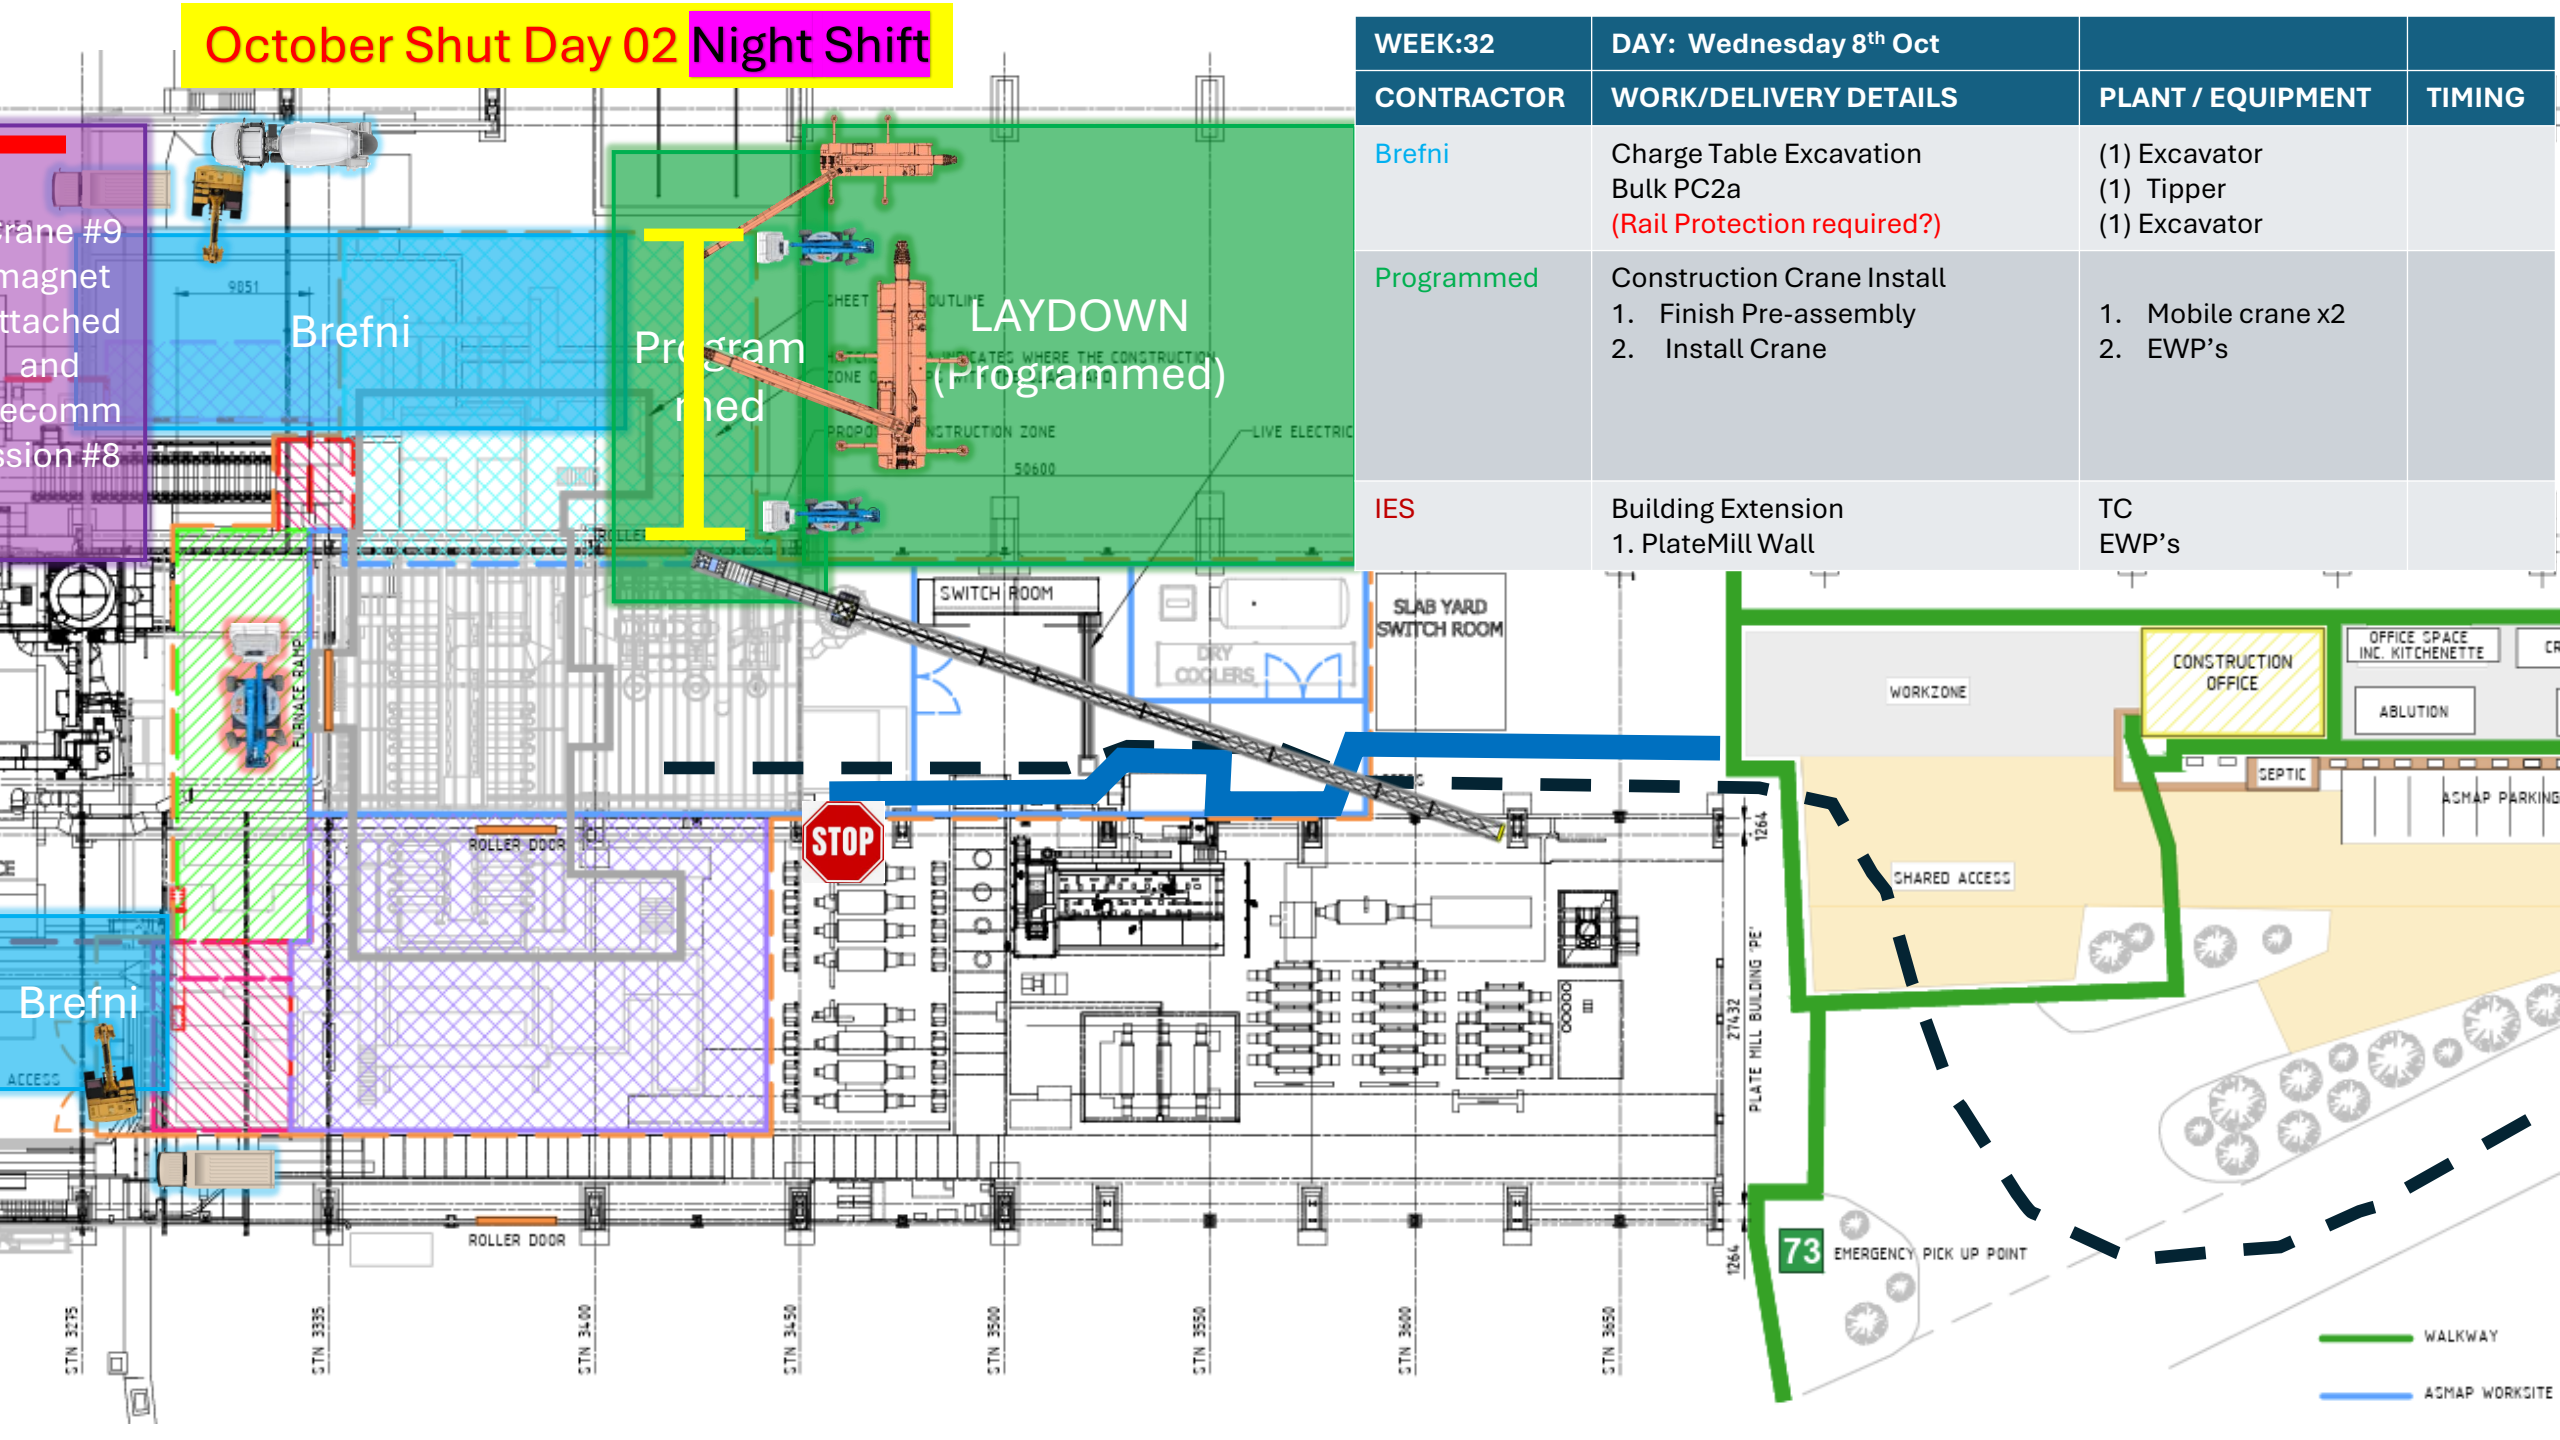


WEEK:32	DAY: Wednesday 8 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation Bulk PC2a (Rail Protection required?)	(1) Excavator (1) Tipper (1) Excavator	
Programmed	Construction Crane Install 1. Finish Pre-assembly 2. Install Crane	1. Mobile crane x2 2. EWP's	
IES	Building Extension 1. PlateMill Wall	TC EWP's	

October Shut Day 03 Night Shift

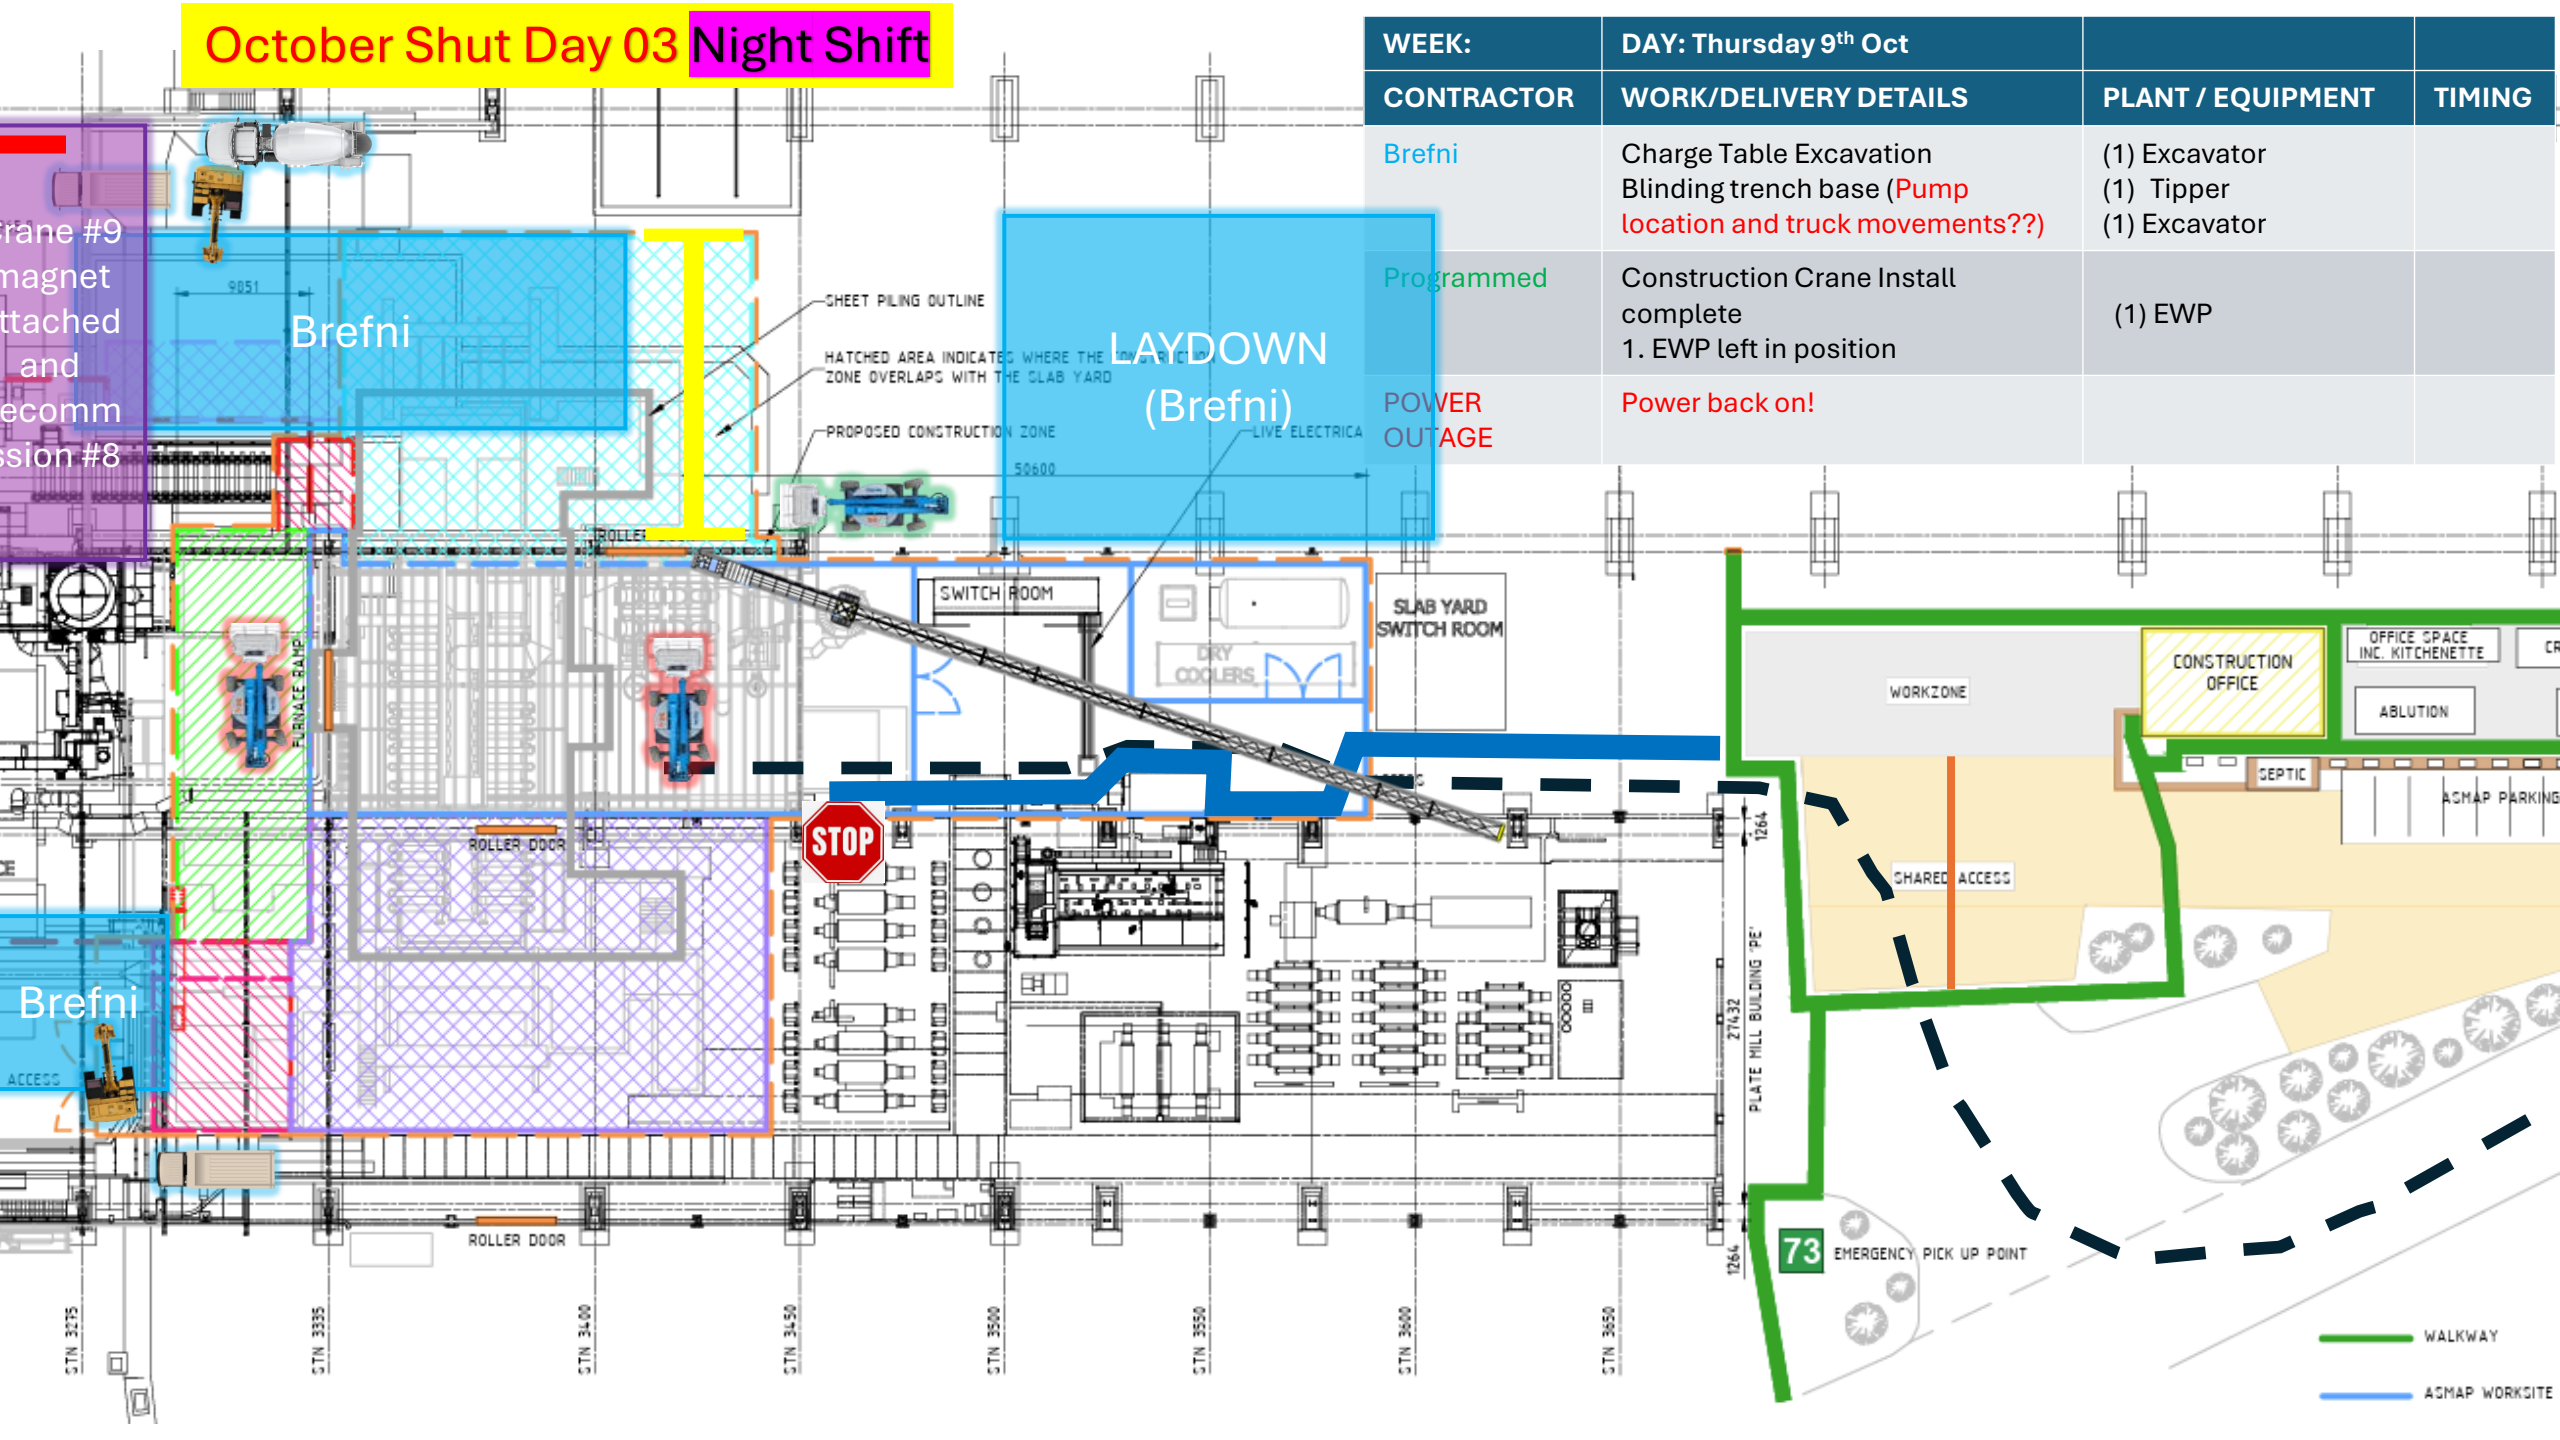

WEEK:	DAY: Thursday 9 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation Blinding trench base (Pump location and truck movements??)	(1) Excavator (1) Tipper (1) Excavator	
Programmed	Construction Crane Install complete 1. EWP left in position	(1) EWP	
POWER OUTAGE	Power back on!		

October Shut Day 04 Day Shift

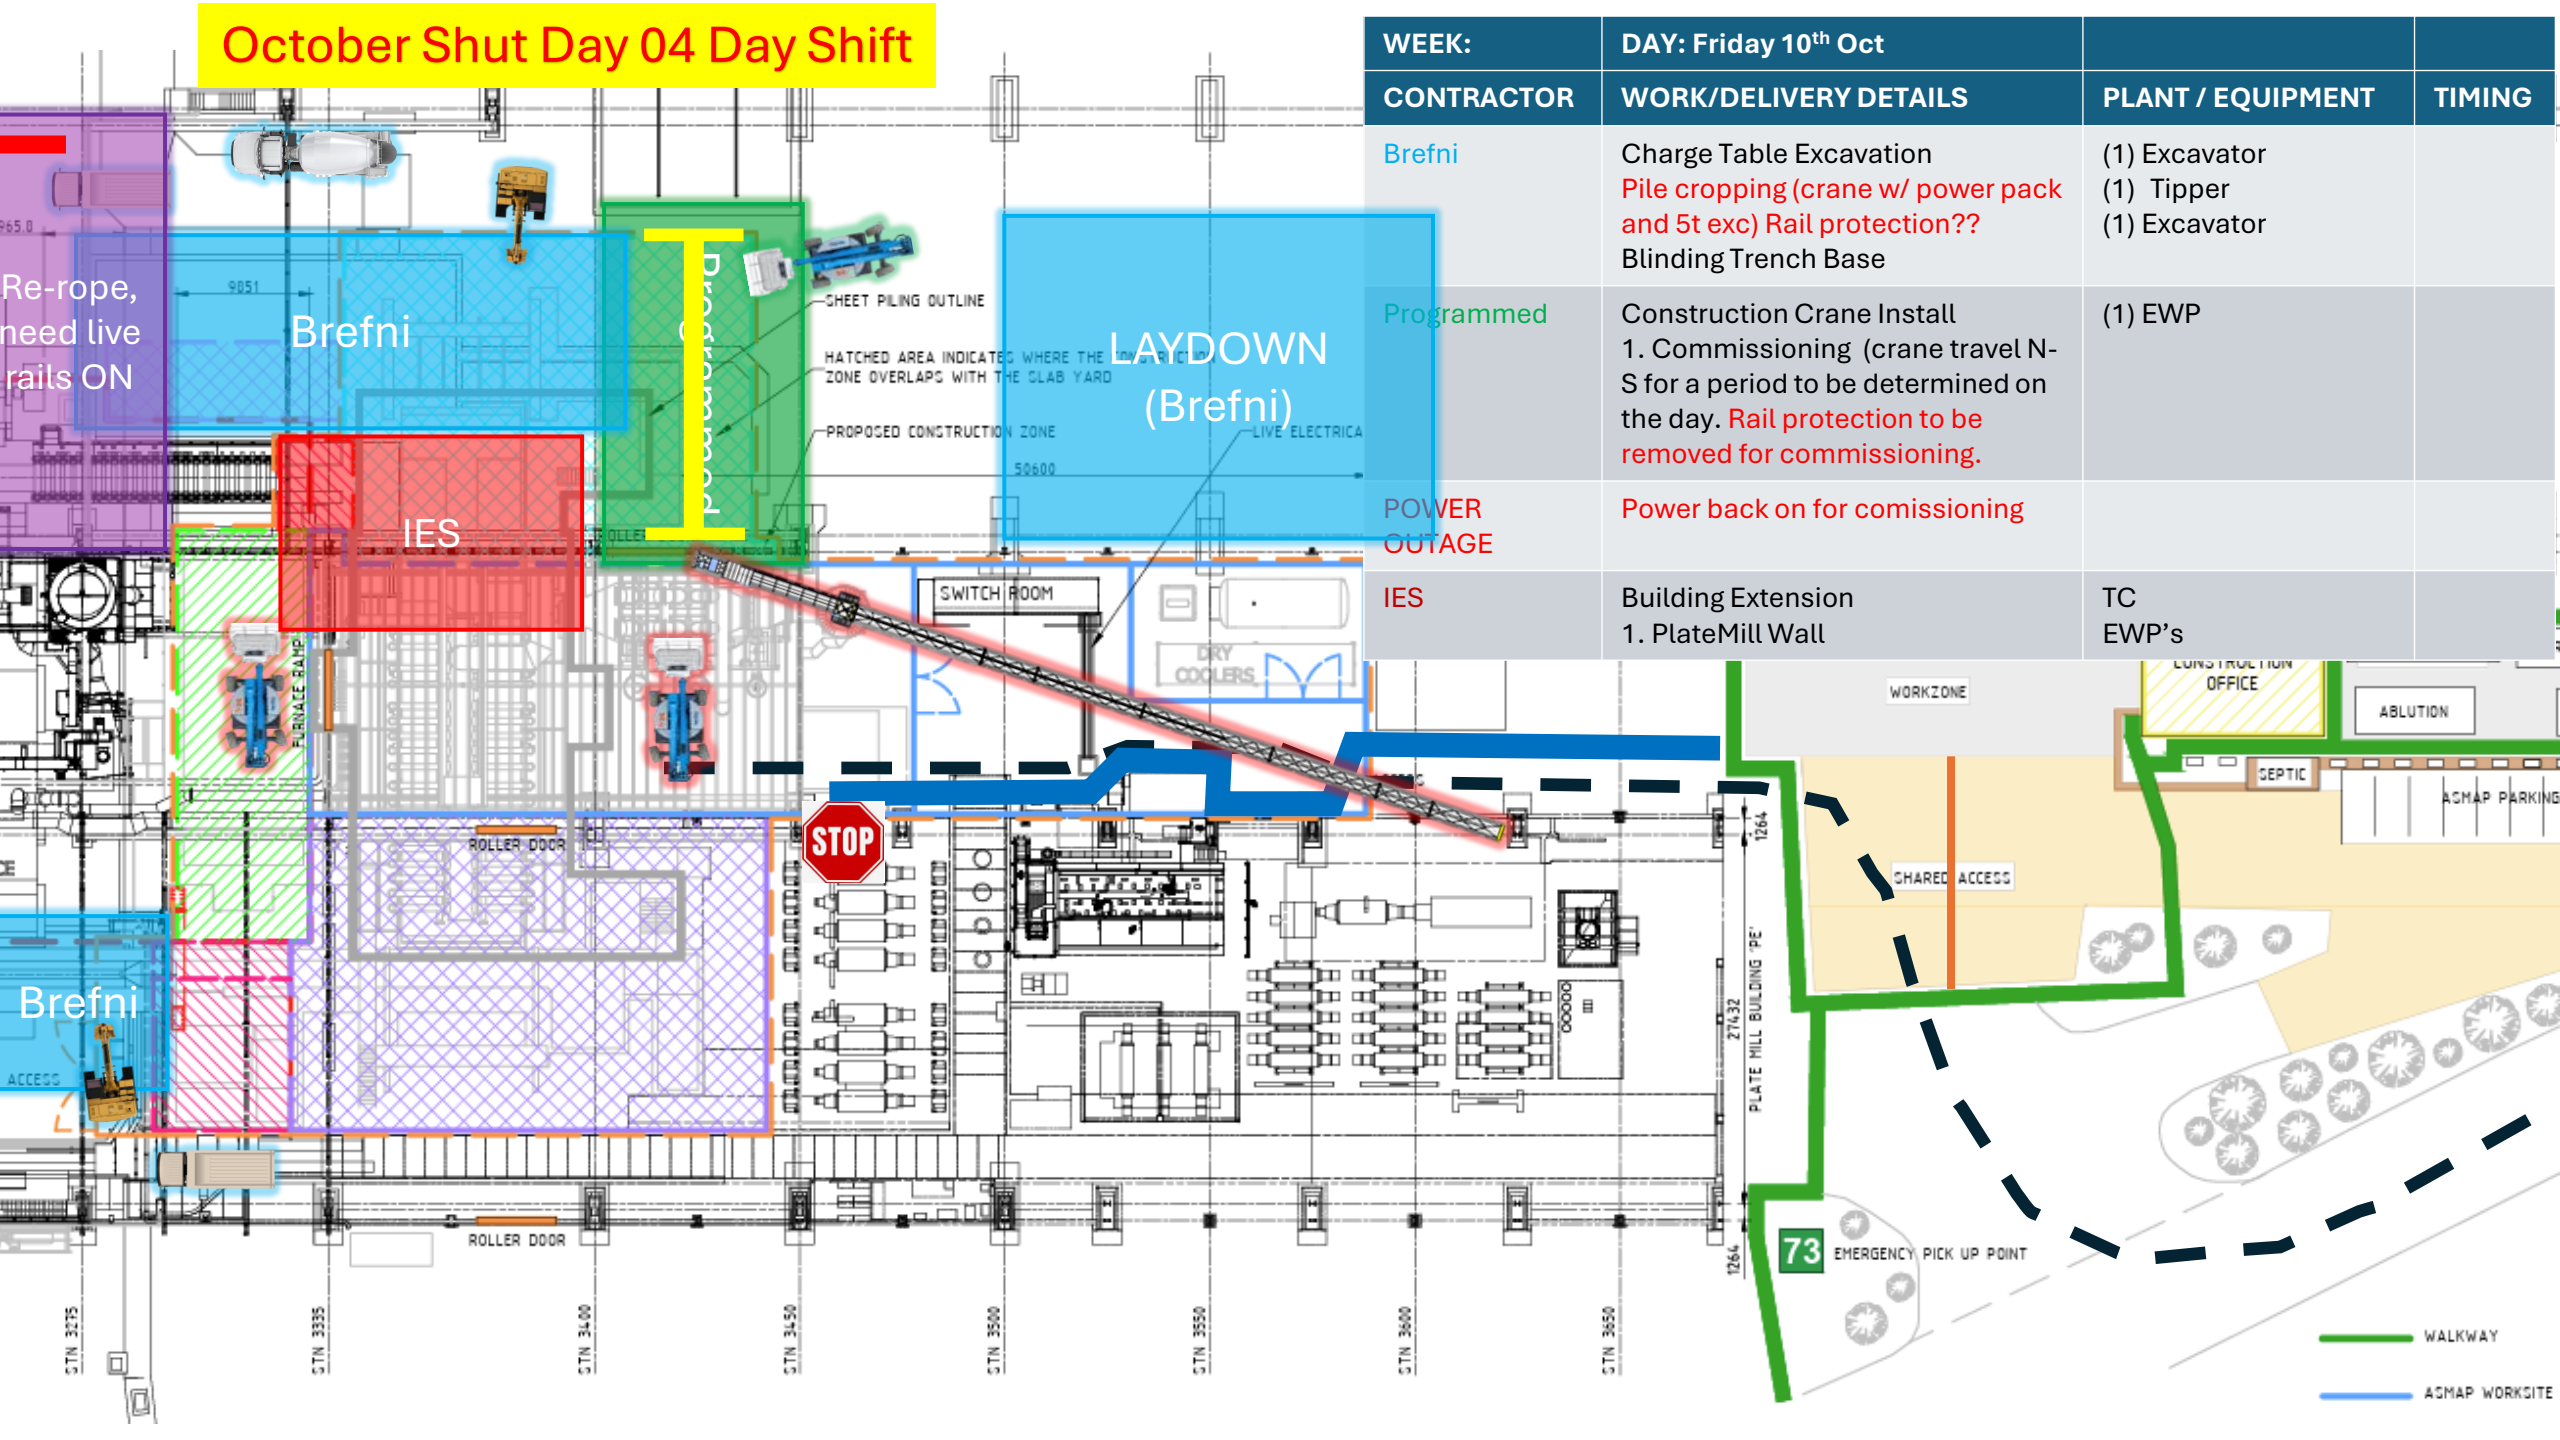


WEEK:	DAY: Friday 10 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation Pile cropping (crane w/ power pack and 5t exc) Rail protection?? Blinding Trench Base	(1) Excavator (1) Tipper (1) Excavator	
Programmed	Construction Crane Install 1. Commissioning (crane travel N-S for a period to be determined on the day. Rail protection to be removed for commissioning.	(1) EWP	
POWER OUTAGE	Power back on for comissioning		
IES	Building Extension 1. PlateMill Wall	TC EWP's	

October Shut Day 04 Night Shift


WEEK:	DAY: Friday 10 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation Pile Cropping FRP Trench Base	(1) Excavator (1) Tipper (1) Excavator	

Re-rope,
need live
rails ON

Brefni

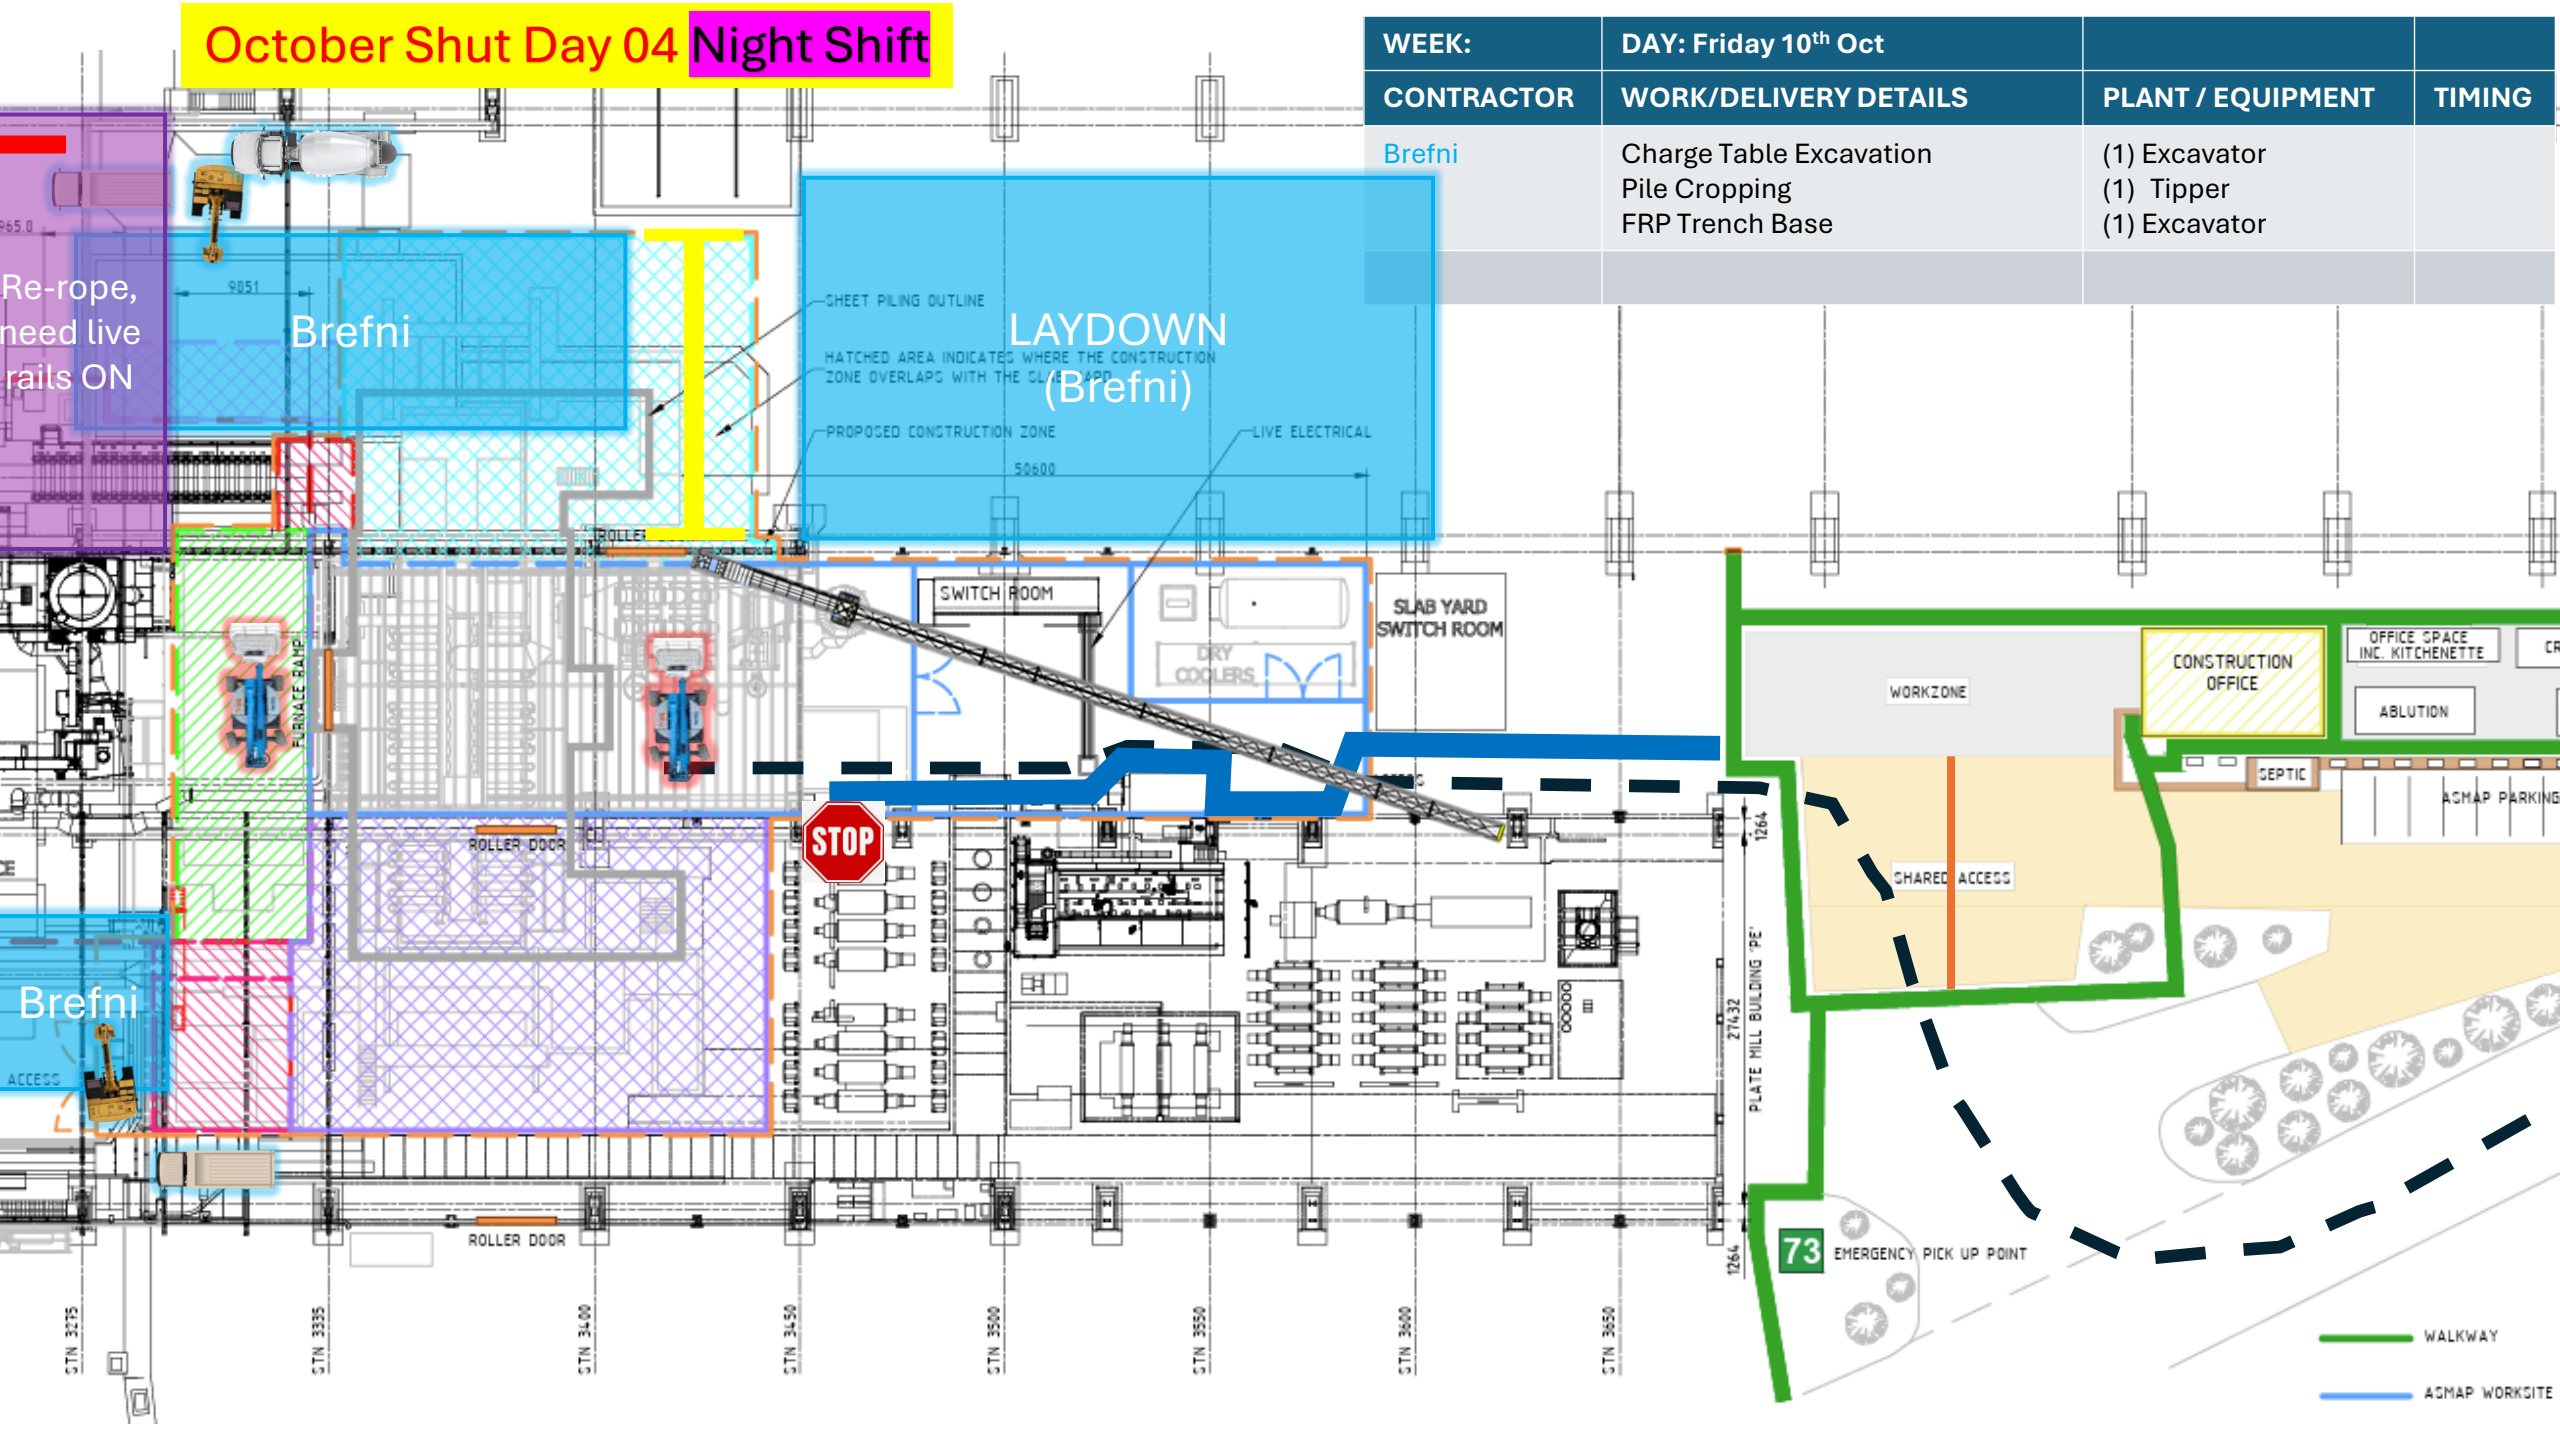


October Shut – Post Crane Install

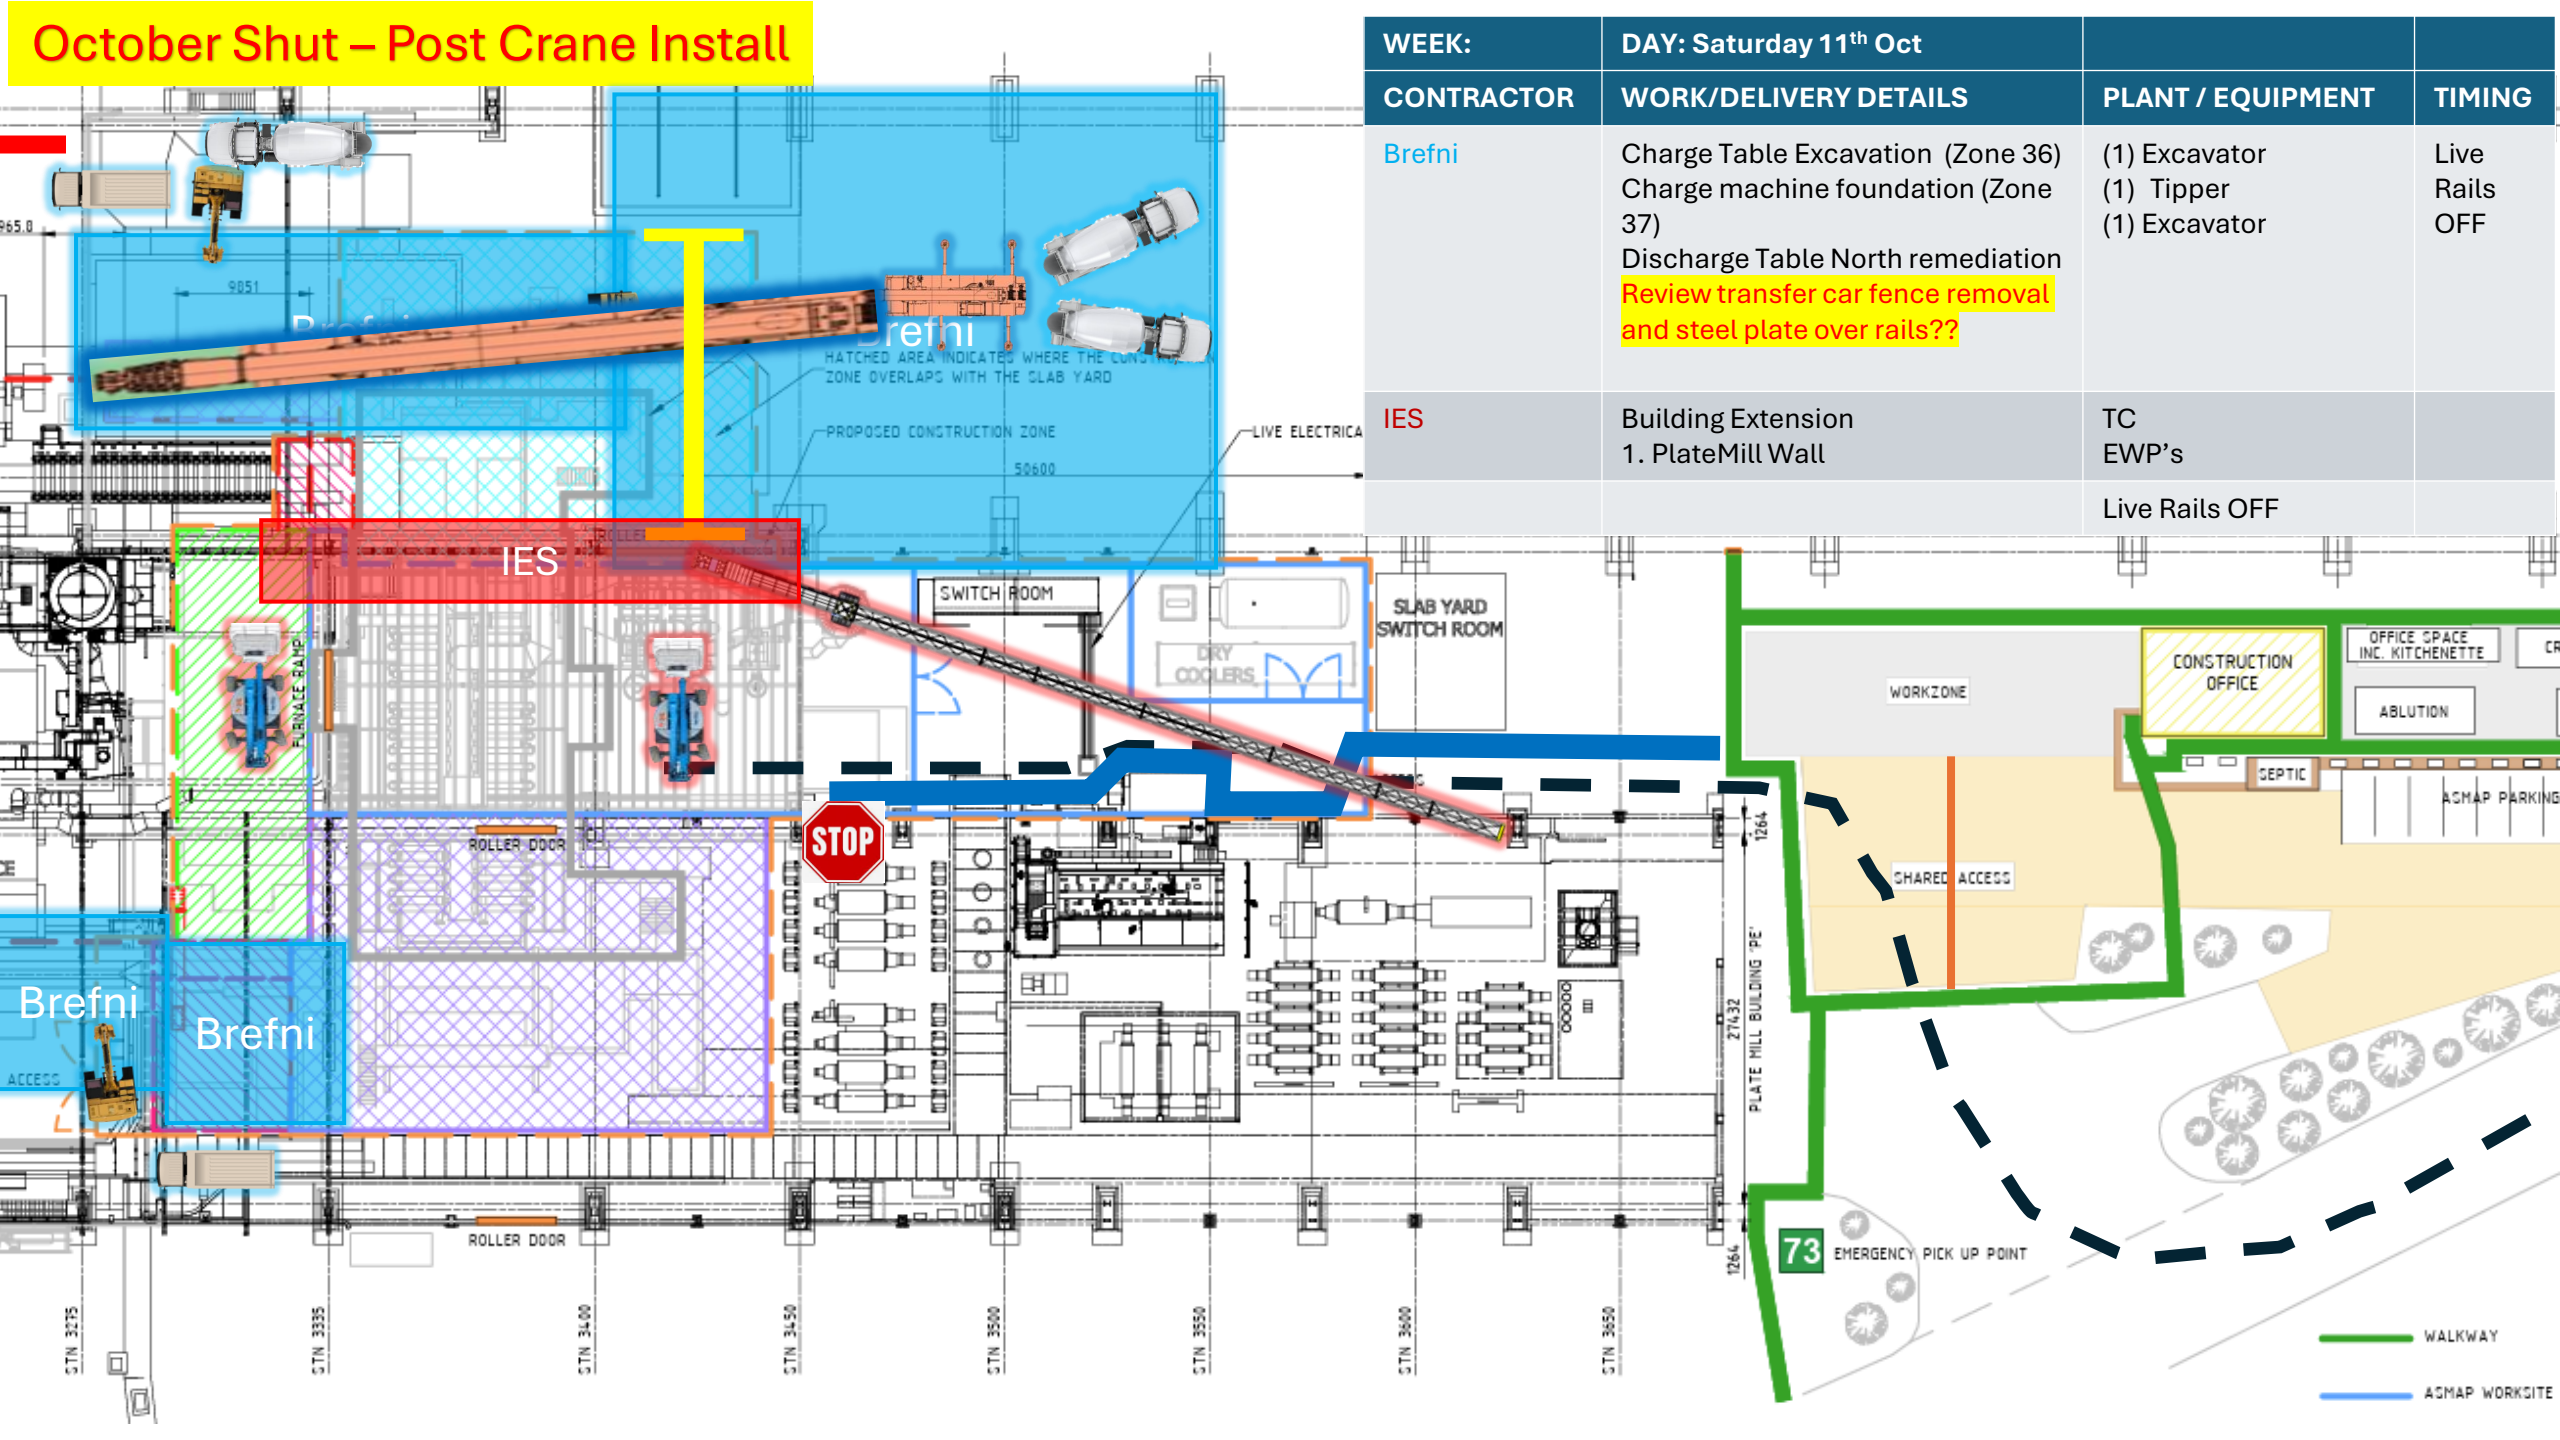


WEEK:	DAY: Saturday 11 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation Review transfer car fence removal and steel plate over rails??	(1) Excavator (1) Tipper (1) Excavator	Live Rails OFF
IES	Building Extension 1. PlateMill Wall	TC EWP's	
		Live Rails OFF	

October Shut – Post Crane Install

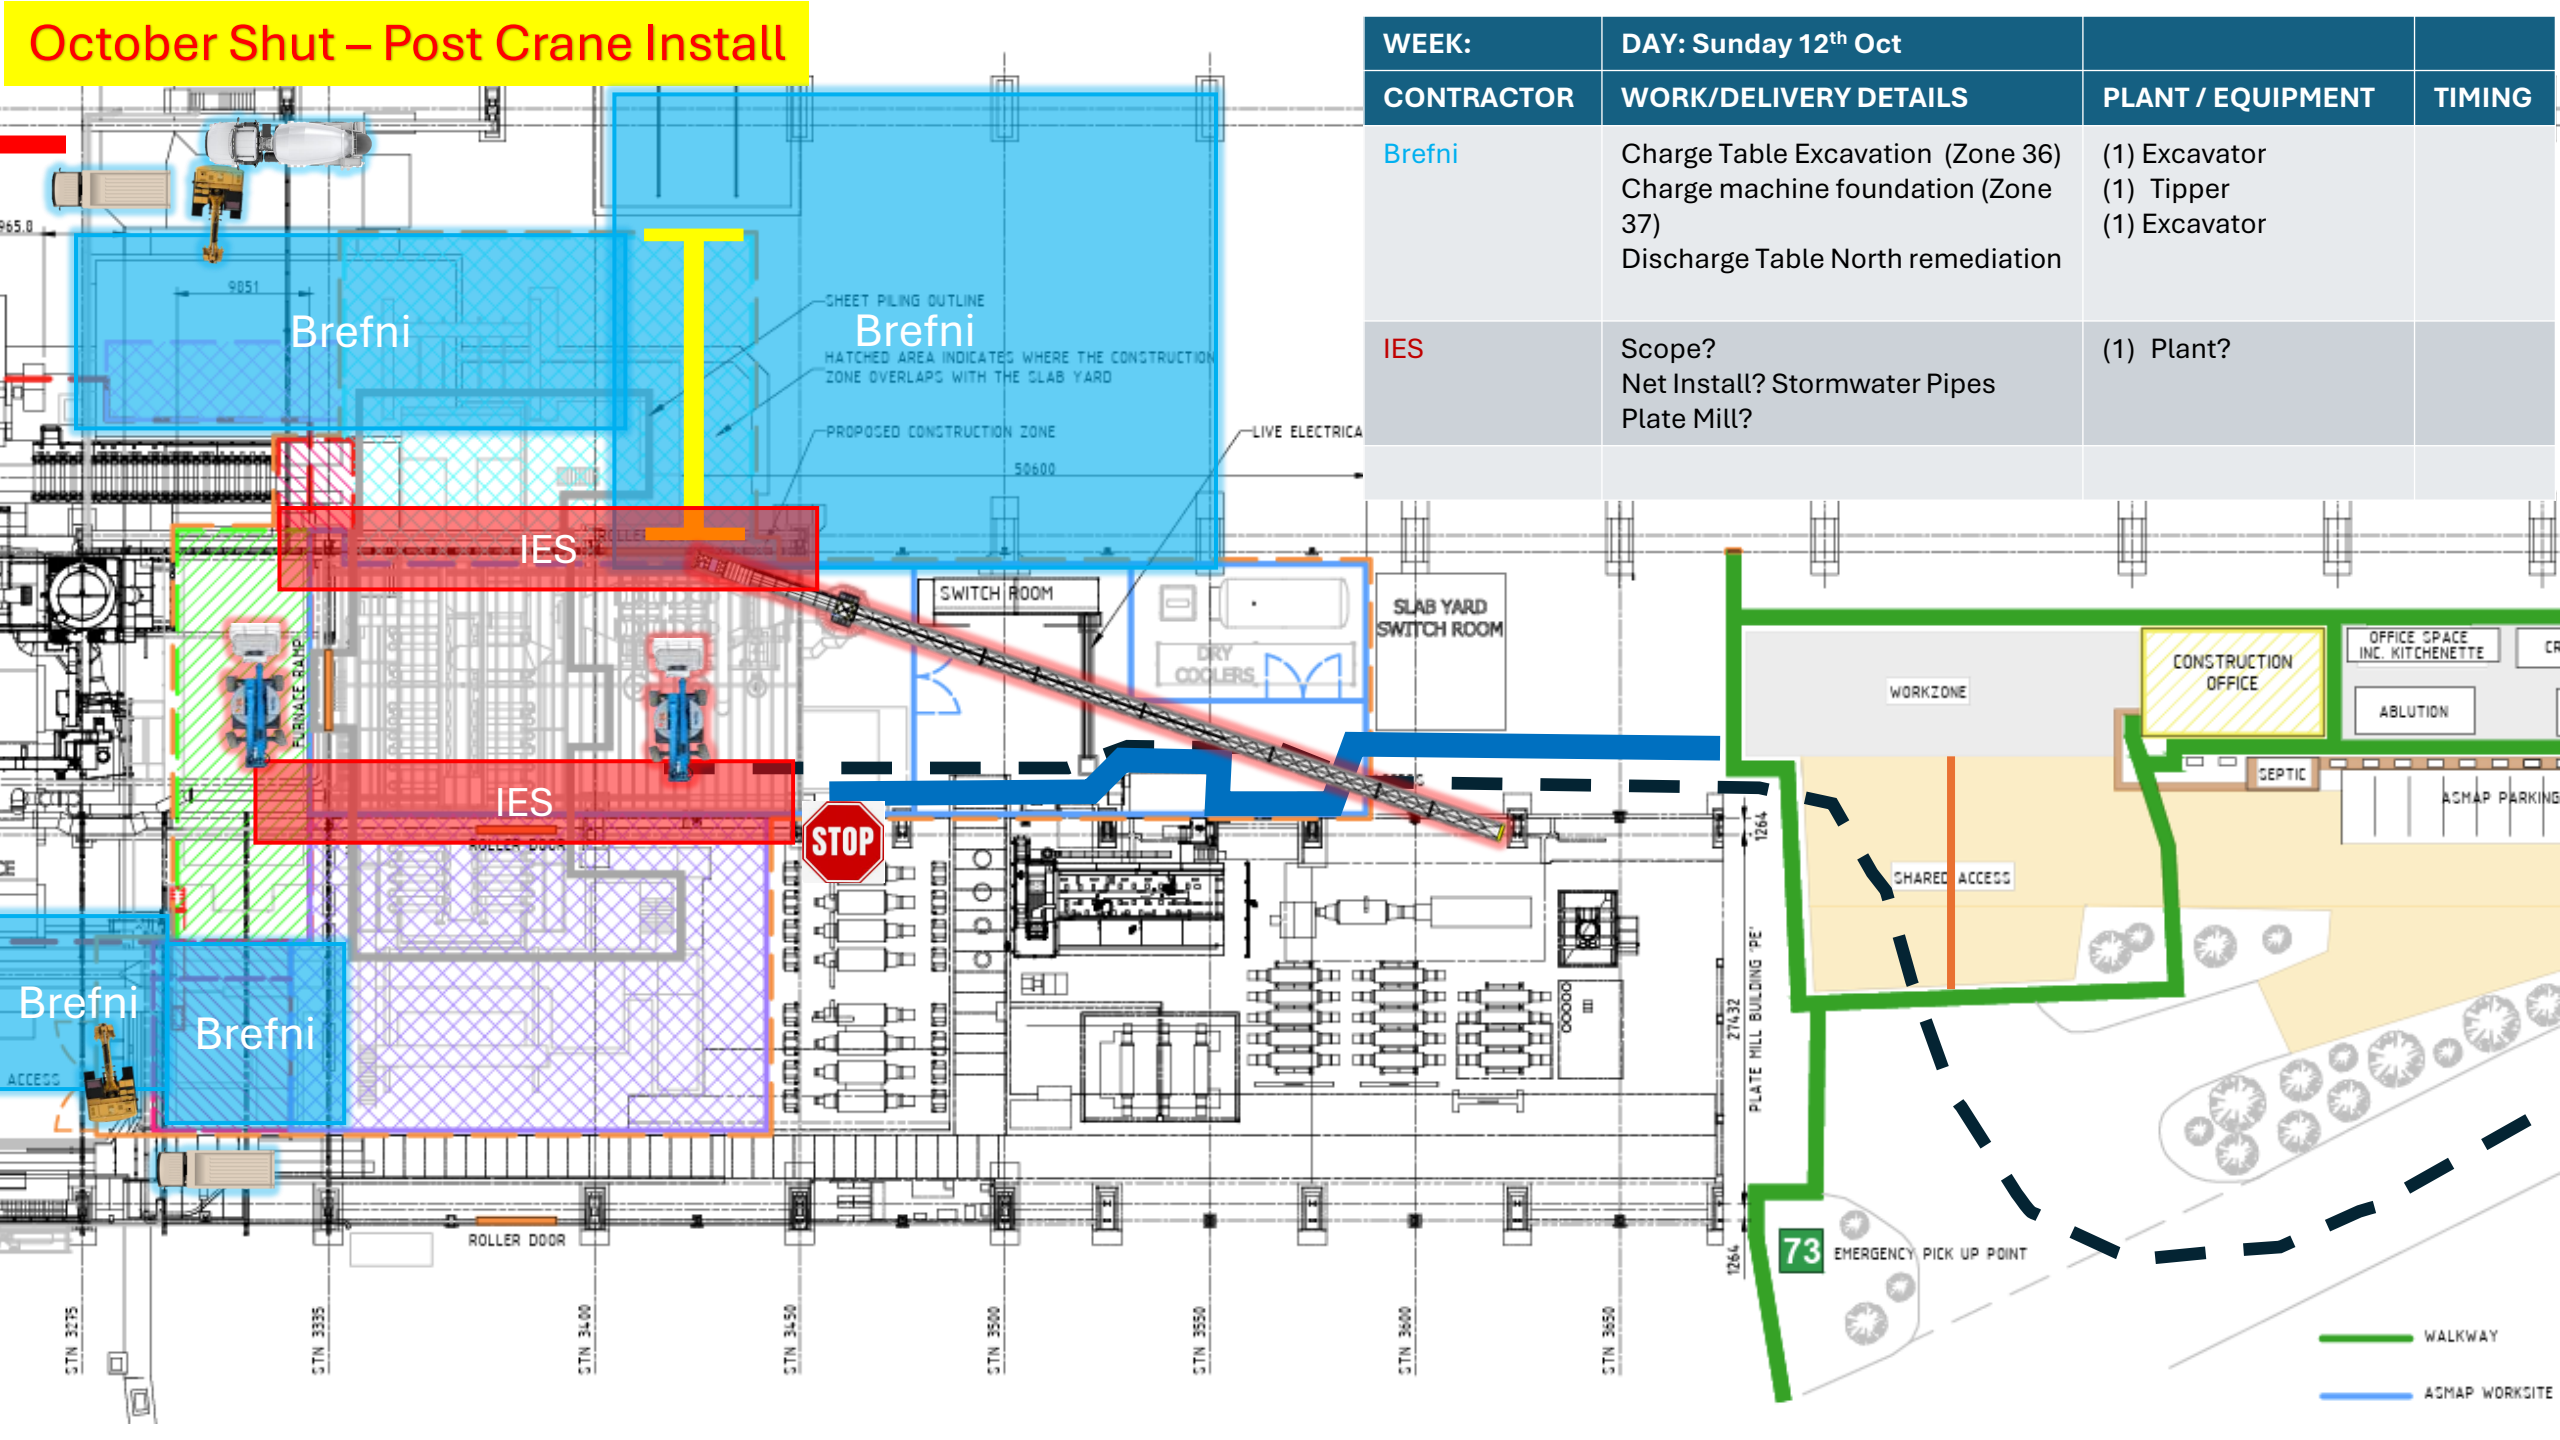


WEEK:	DAY: Sunday 12 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Scope? Net Install? Stormwater Pipes Plate Mill?	(1) Plant?	

October Shut – Post Crane Install

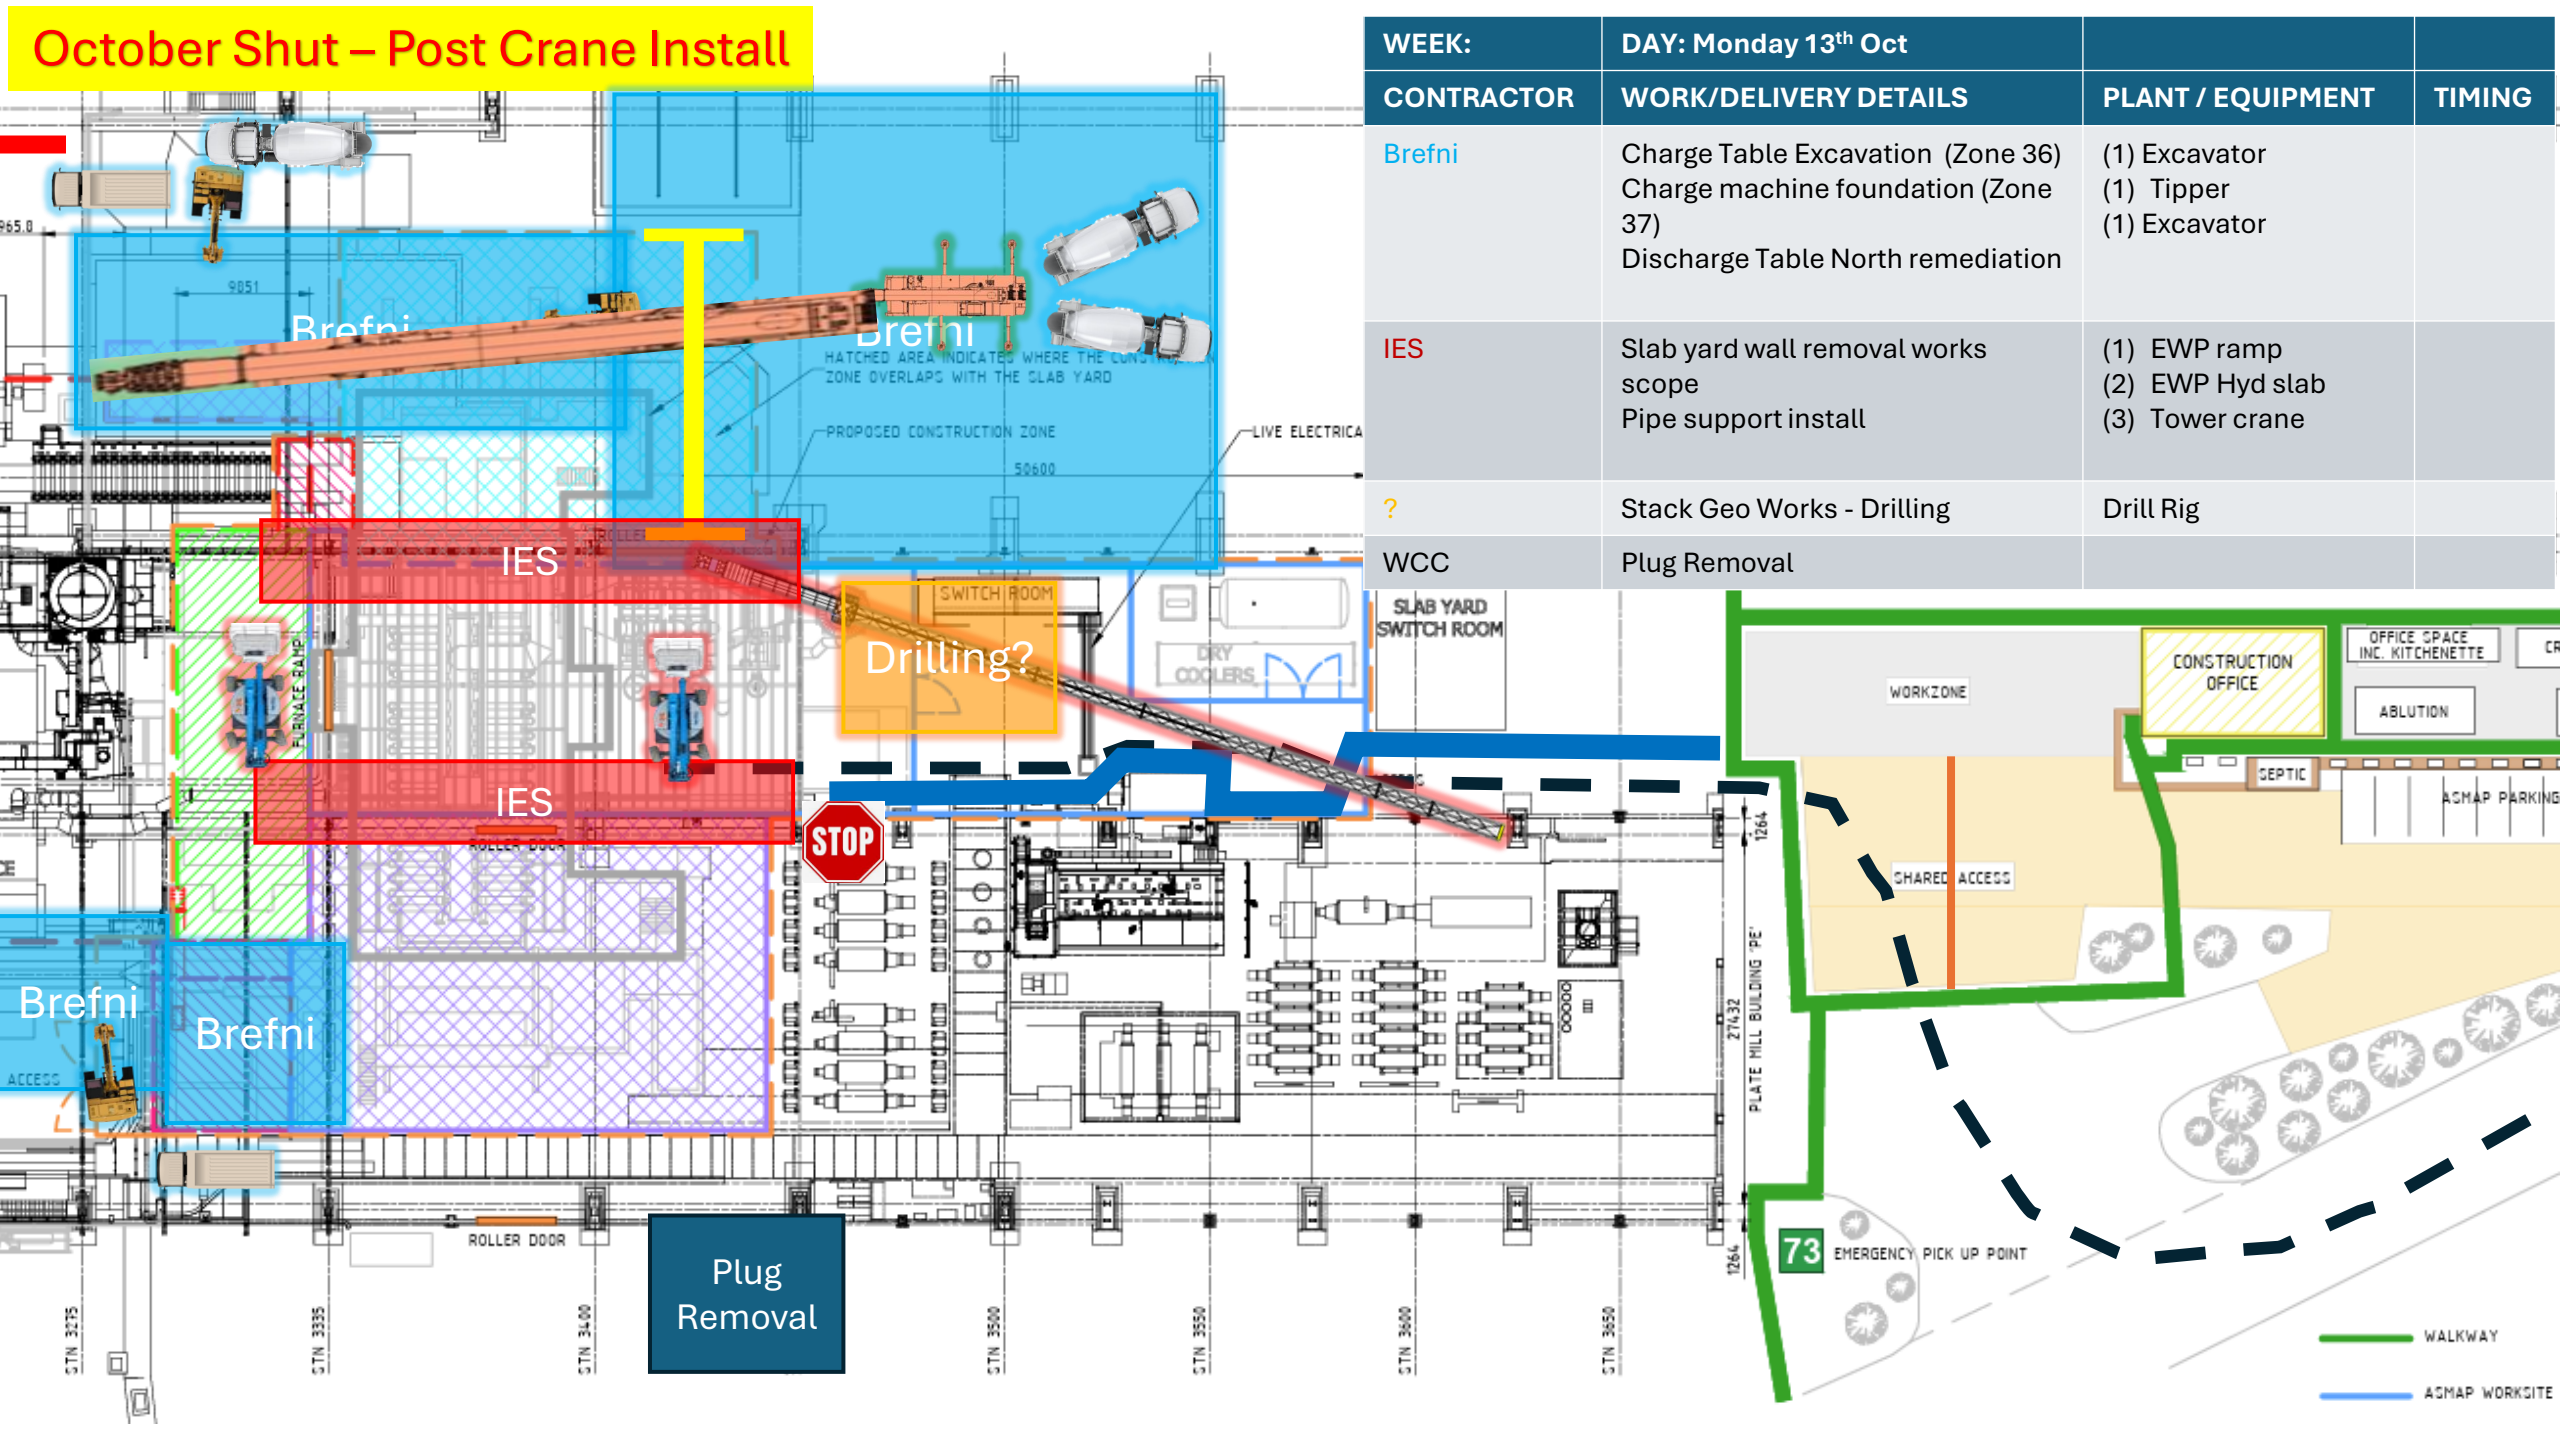


WEEK:	DAY: Monday 13 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Slab yard wall removal works scope Pipe support install	(1) EWP ramp (2) EWP Hyd slab (3) Tower crane	
?	Stack Geo Works - Drilling	Drill Rig	
WCC	Plug Removal		

October Shut – Post Crane Install

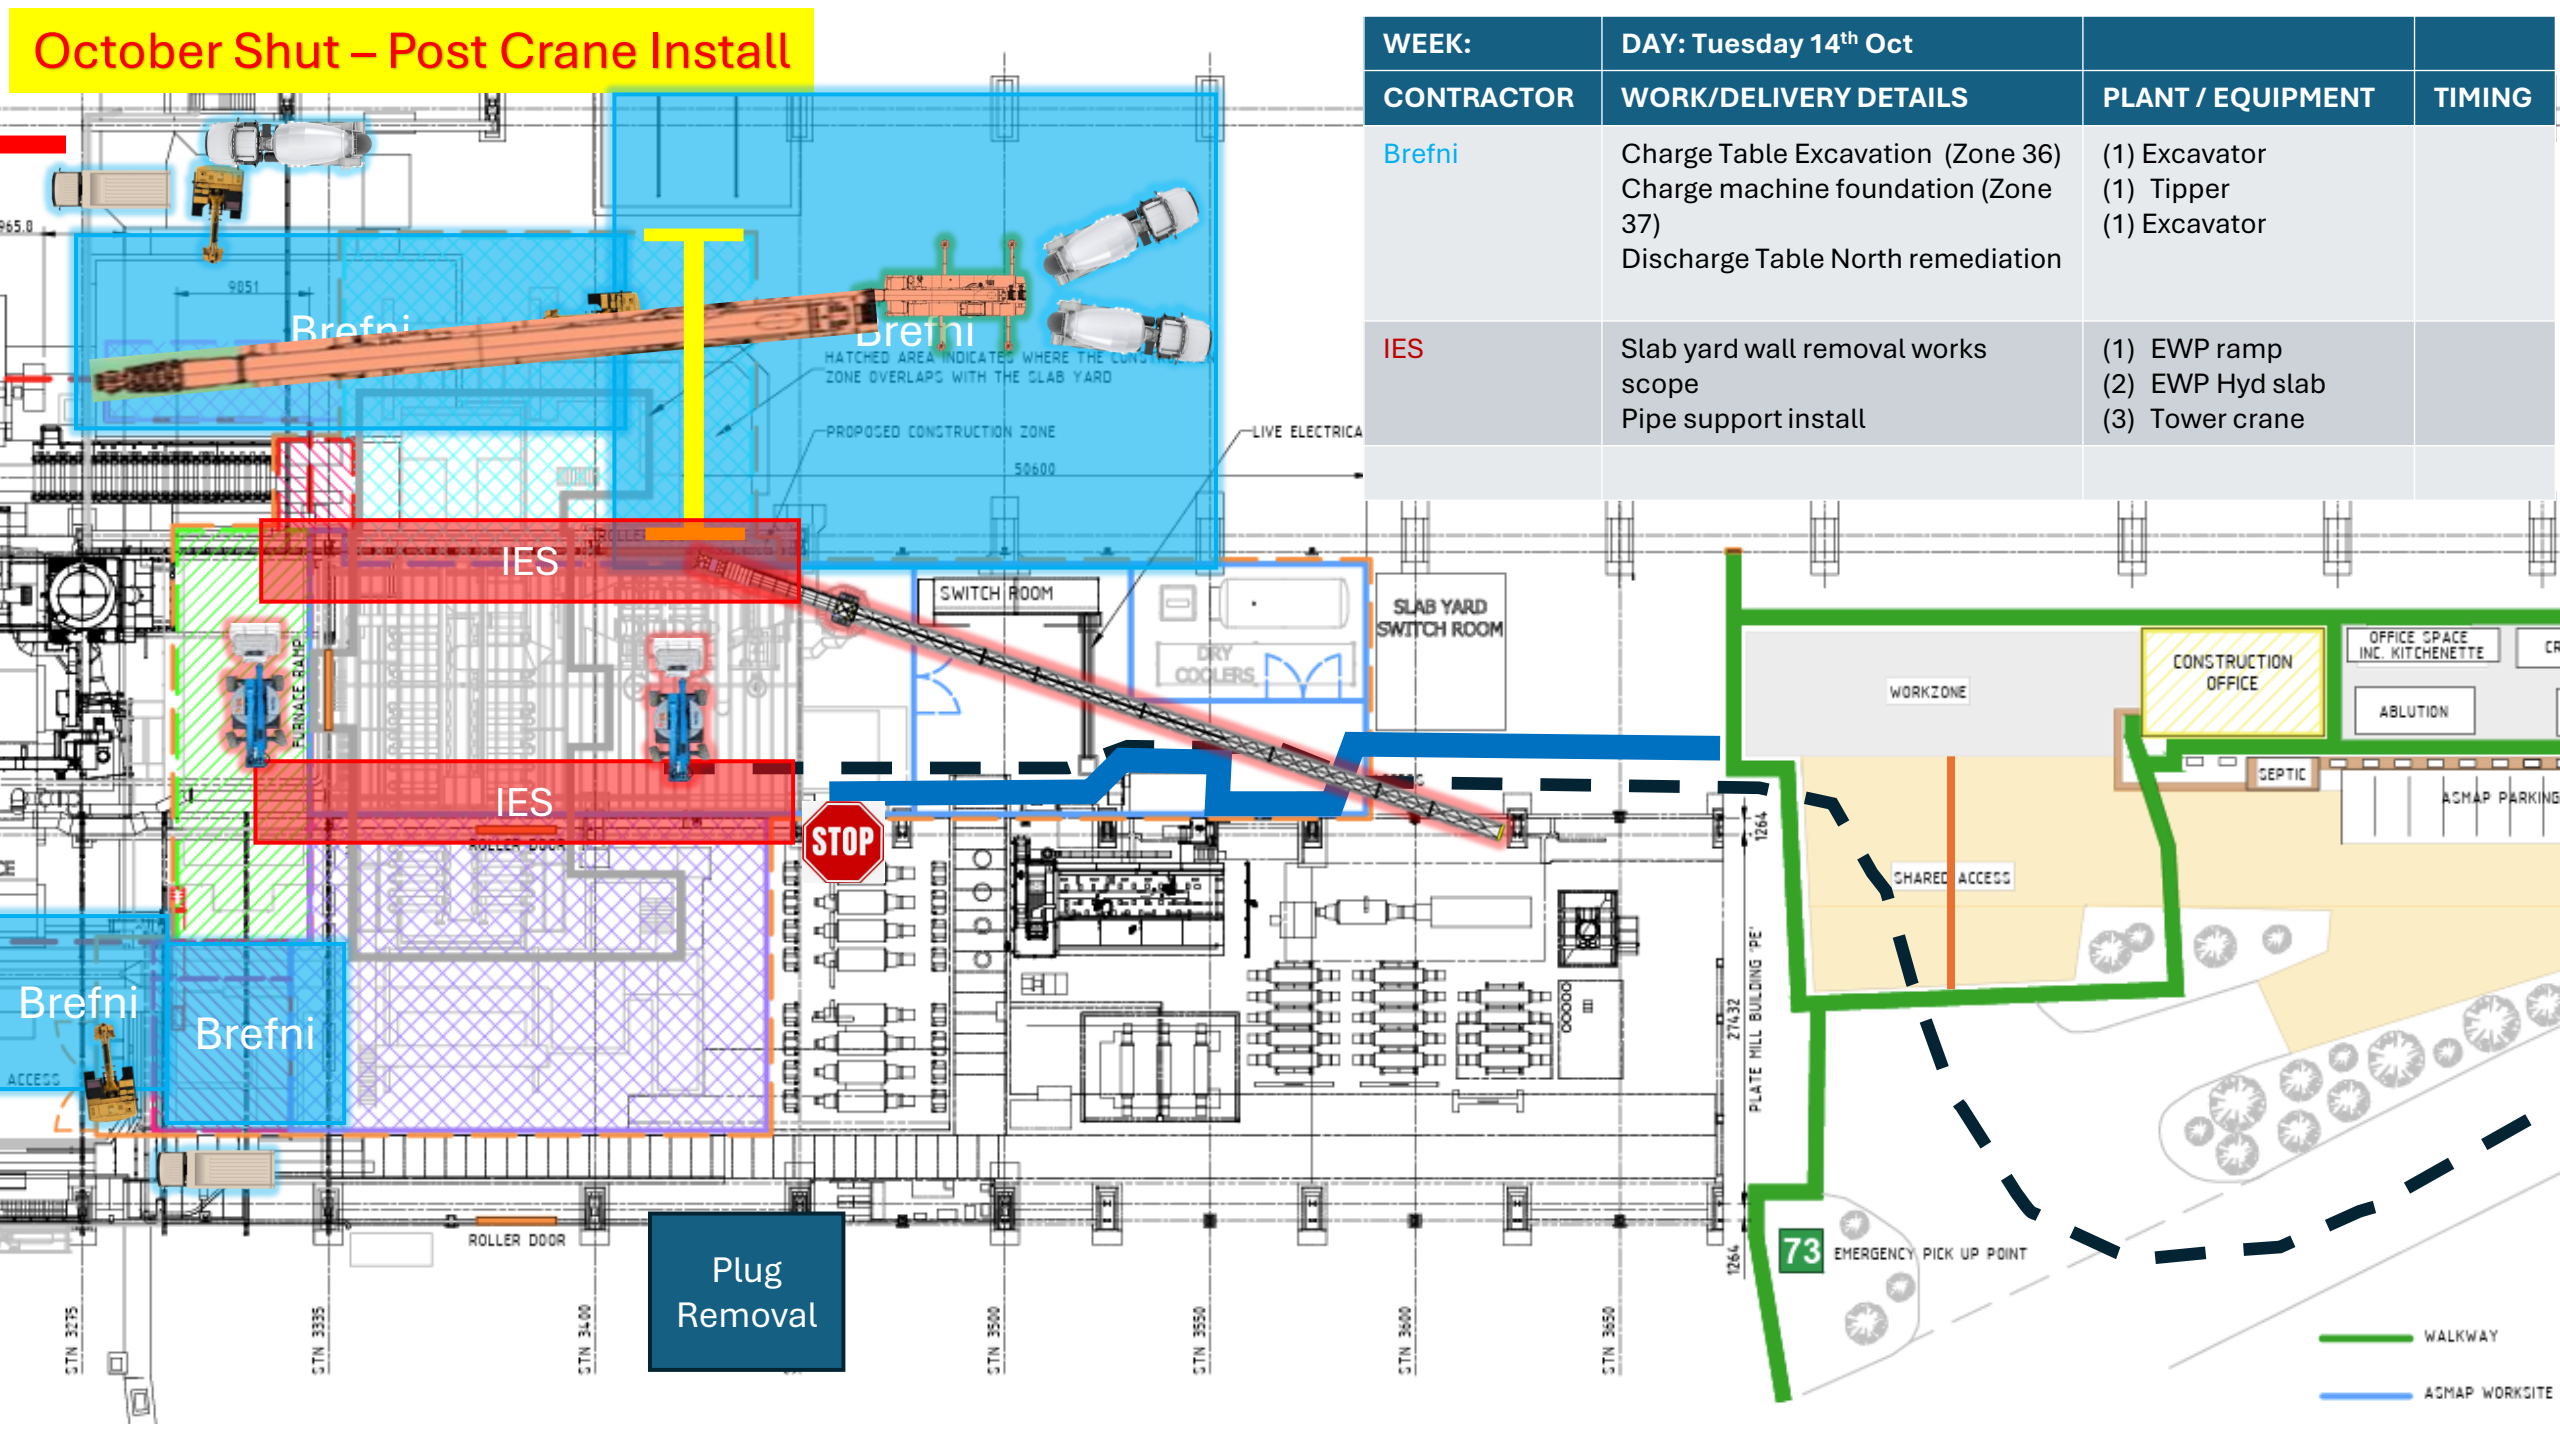


WEEK:	DAY: Tuesday 14 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Slab yard wall removal works scope Pipe support install	(1) EWP ramp (2) EWP Hyd slab (3) Tower crane	

October Shut – Post Crane Install

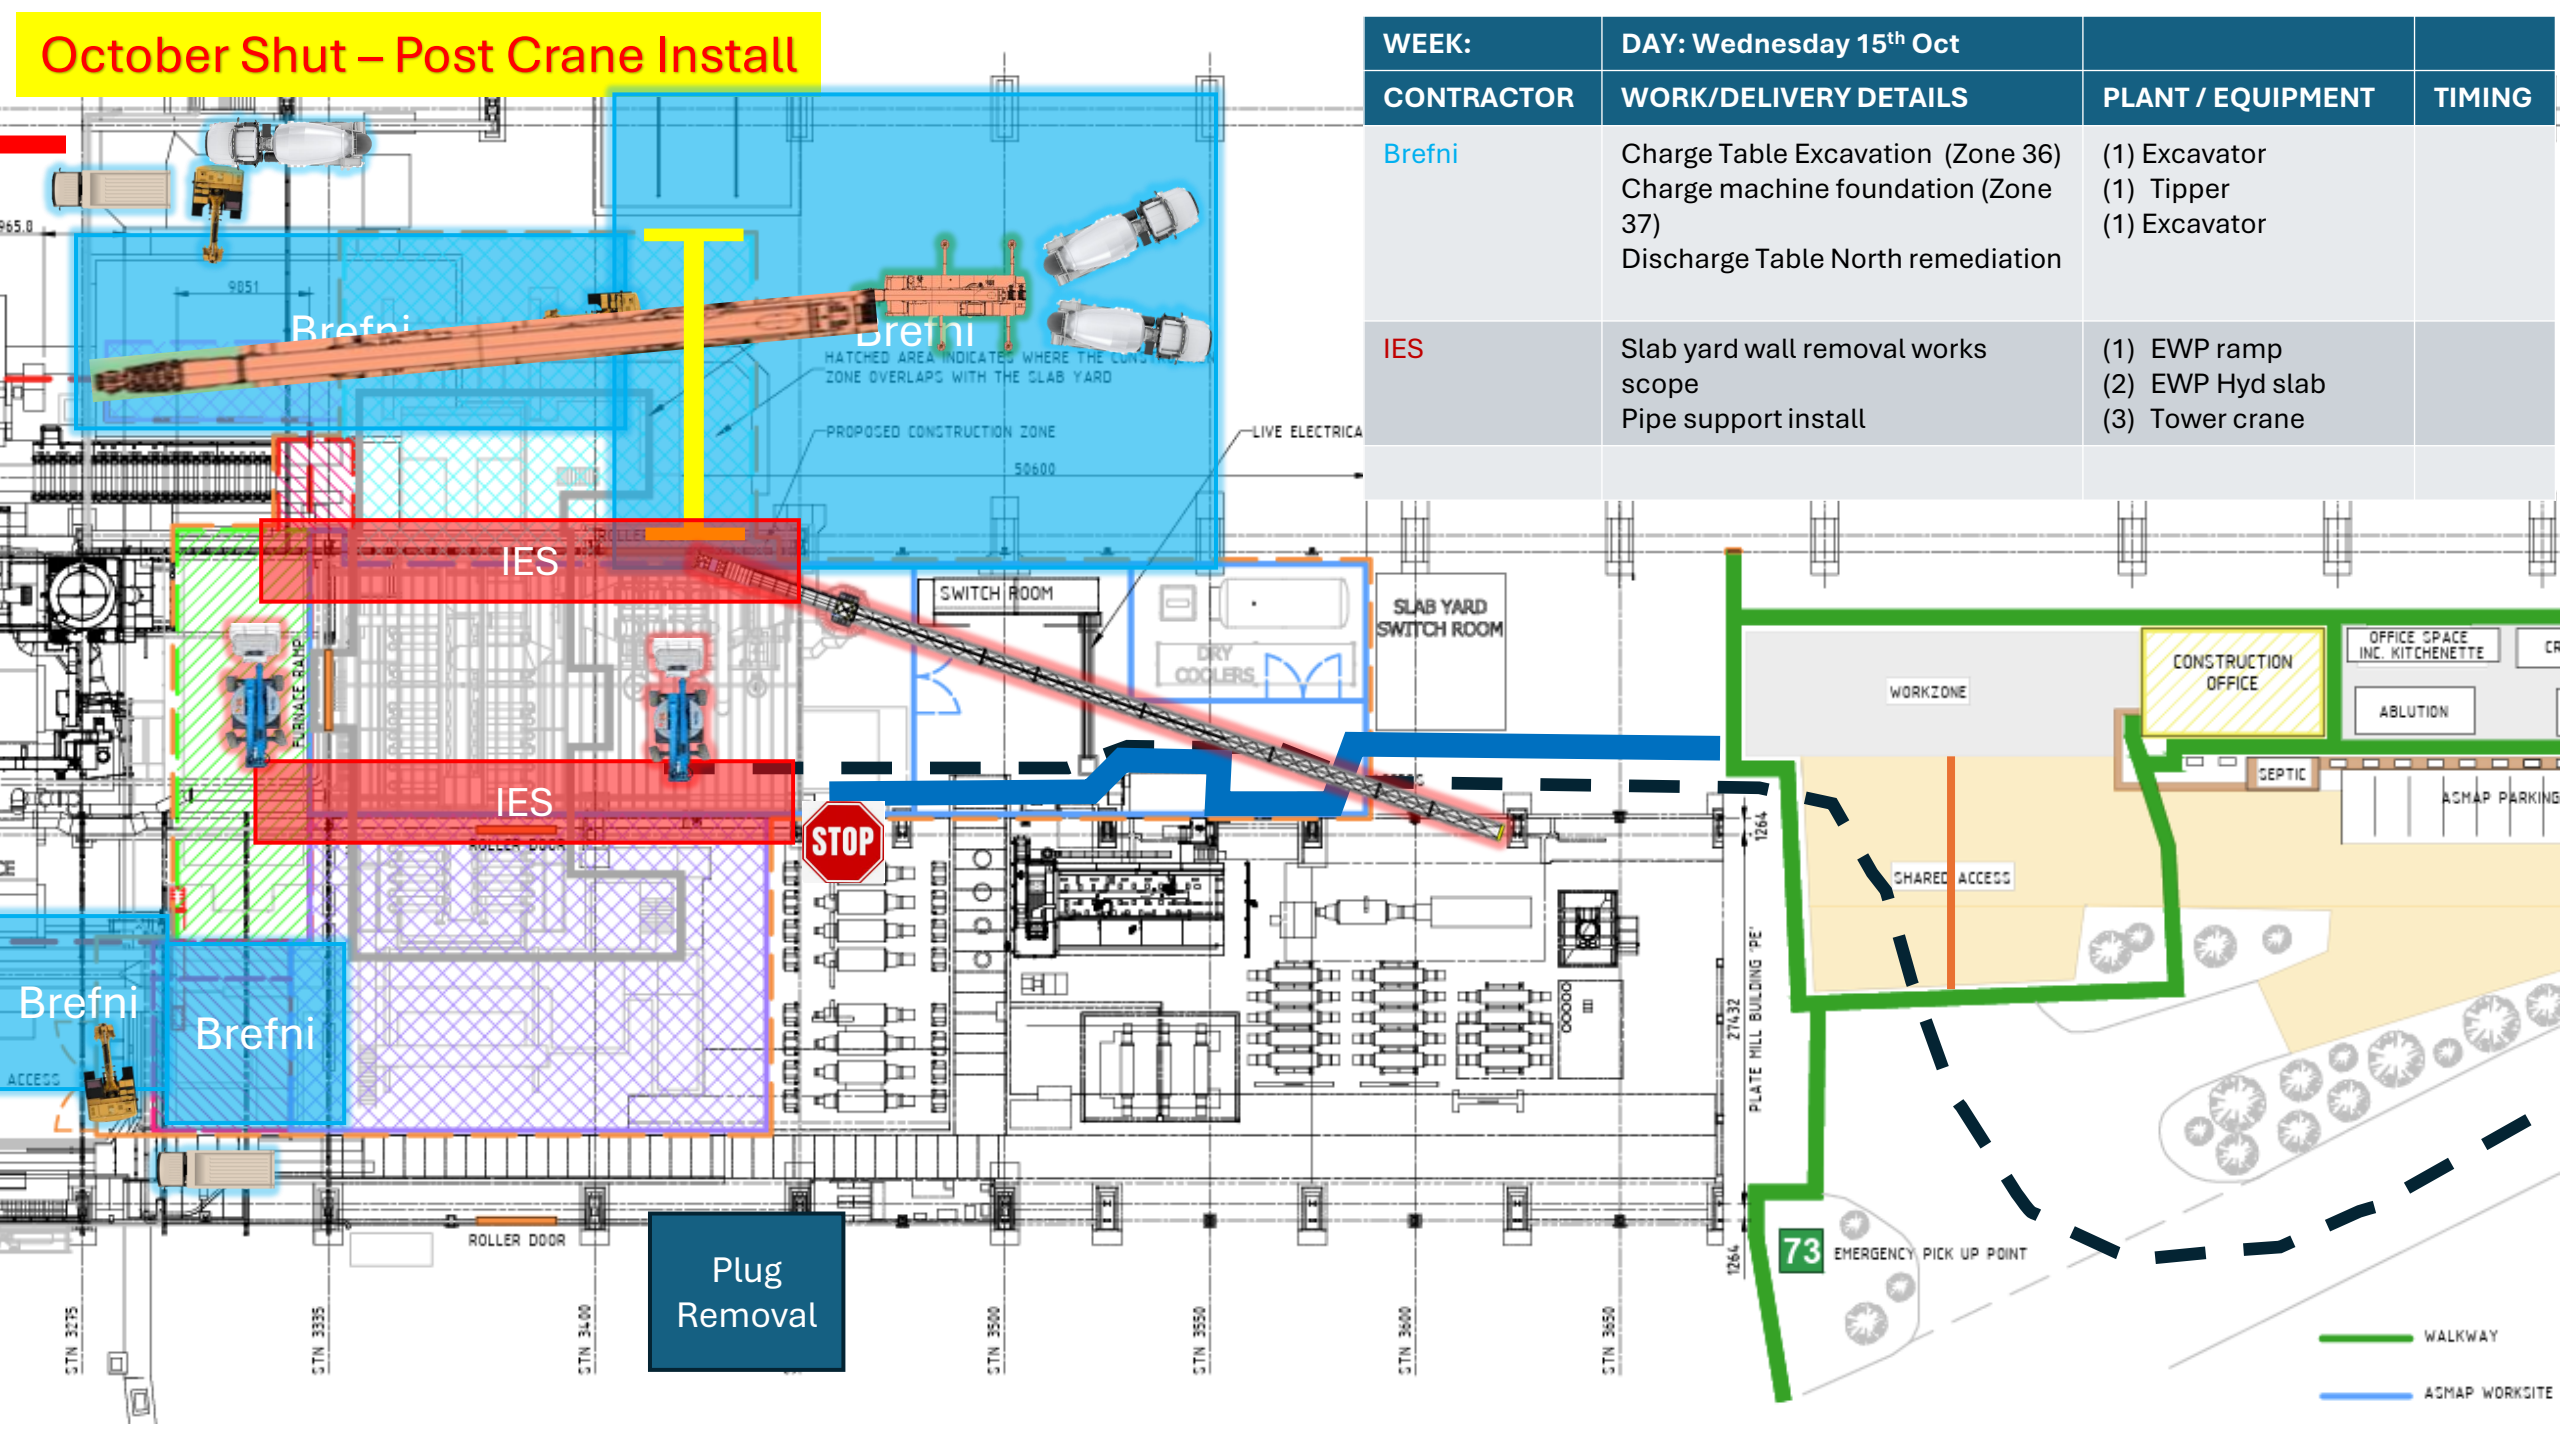


WEEK:	DAY: Wednesday 15 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Slab yard wall removal works scope Pipe support install	(1) EWP ramp (2) EWP Hyd slab (3) Tower crane	

October Shut – Post Crane Install

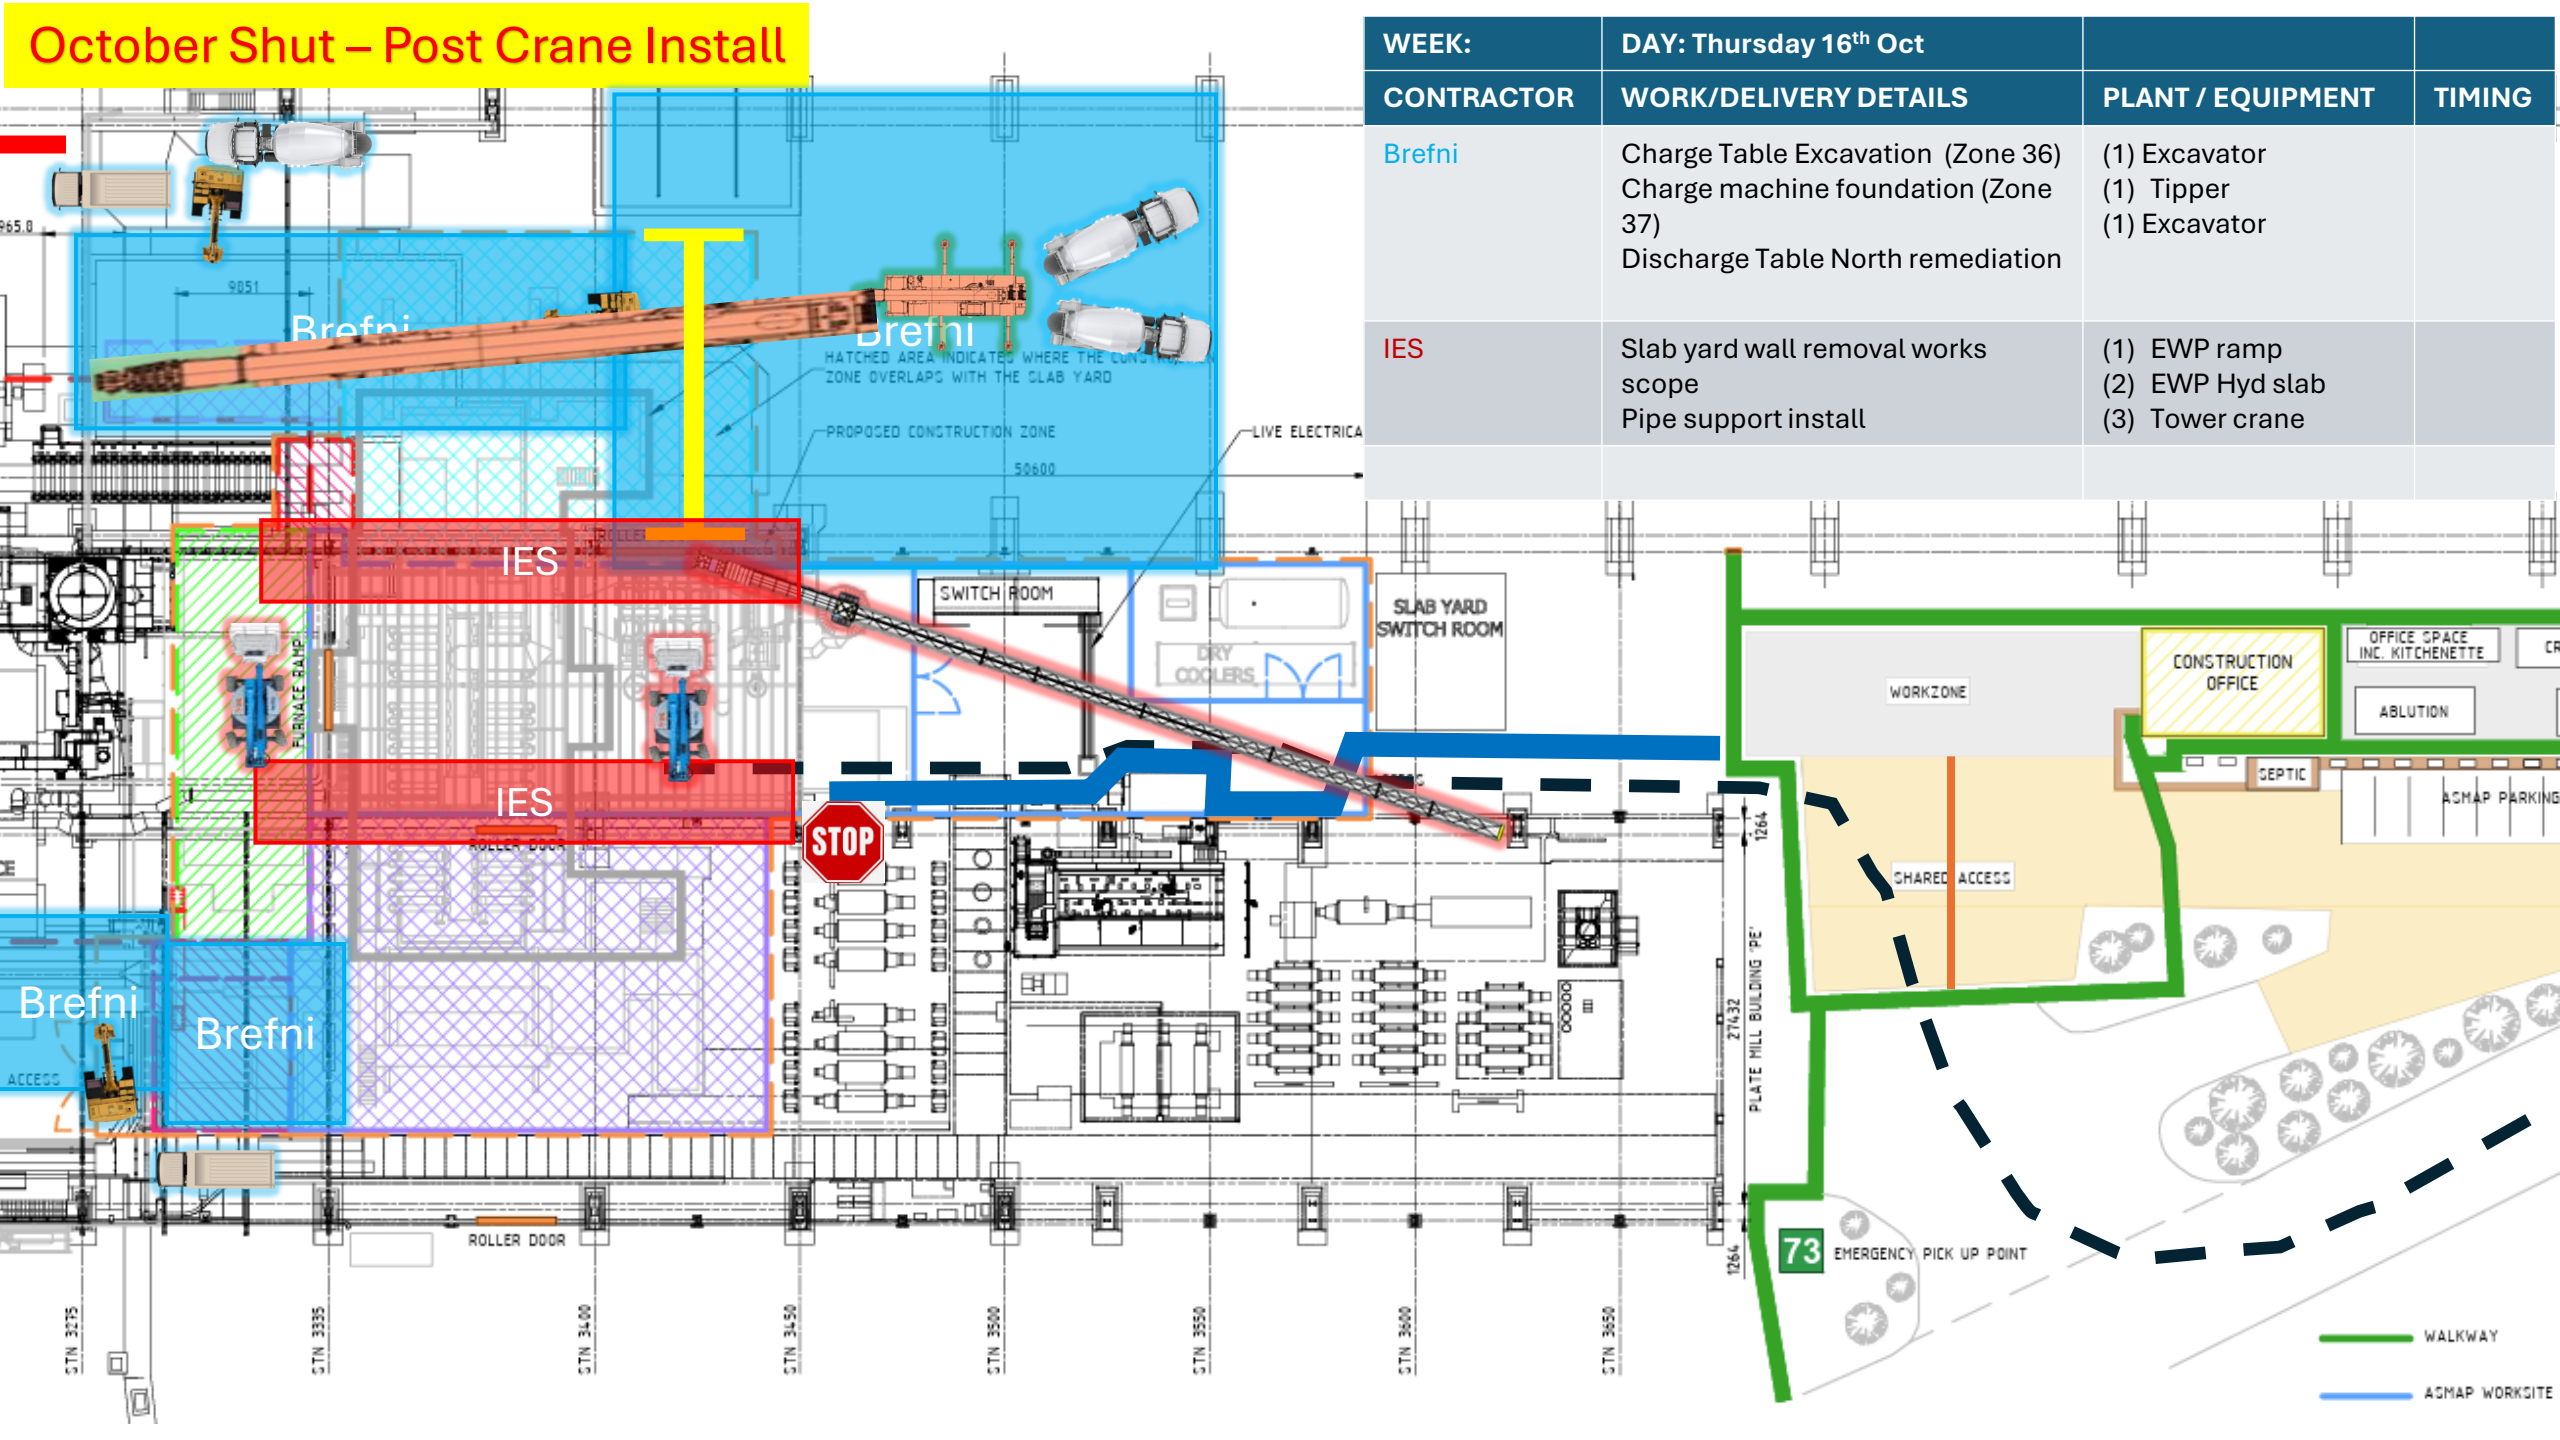


WEEK:	DAY: Thursday 16 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Slab yard wall removal works scope Pipe support install	(1) EWP ramp (2) EWP Hyd slab (3) Tower crane	

October Shut – Post Crane Install

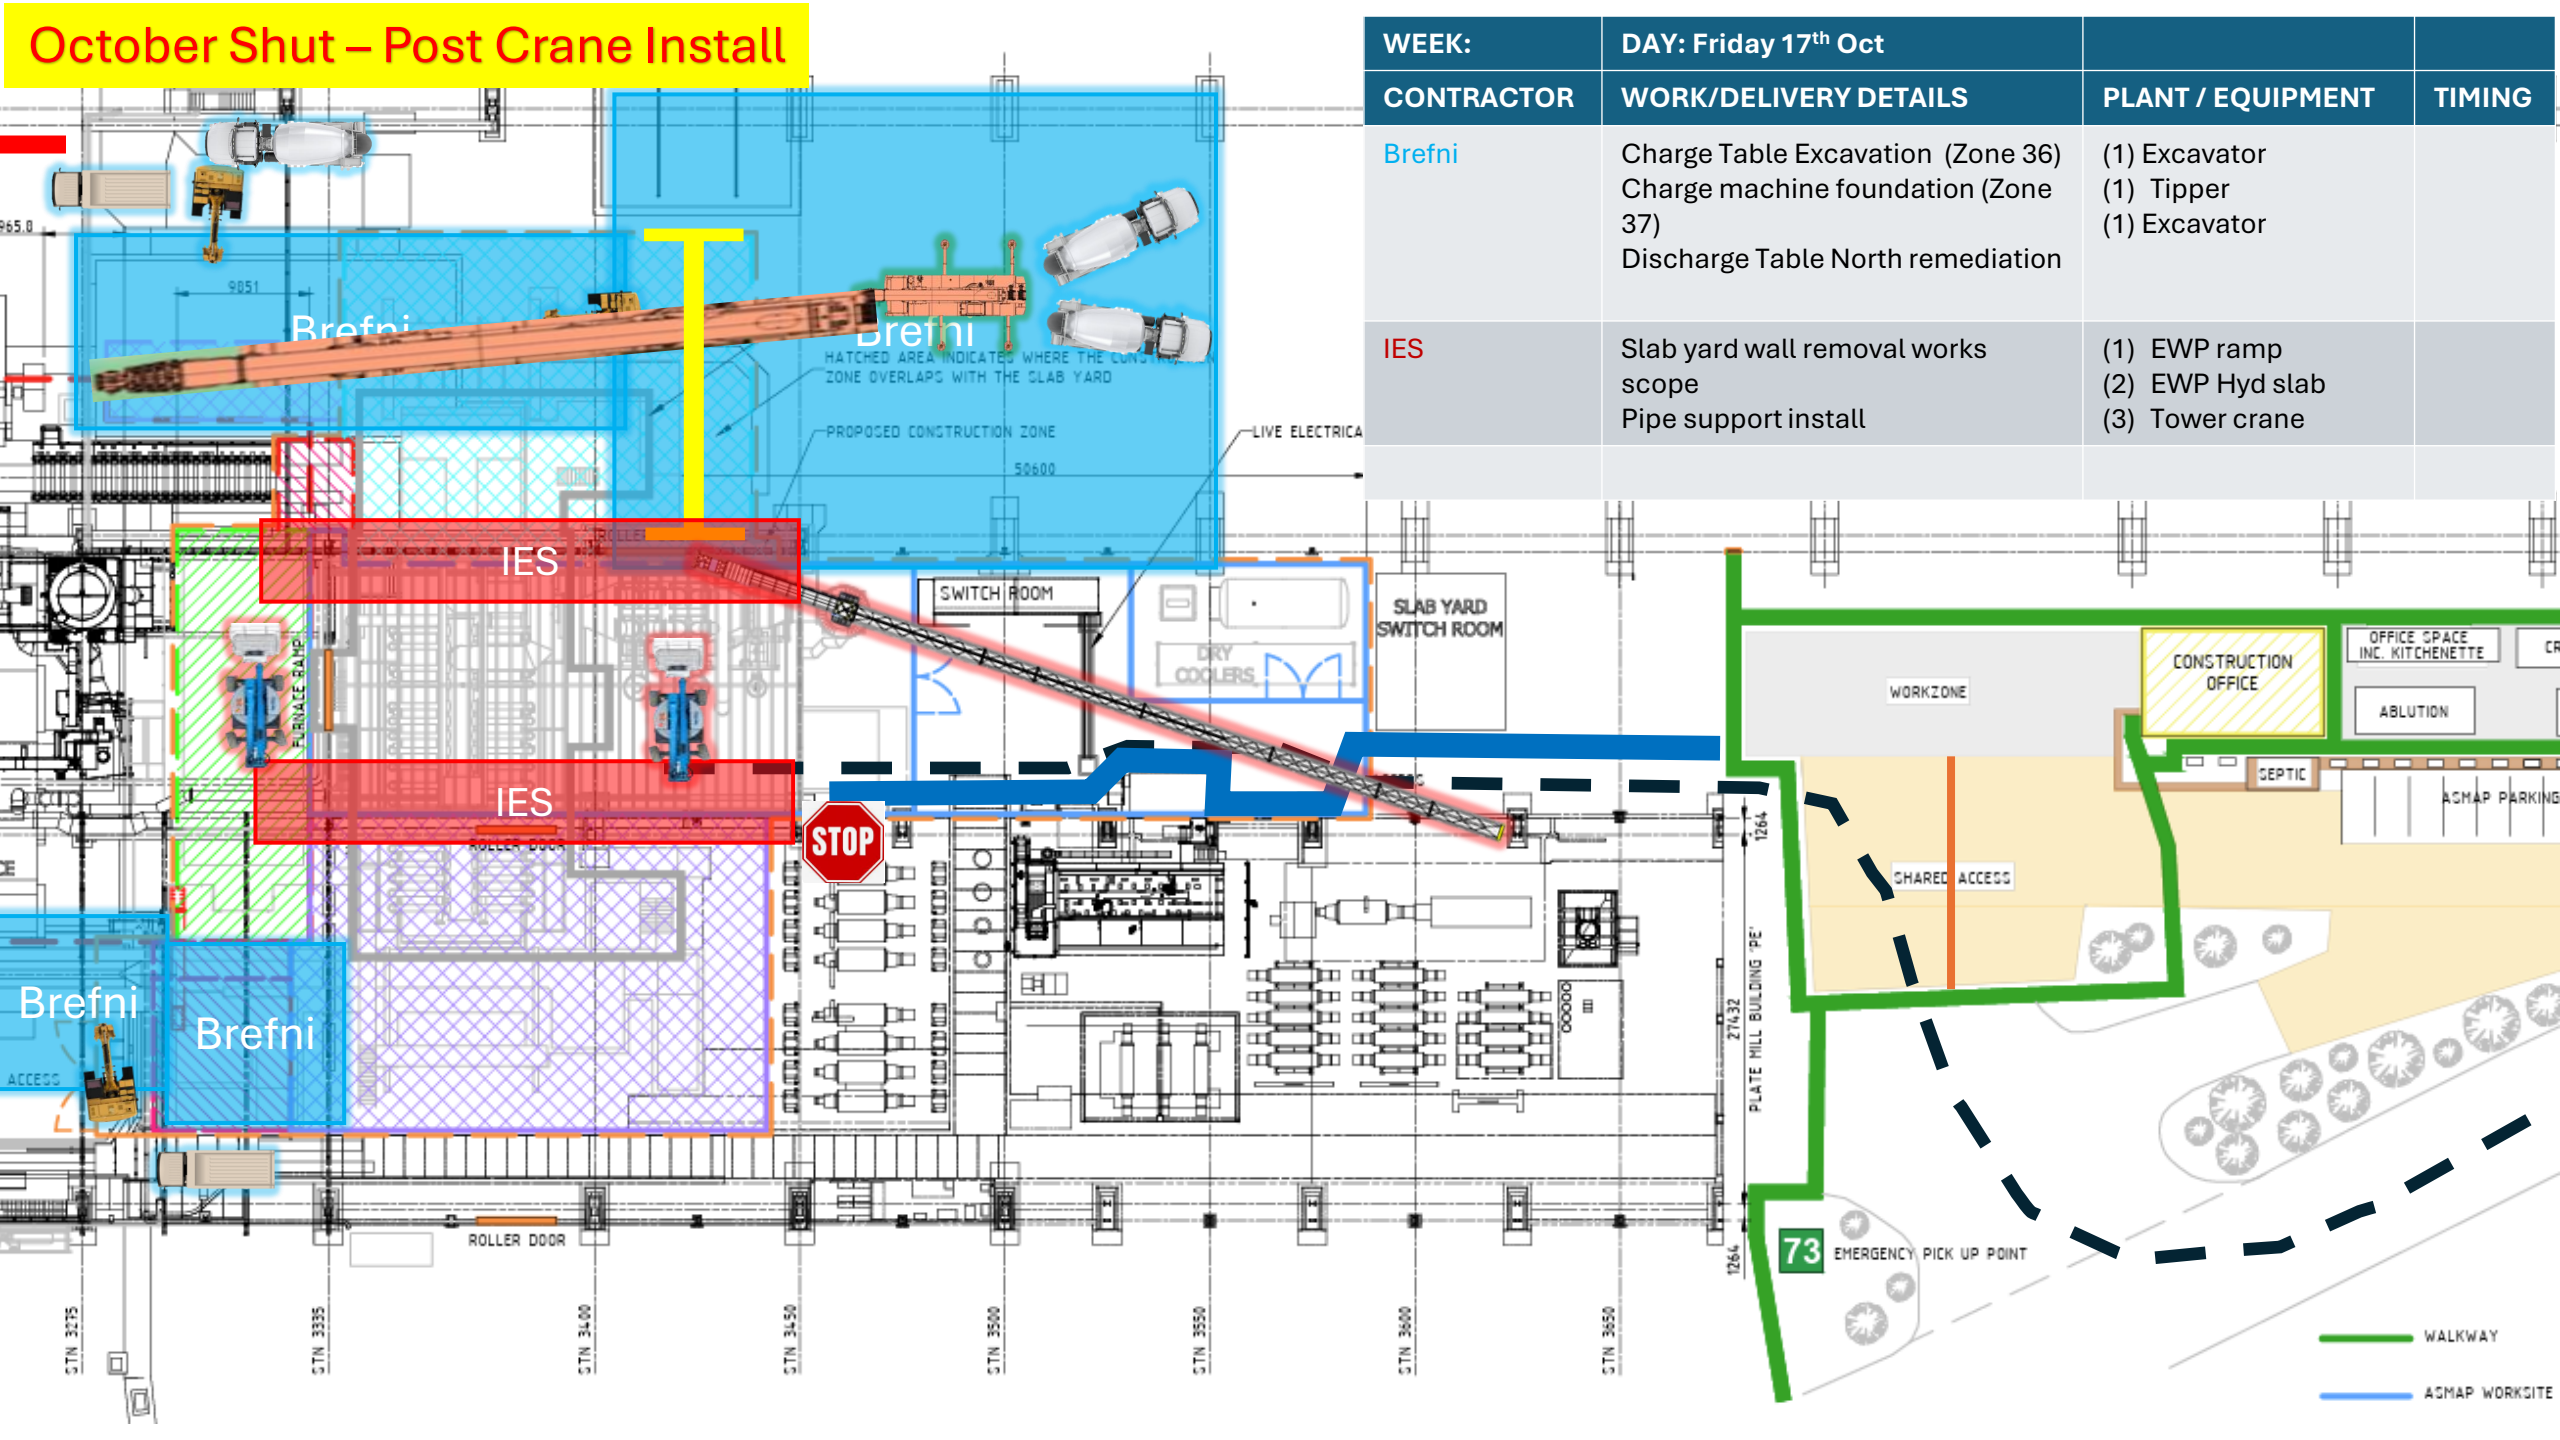


WEEK:	DAY: Friday 17 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Slab yard wall removal works scope Pipe support install	(1) EWP ramp (2) EWP Hyd slab (3) Tower crane	

October Shut – Post Crane Install

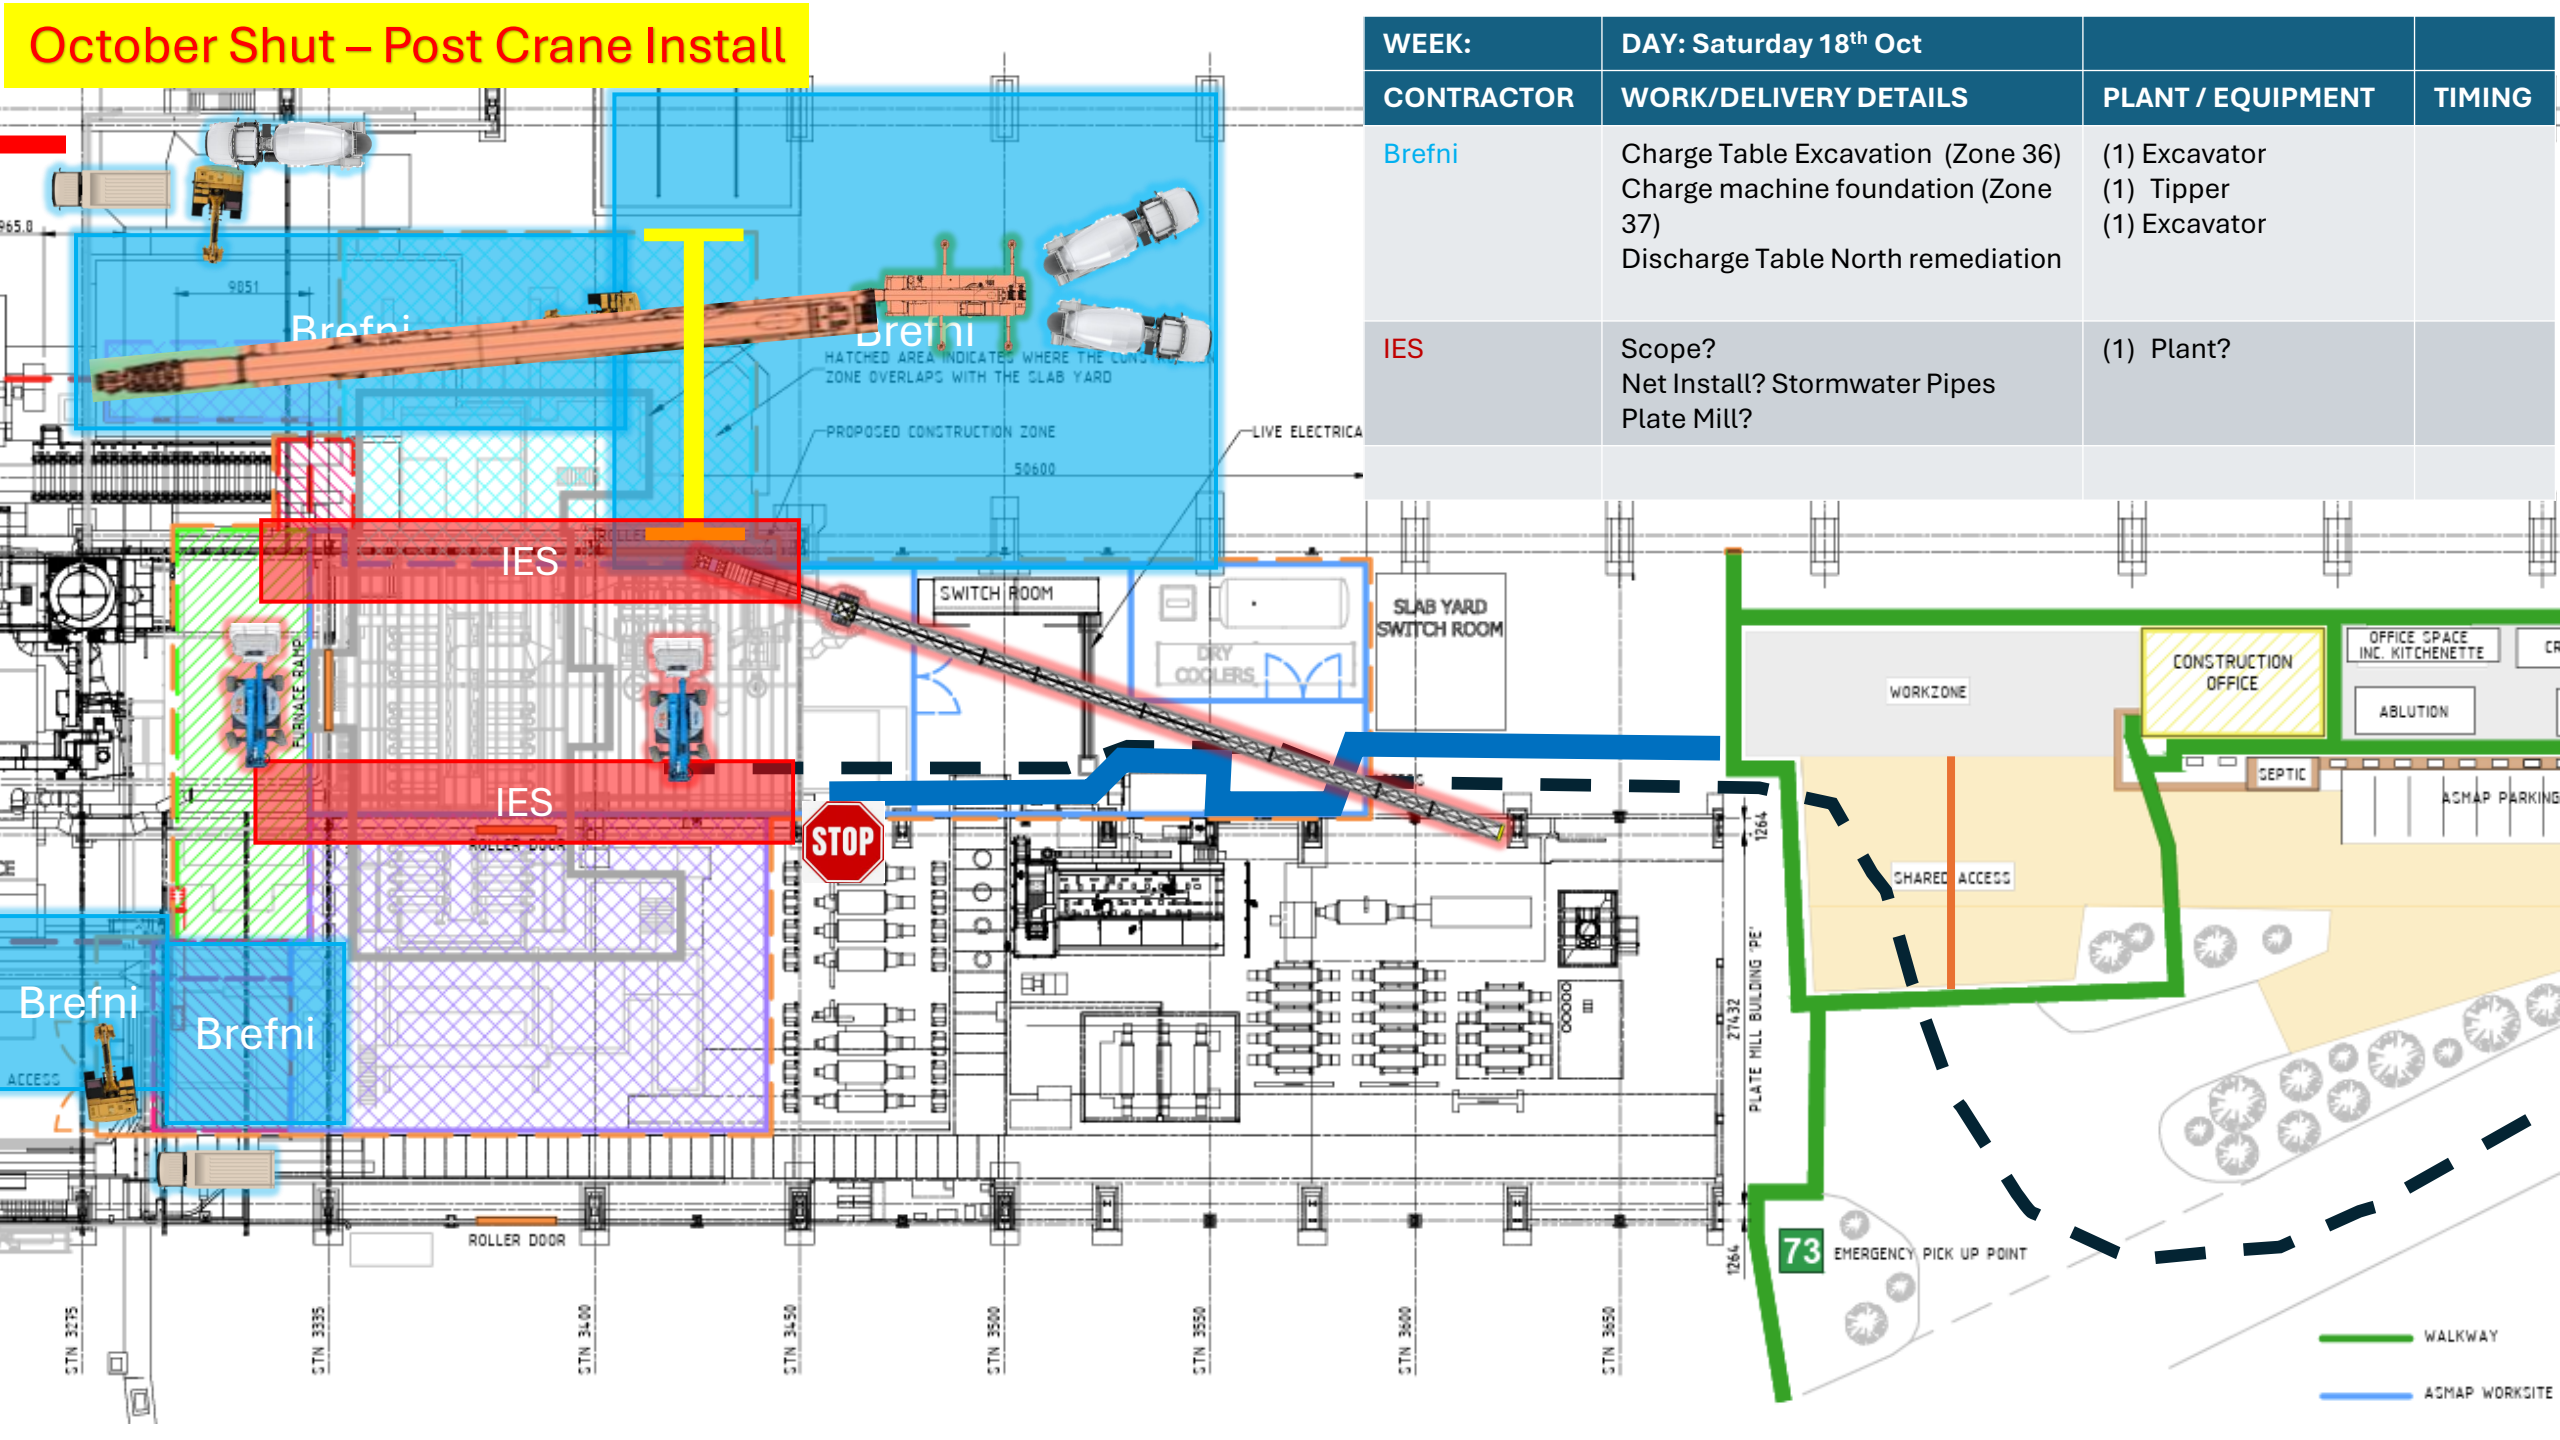


WEEK:	DAY: Saturday 18 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Scope? Net Install? Stormwater Pipes Plate Mill?	(1) Plant?	

October Shut – Post Crane Install

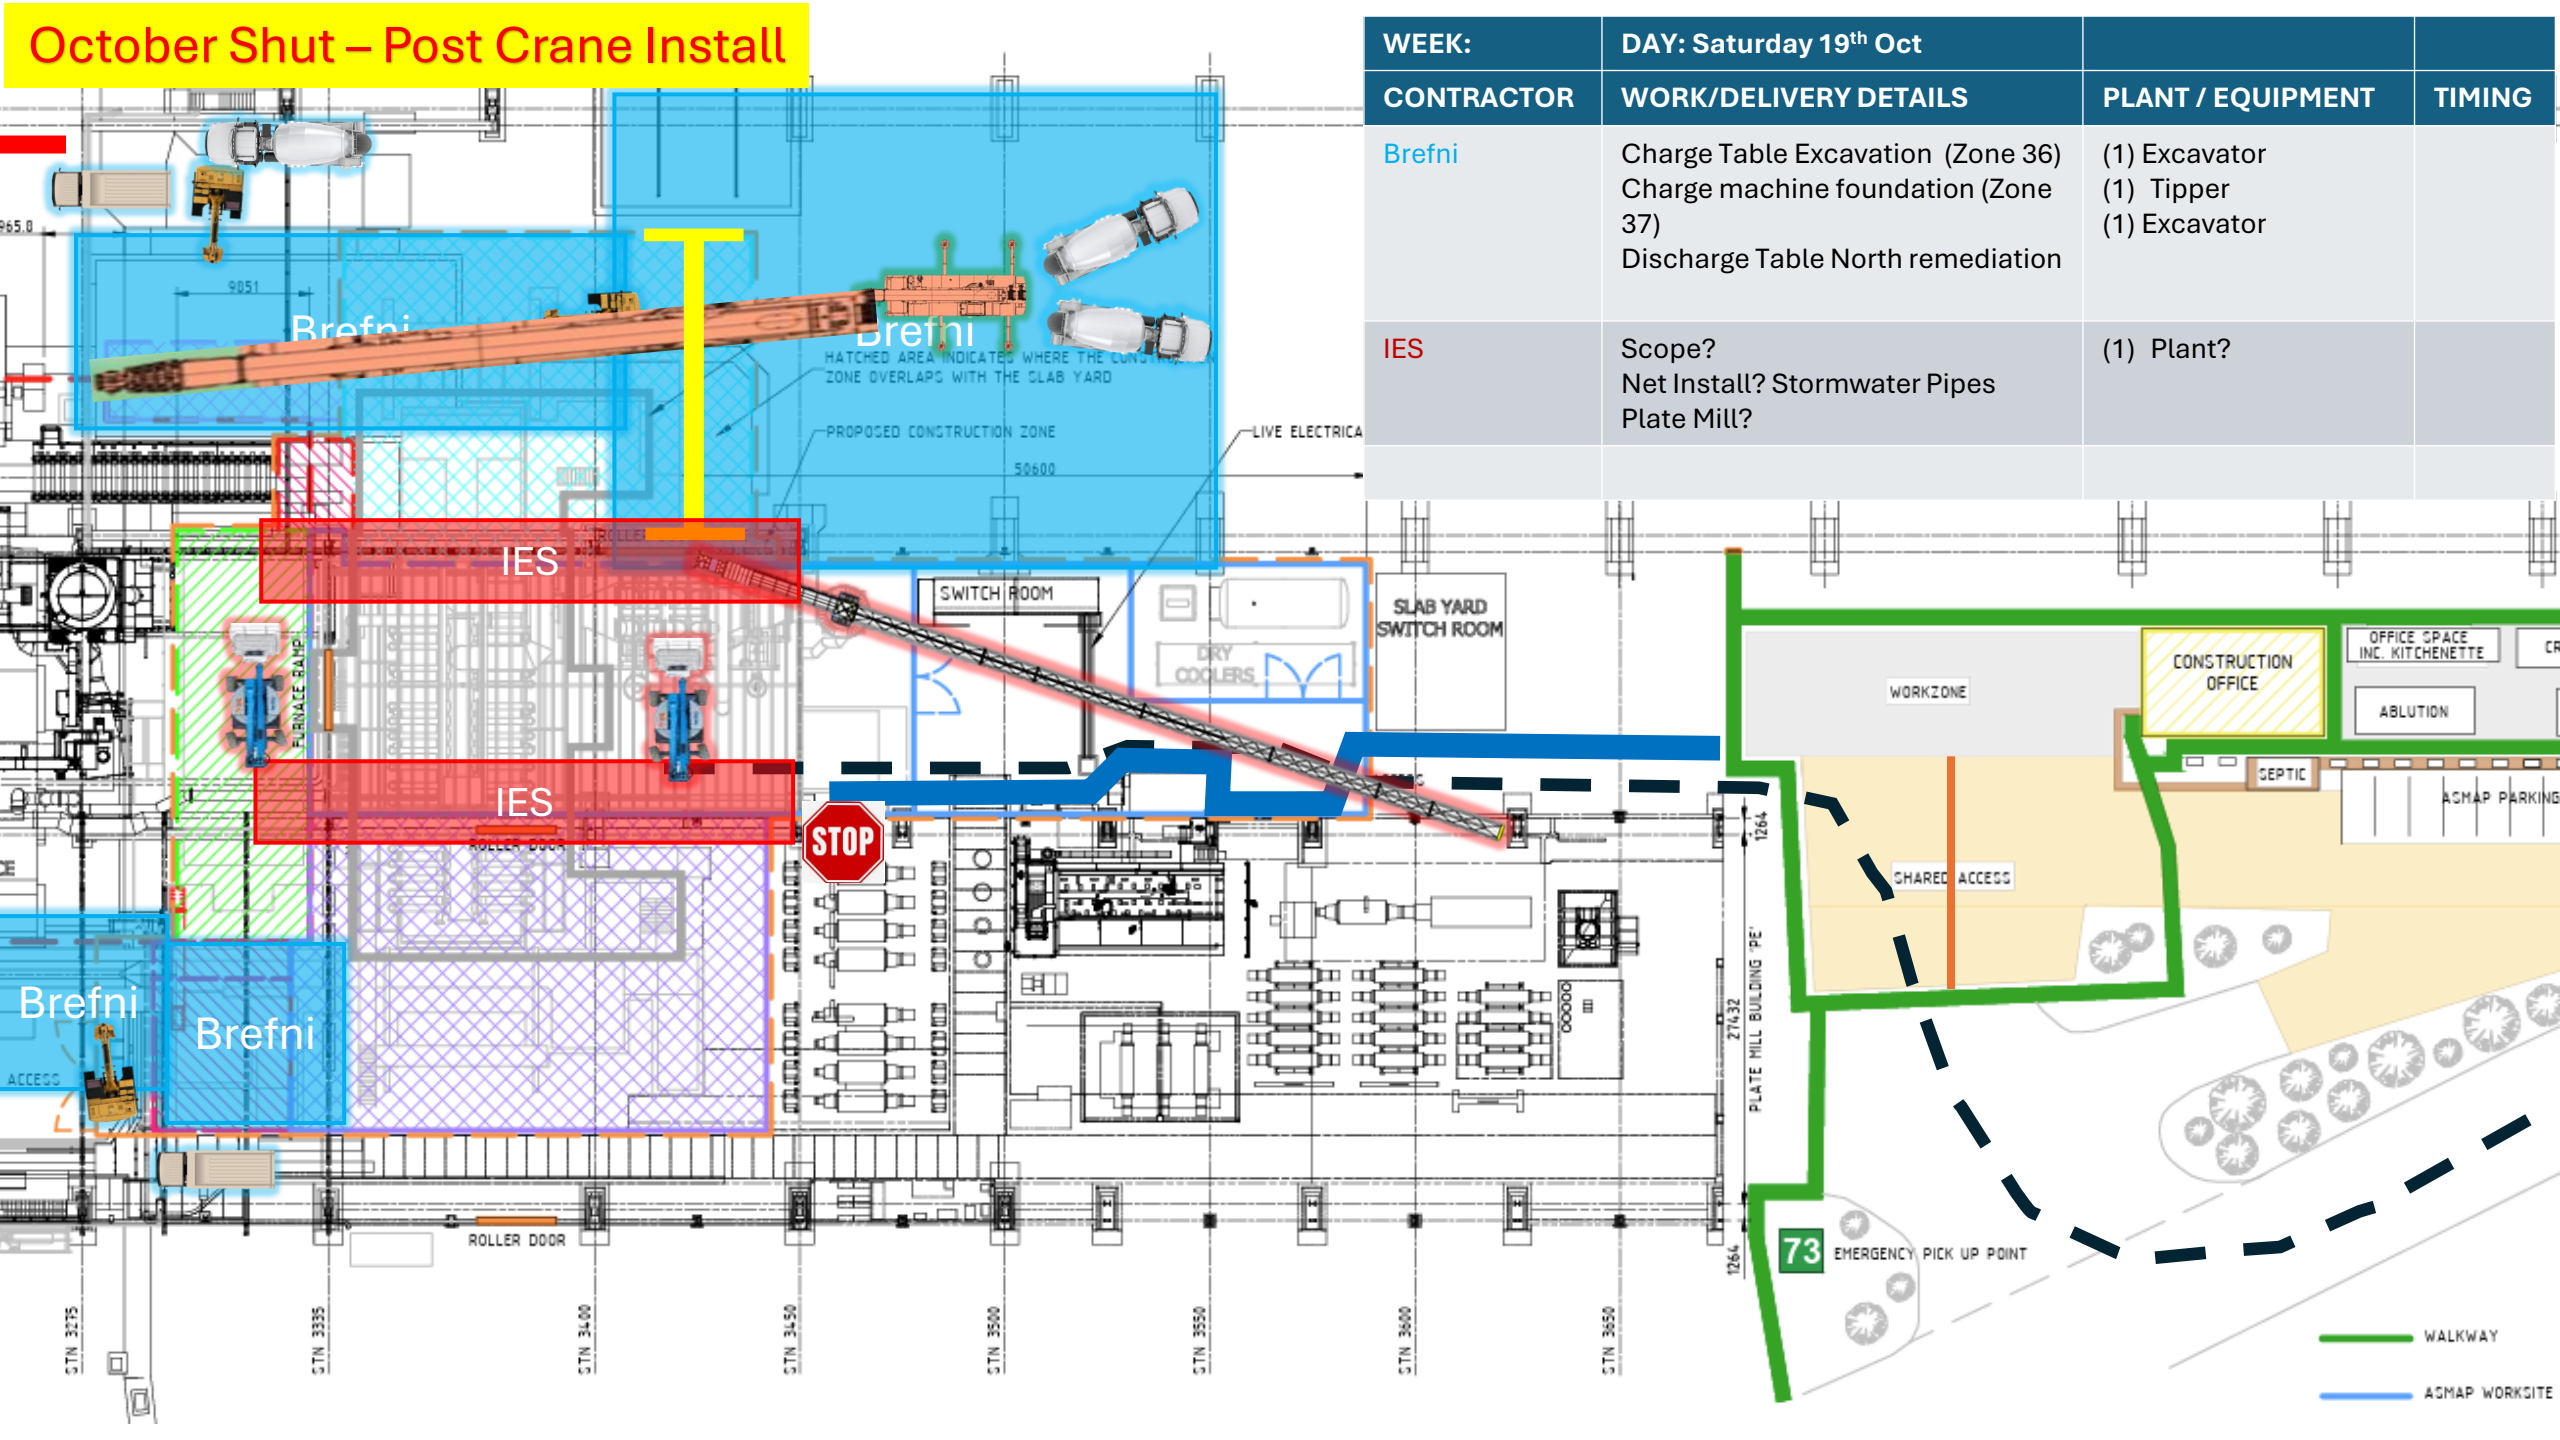


WEEK:	DAY: Saturday 19 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Scope? Net Install? Stormwater Pipes Plate Mill?	(1) Plant?	

October Shut – Post Crane Install

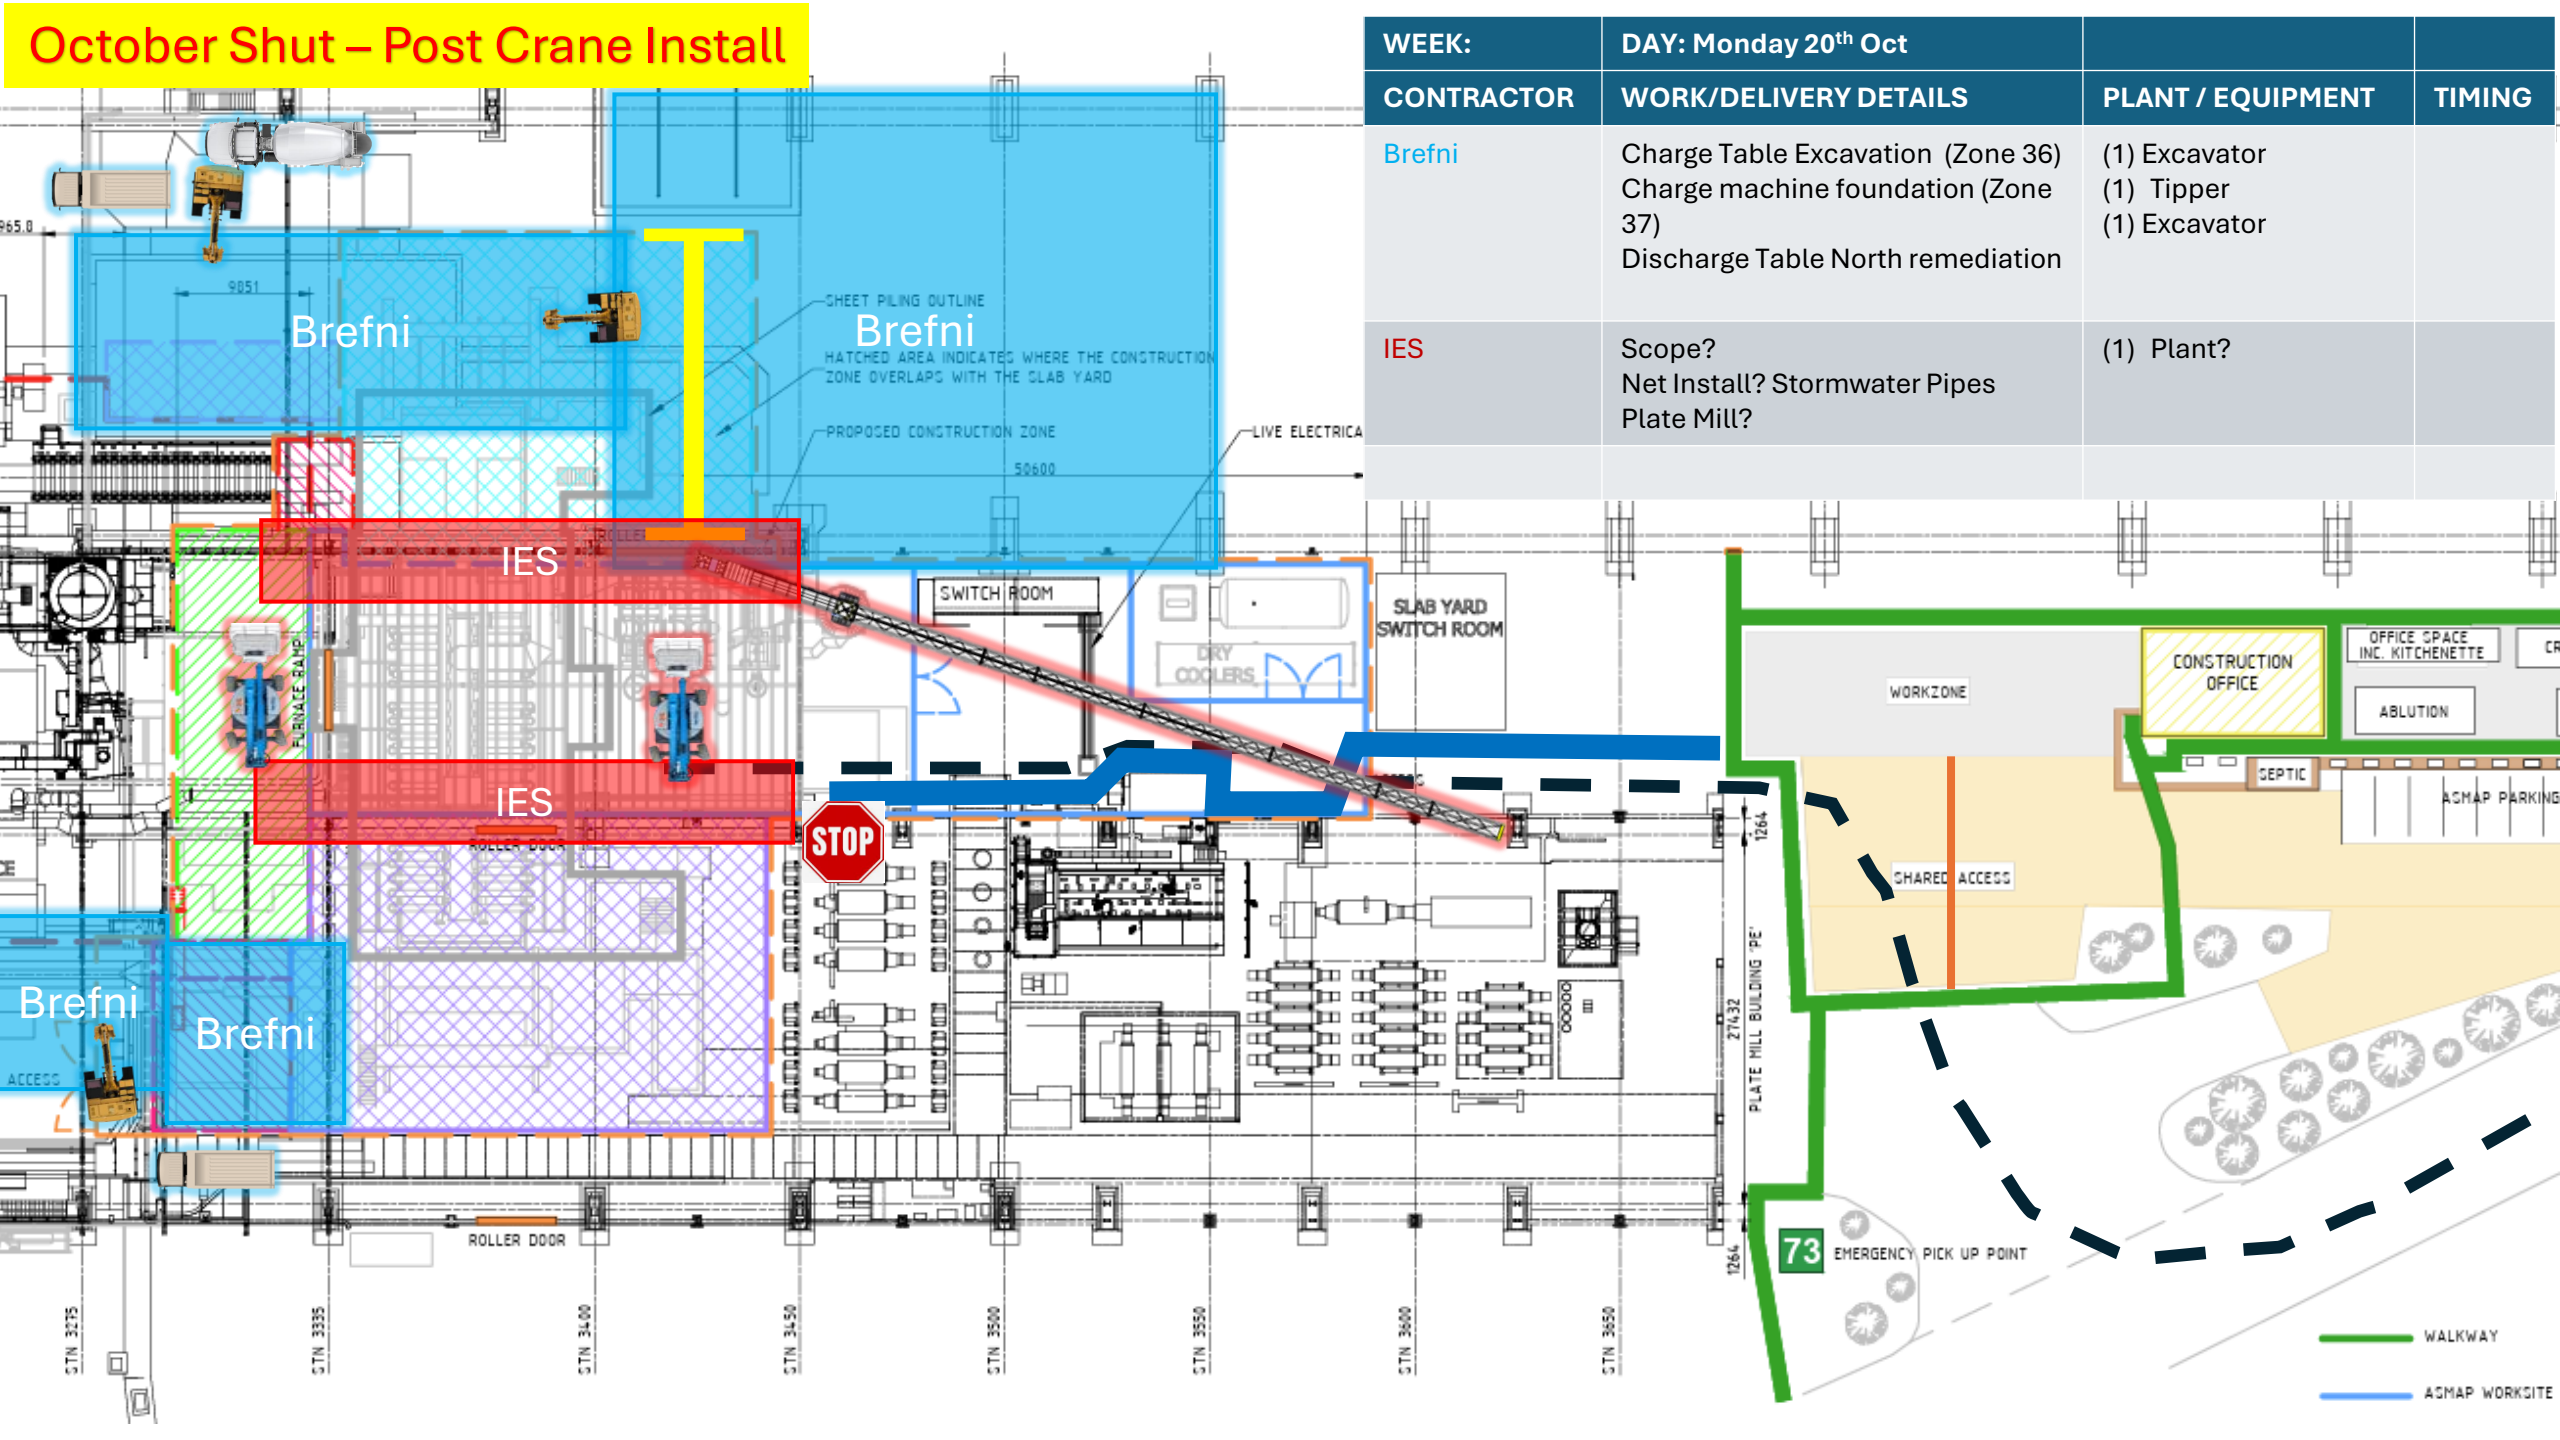


WEEK:	DAY: Monday 20 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Scope? Net Install? Stormwater Pipes Plate Mill?	(1) Plant?	

October Shut – Post Crane Install

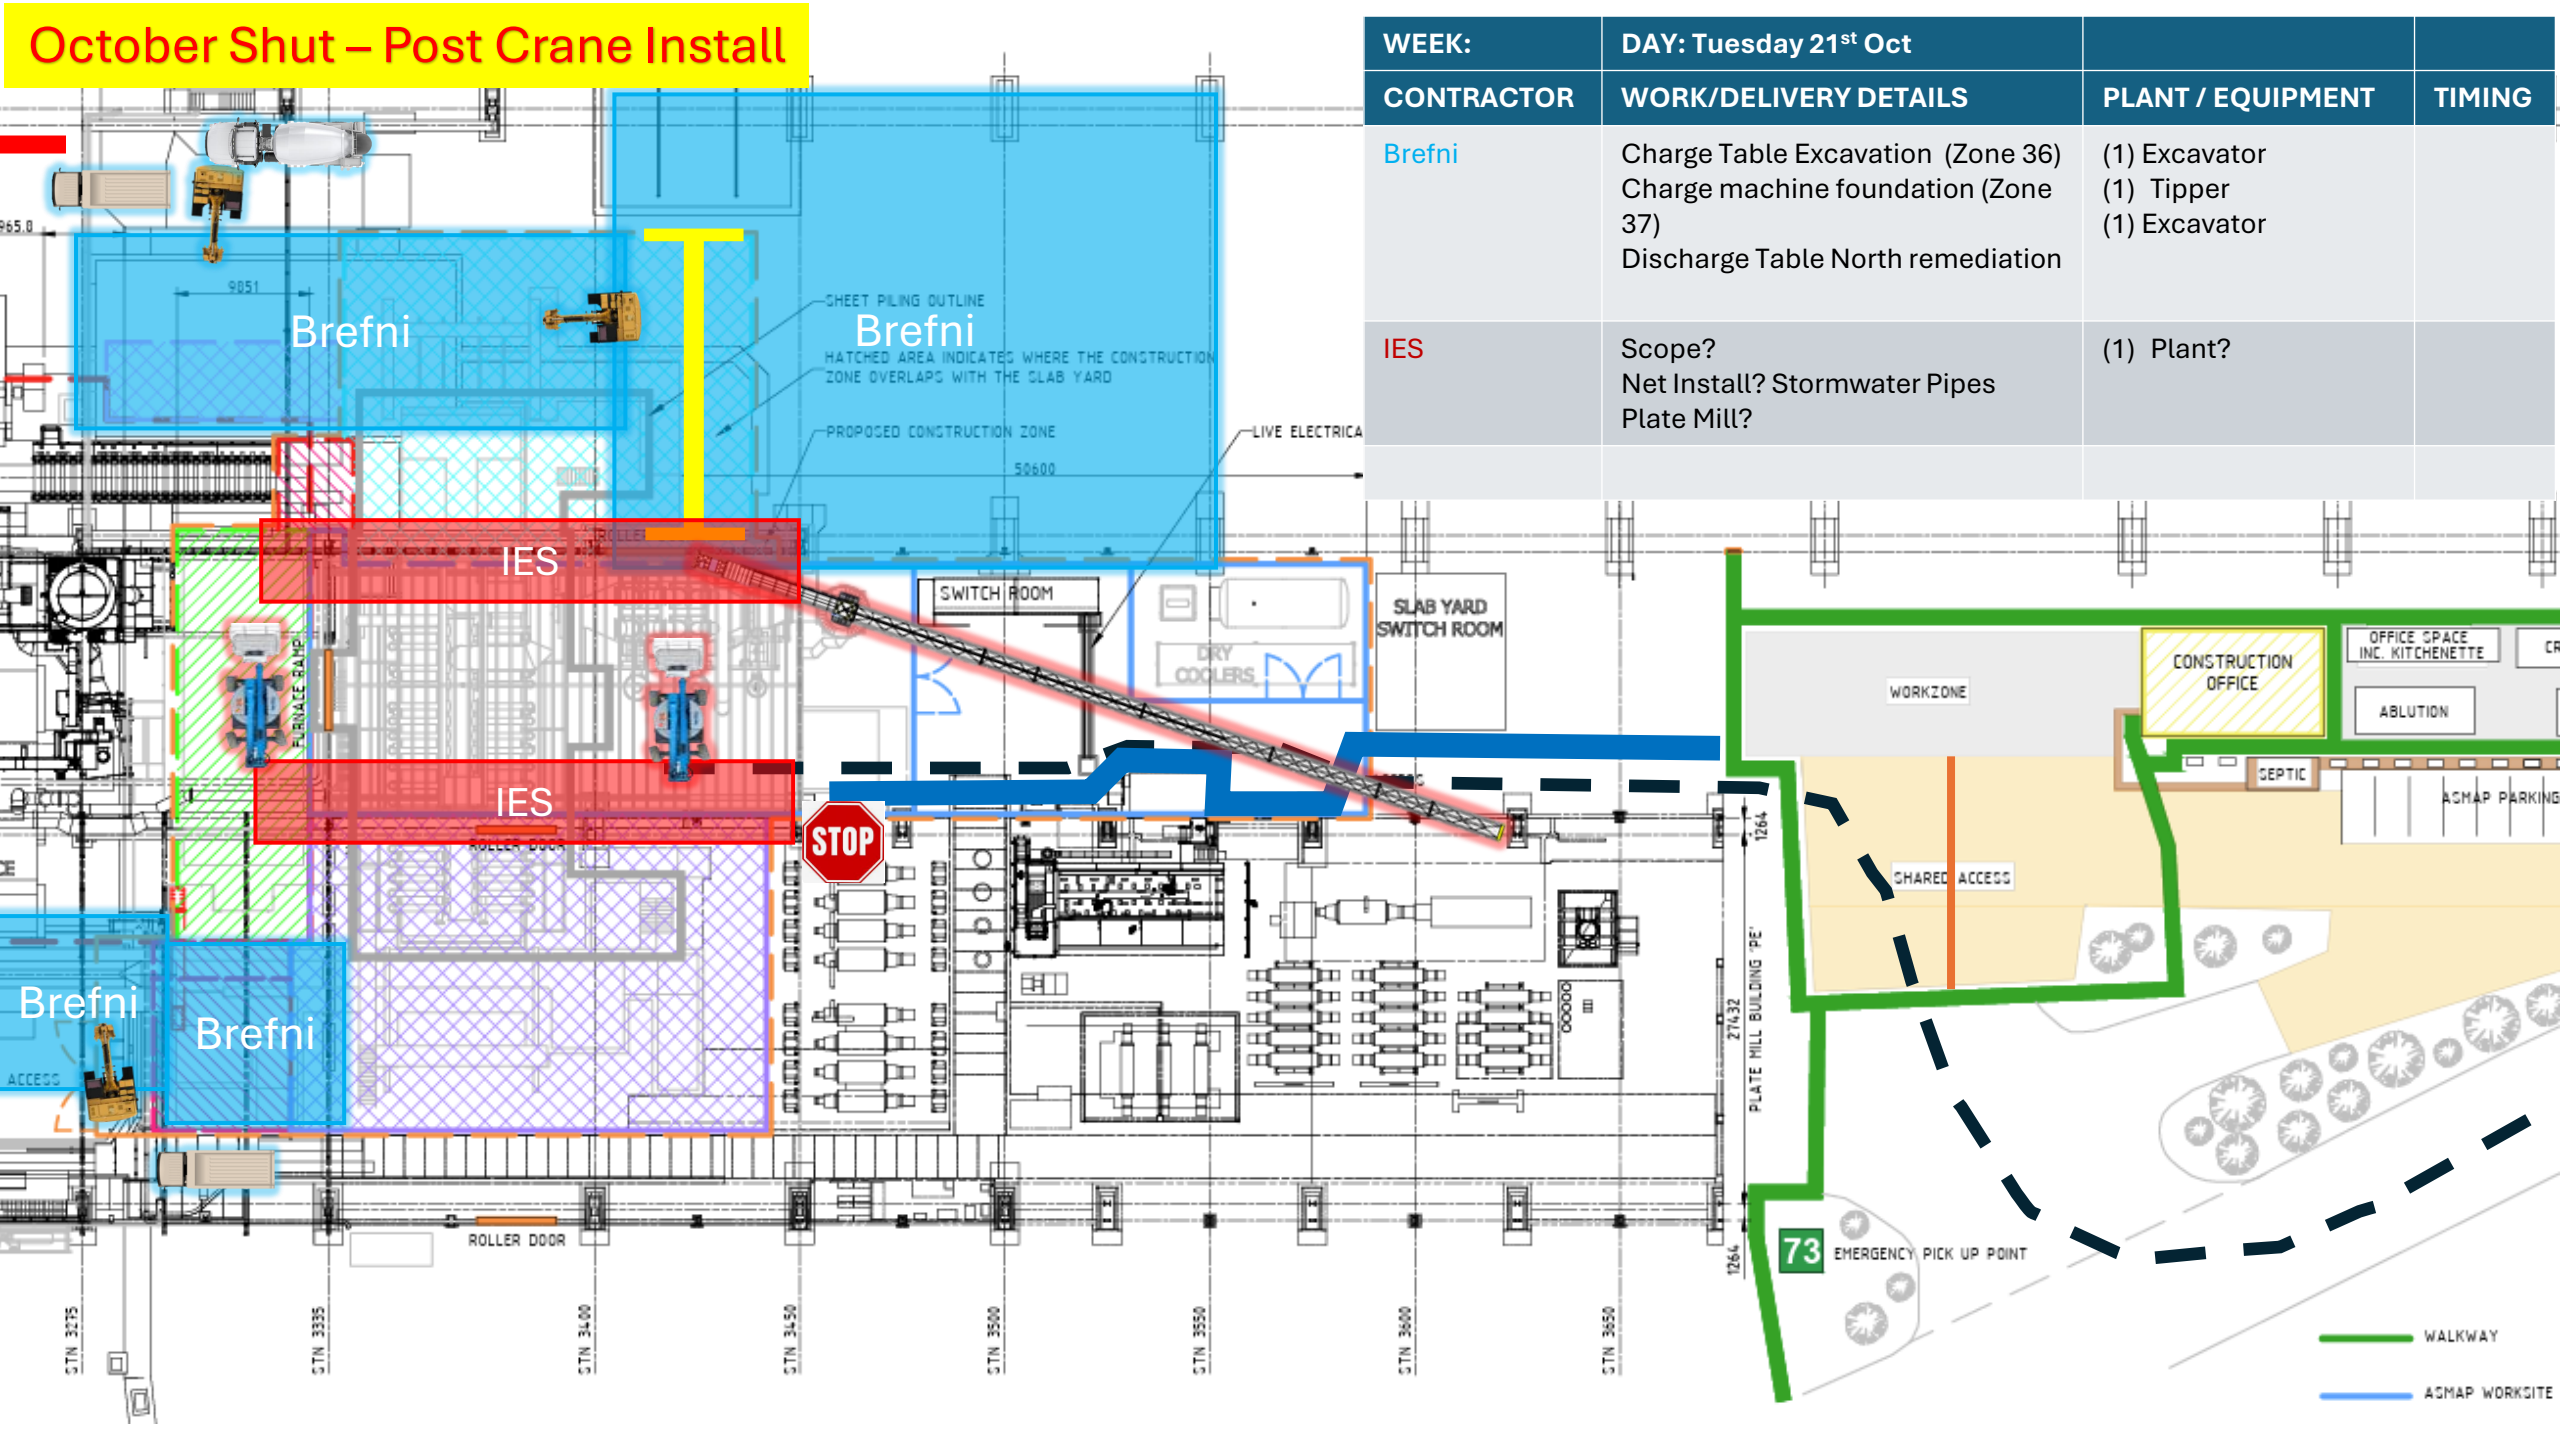


WEEK:	DAY: Tuesday 21 st Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Scope? Net Install? Stormwater Pipes Plate Mill?	(1) Plant?	

October Shut – Post Crane Install

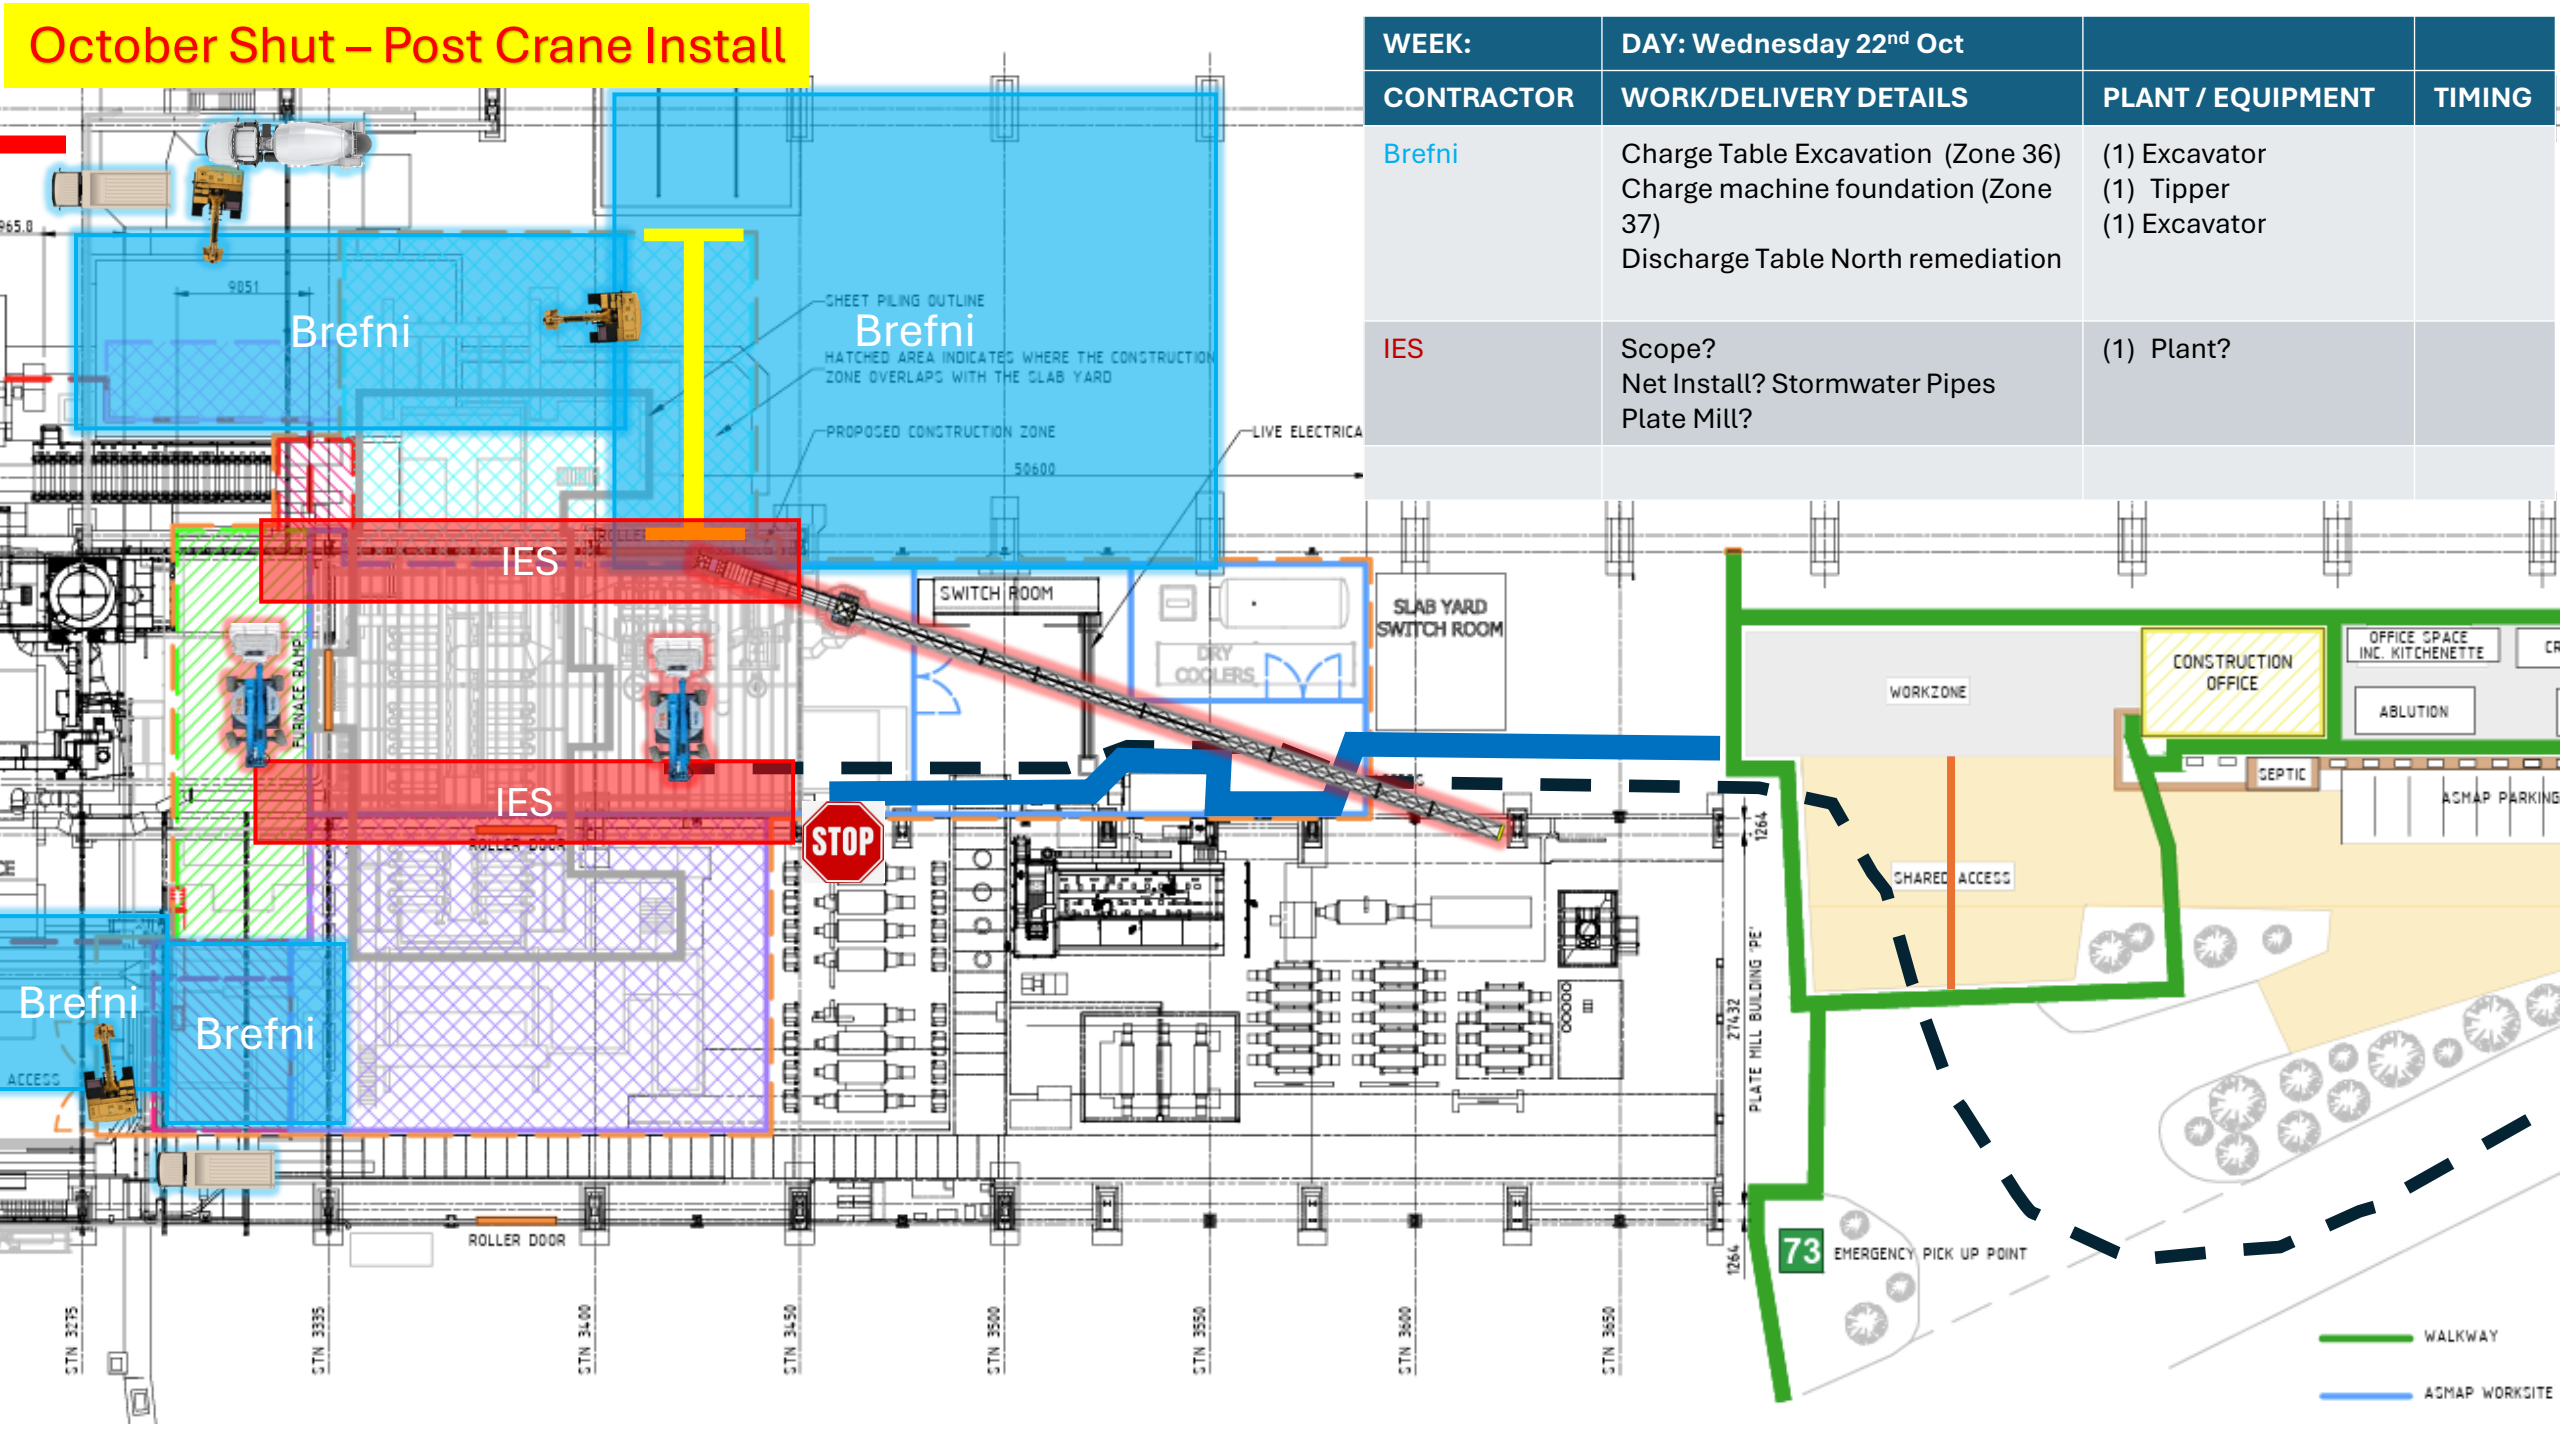

WEEK:	DAY: Wednesday 22 nd Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Scope? Net Install? Stormwater Pipes Plate Mill?	(1) Plant?	

October Shut – Post Crane Install

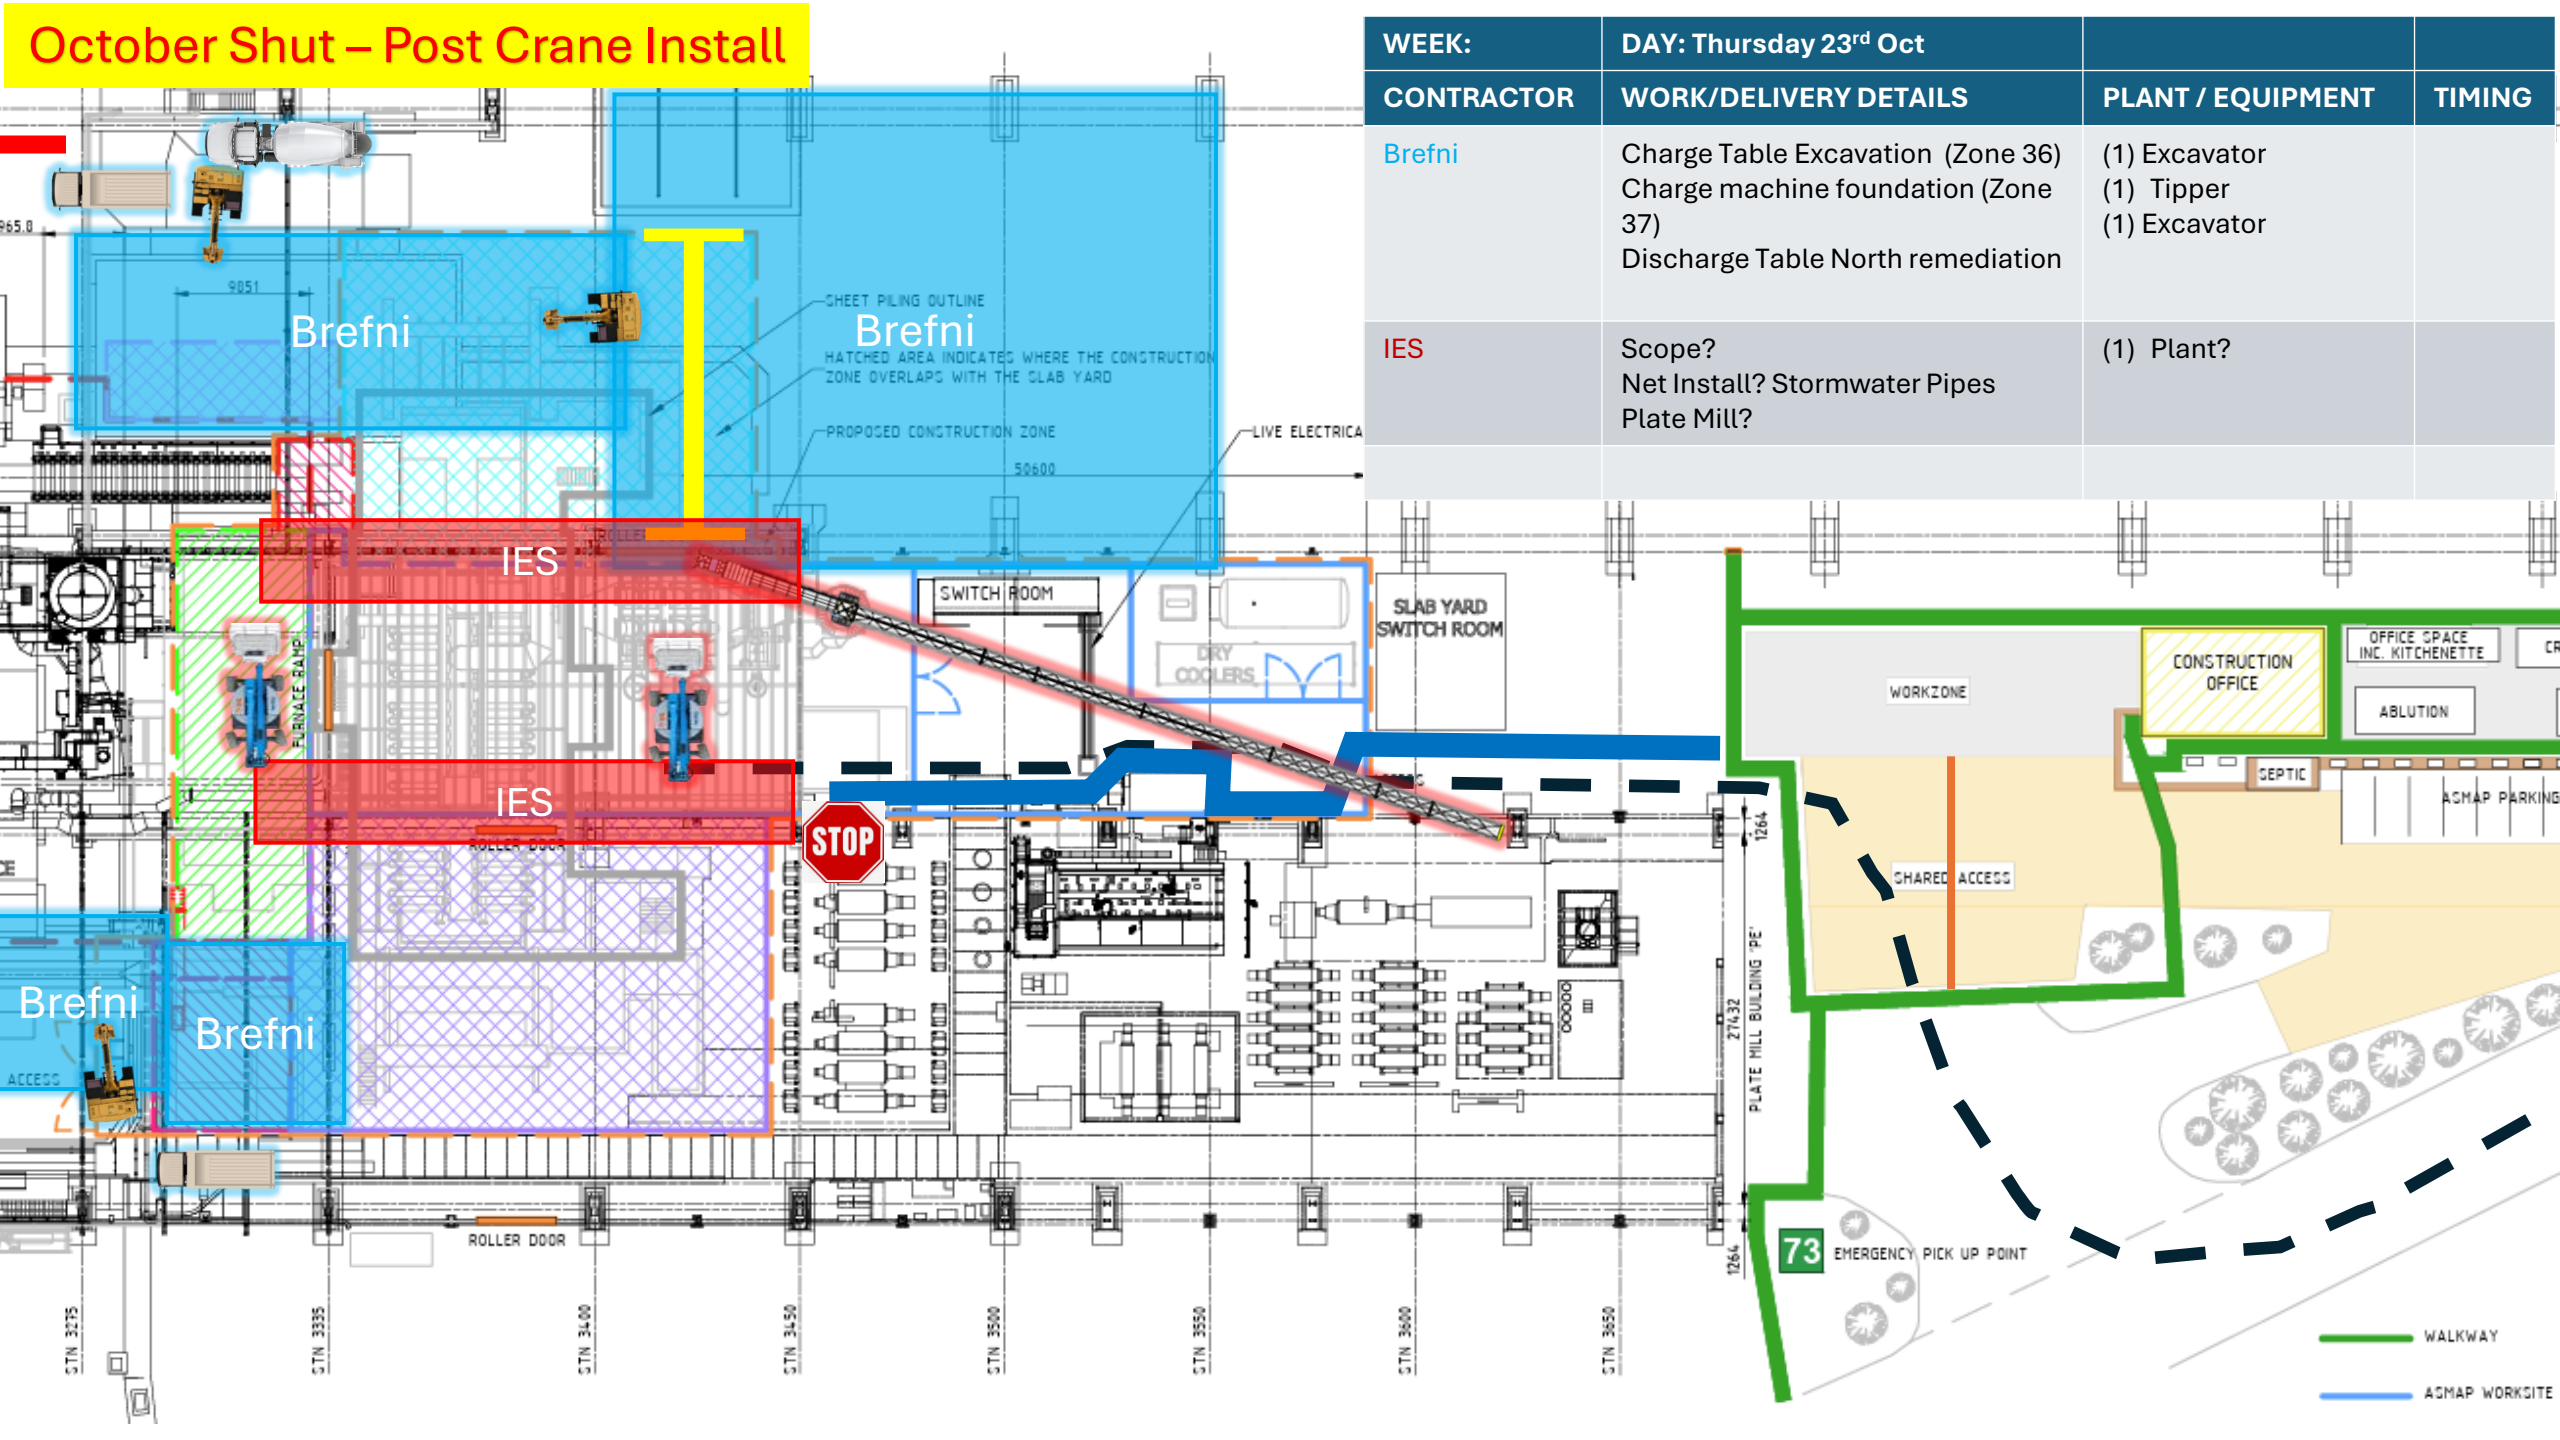

WEEK:	DAY: Thursday 23 rd Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Scope? Net Install? Stormwater Pipes Plate Mill?	(1) Plant?	


October Shut – Post Crane Install

WEEK:	DAY: Friday 24 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Scope? Net Install? Stormwater Pipes Plate Mill?	(1) Plant?	
BSL	Replace fishplate isolators for full length live rails		TBC
Transfer Car work	1. re-instate fence then. 2. Remove temp fence		

October Shut – Post Crane Install


WEEK:	DAY: Friday 24 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Scope? Net Install? Stormwater Pipes Plate Mill?	(1) Plant?	
BSL	Replace fishplate isolators for full length live rails		TBC
Transfer Car work	1. re-instate fence then. 2. Remove temp fence		

October Shut – END

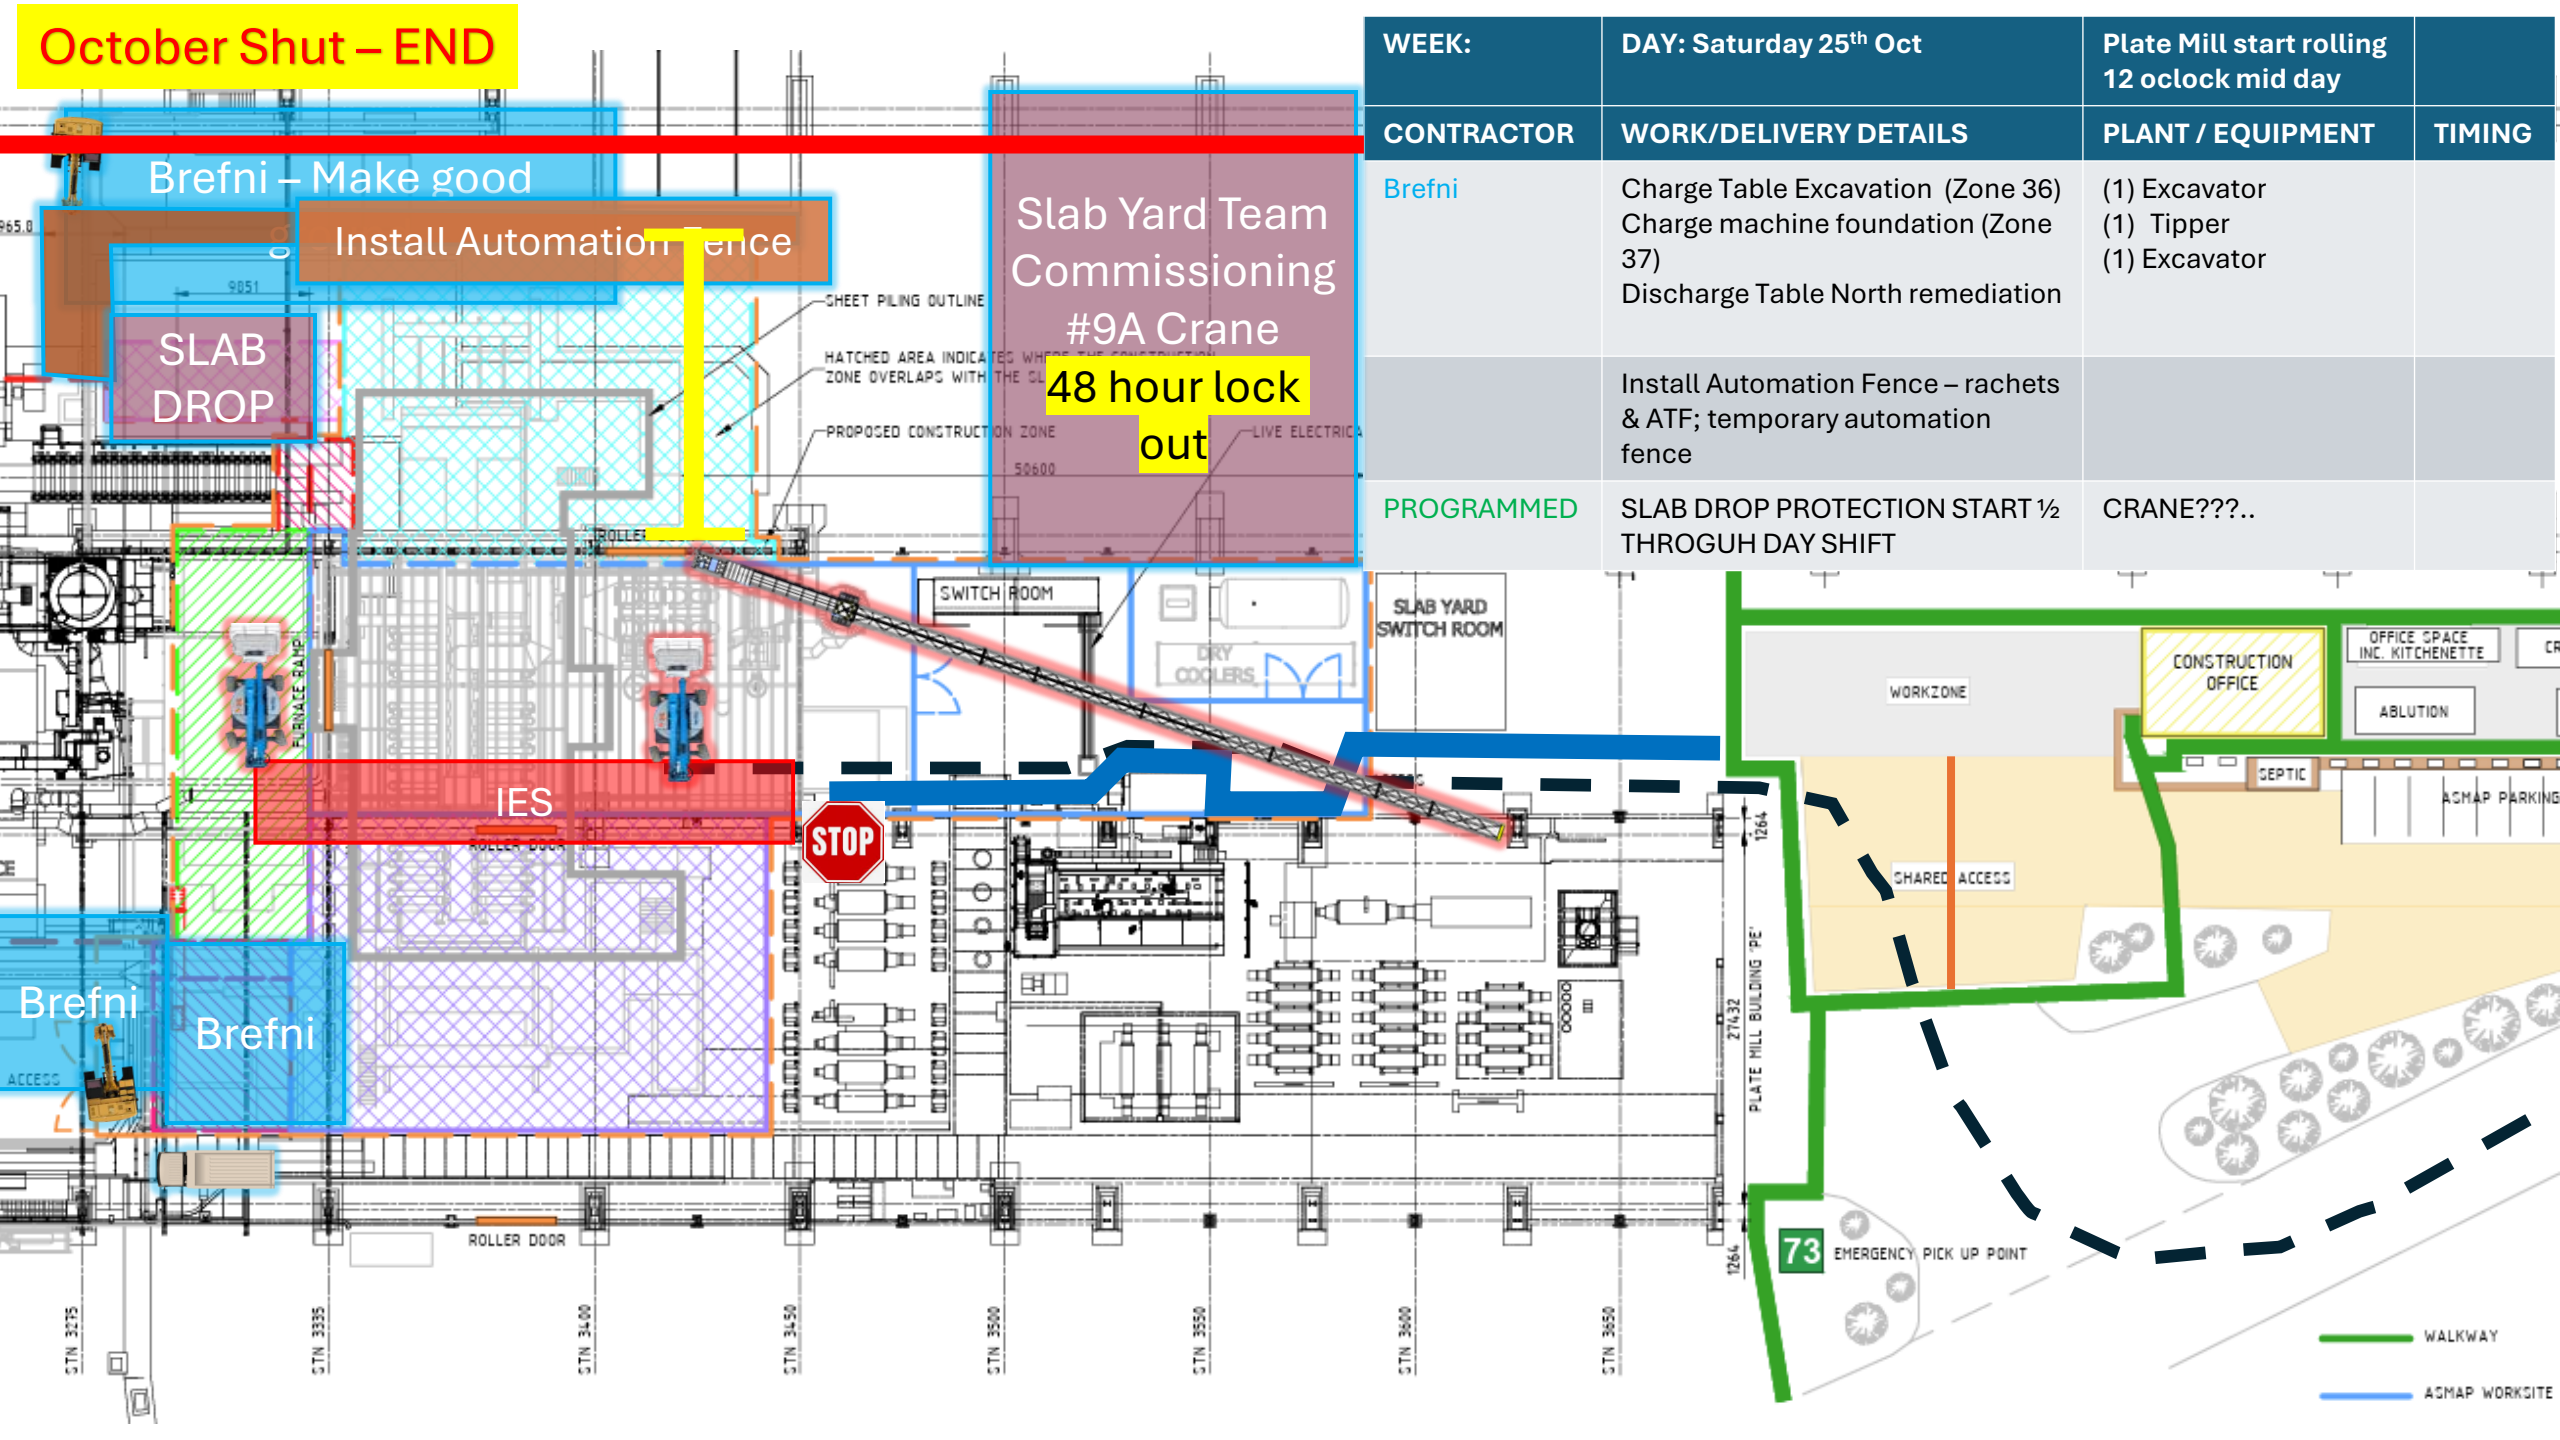


WEEK:	DAY: Saturday 25 th Oct	Plate Mill start rolling 12 oclock mid day	
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation (Zone 36) Charge machine foundation (Zone 37) Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
	Install Automation Fence – rachets & ATF; temporary automation fence		
PROGRAMMED	SLAB DROP PROTECTION START ½ THROGUH DAY SHIFT	CRANE????..	

October Shut – END

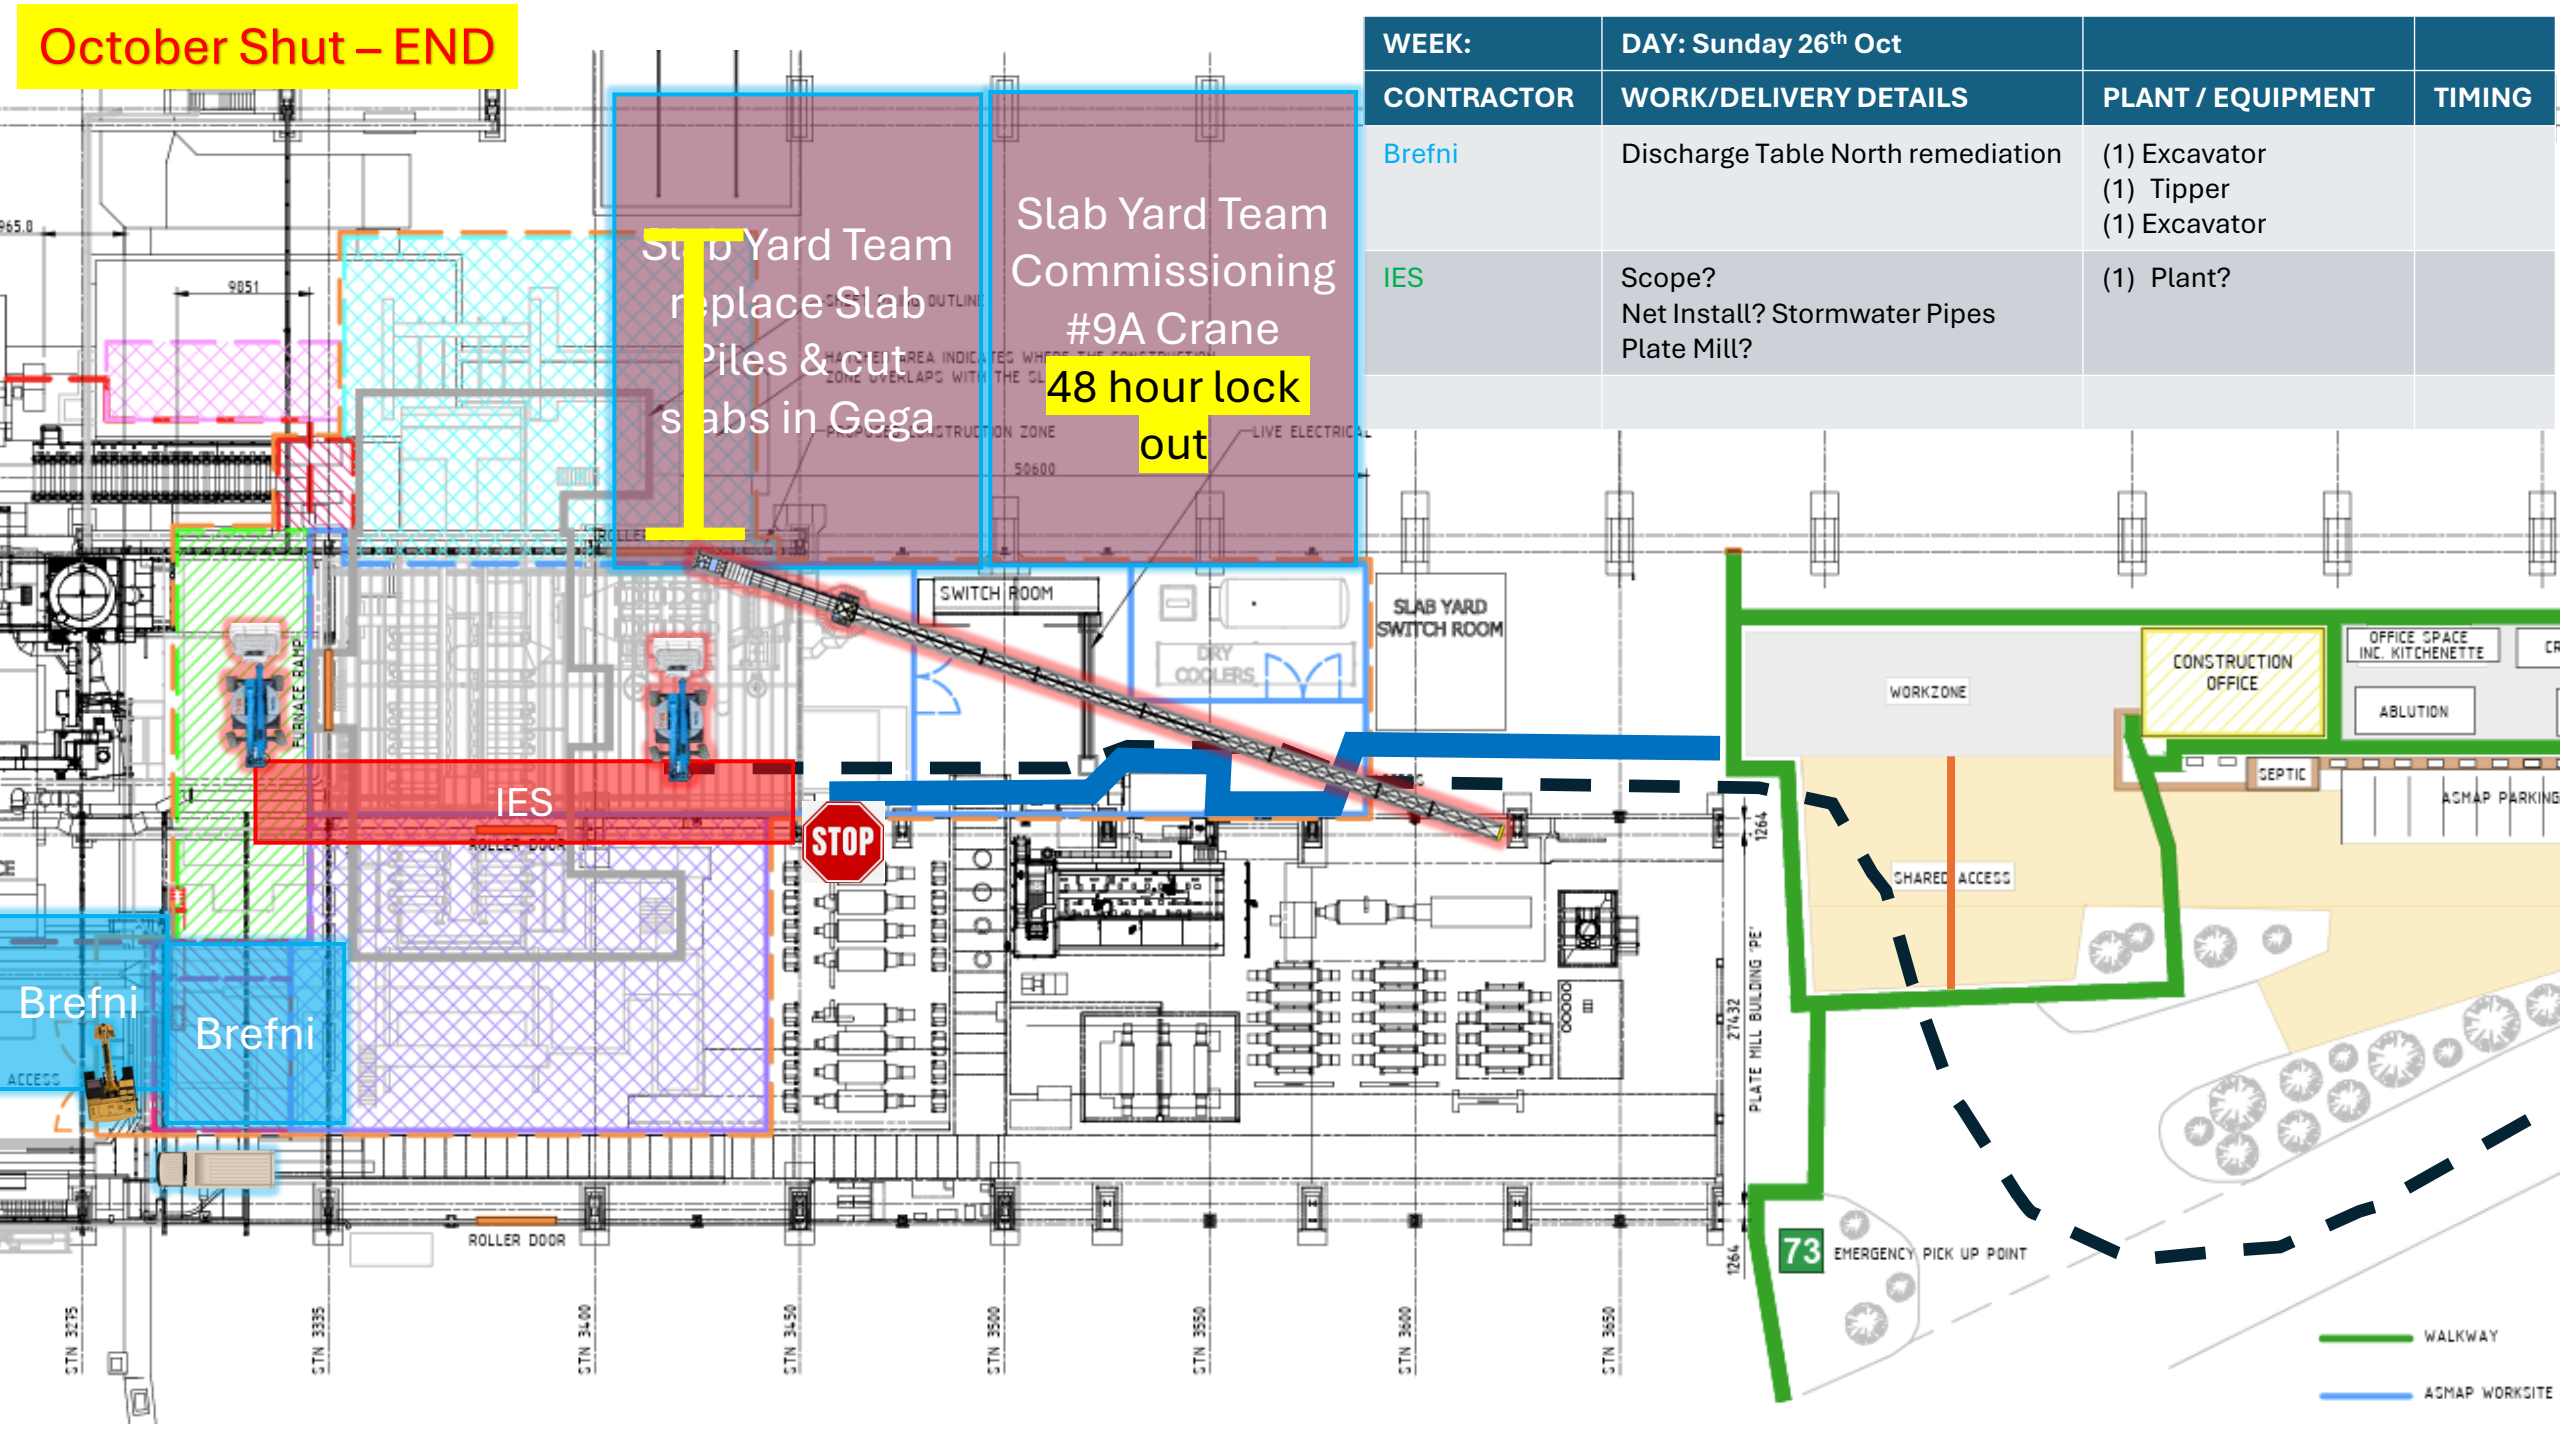

WEEK:	DAY: Sunday 26 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Scope? Net Install? Stormwater Pipes Plate Mill?	(1) Plant?	

October Shut – END

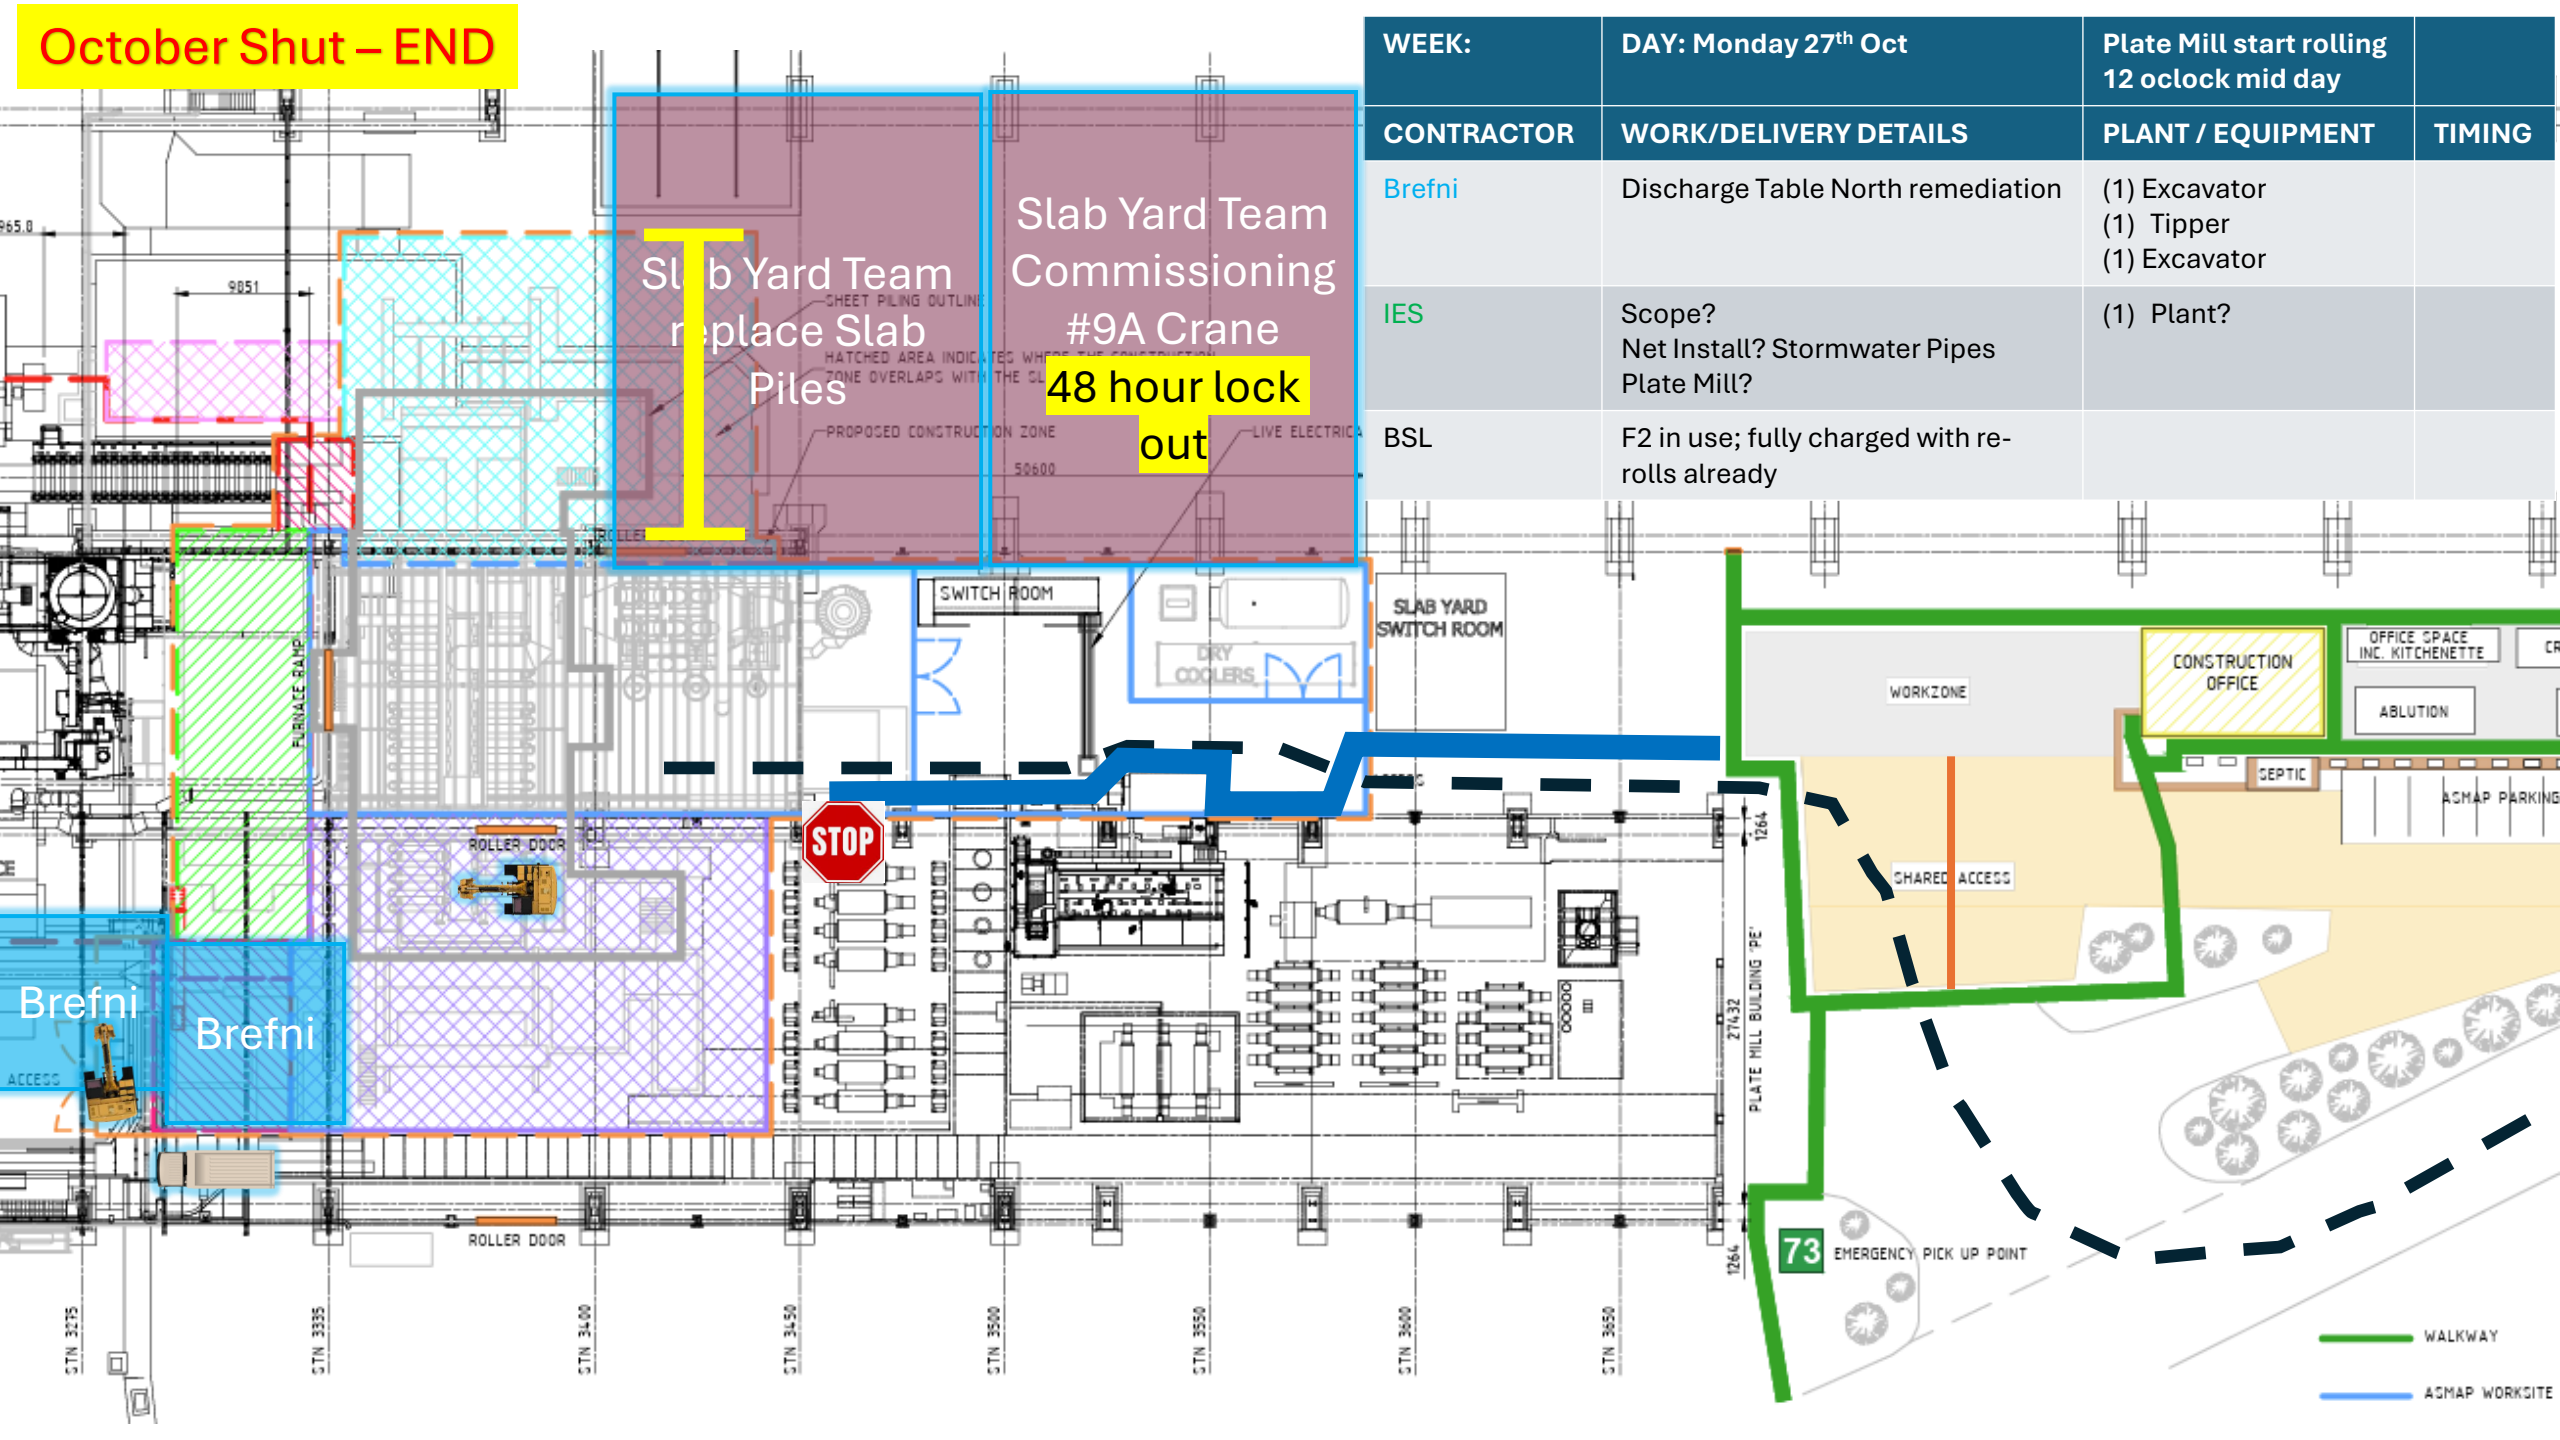

WEEK:	DAY: Monday 27 th Oct	Plate Mill start rolling 12 oclock mid day	
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Discharge Table North remediation	(1) Excavator (1) Tipper (1) Excavator	
IES	Scope? Net Install? Stormwater Pipes Plate Mill?	(1) Plant?	
BSL	F2 in use; fully charged with re-rolls already		
