




Daily Access	
11am	
3pm	
Post 7pm	

# UPCOMING WORK THIS WEEK

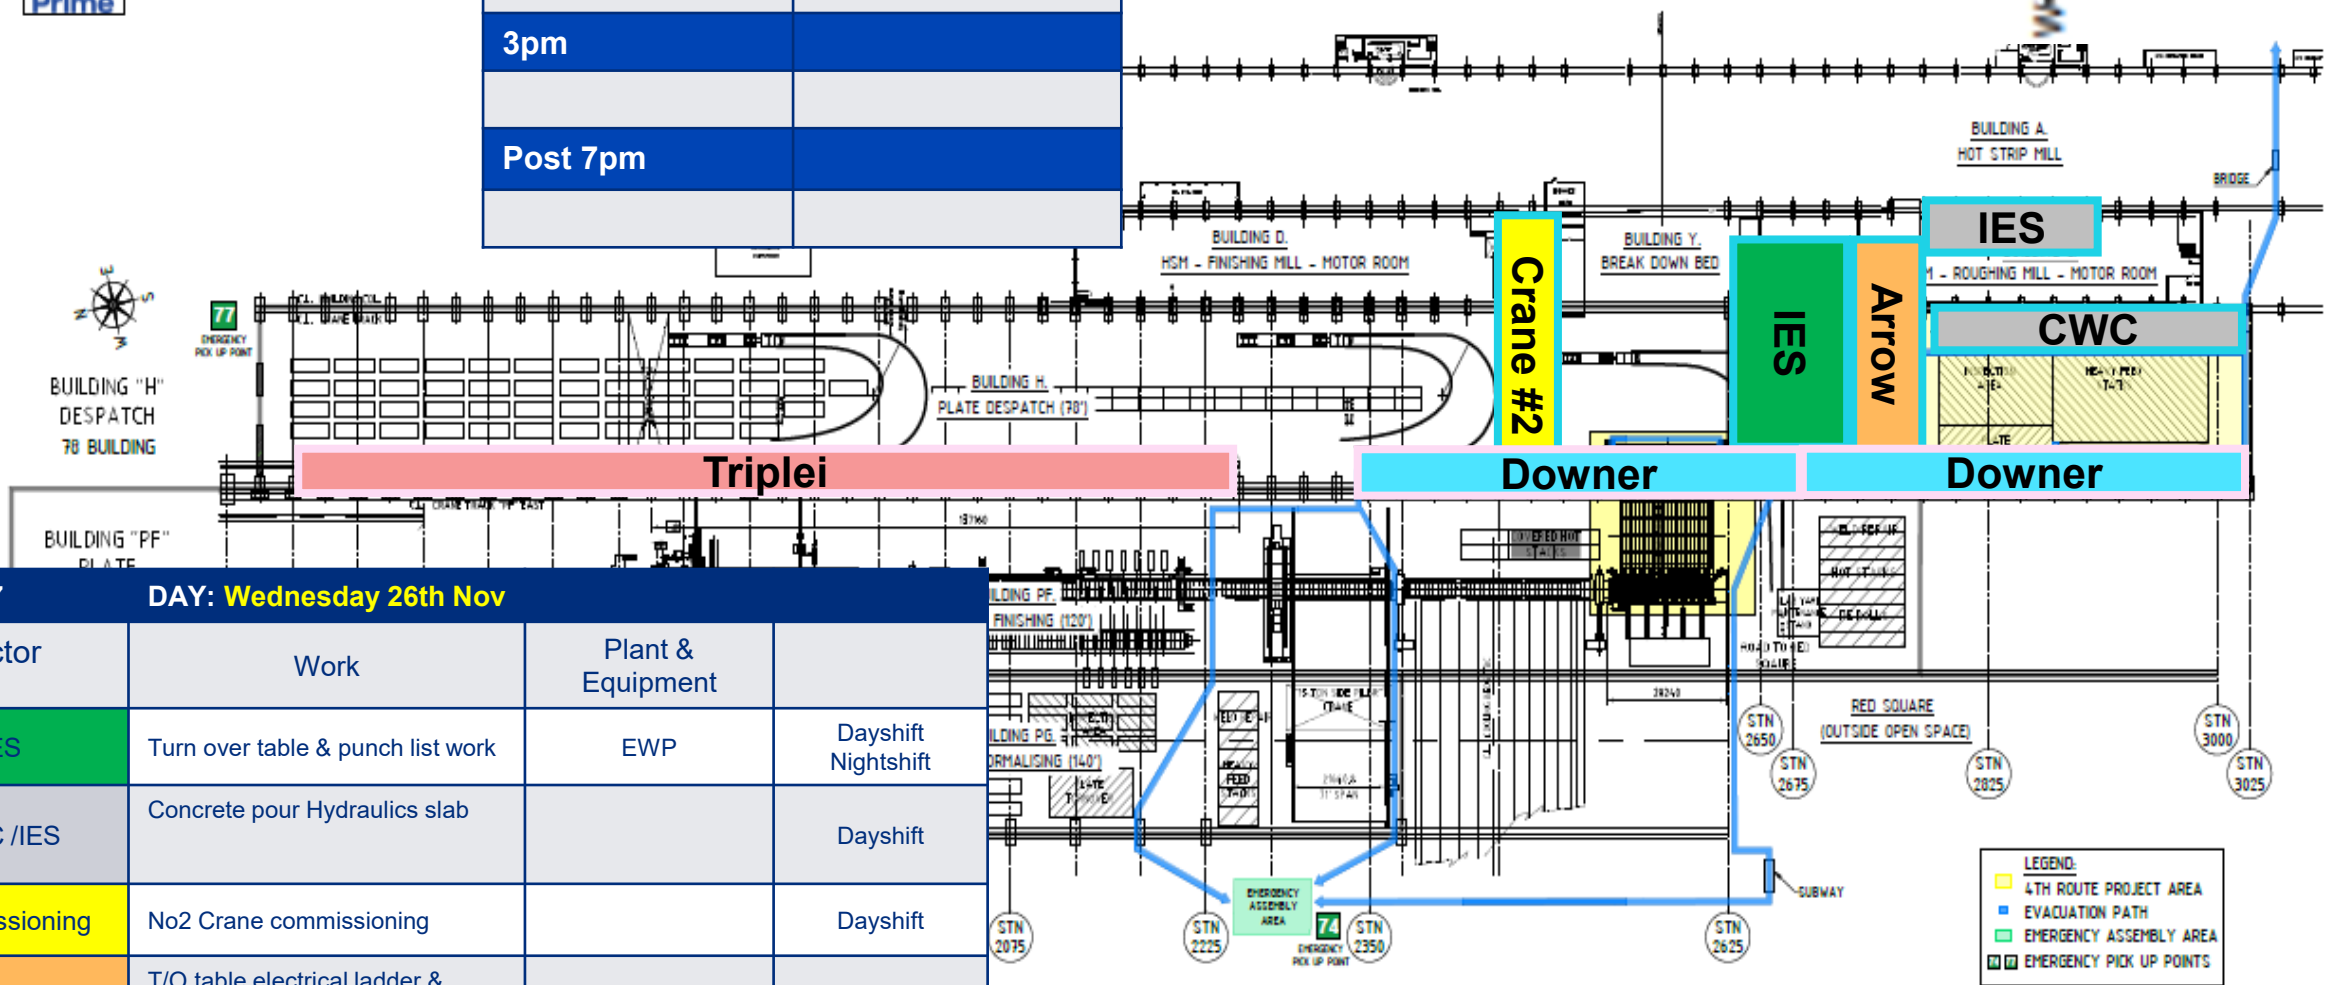


Week 47 DAY: Wednesday 26th Nov			
Contractor	Work	Plant & Equipment	
IES	Turn over table & punch list work	EWP	Dayshift Nightshift
CWC / IES	Concrete pour Hydraulics slab		Dayshift
Commissioning	No2 Crane commissioning		Dayshift
Arrow	T/O table electrical ladder & cable installation		Dayshift
Triple i	Northern rail Isolator terminations Northern rail testing Installing feeder cables into P72	1 x EWP	Nights
Downer	Emergency lighting installation	2 x EWP	Dayshift Nightshift



Daily Access	
11am	
3pm	
Post 7pm	

# UPCOMING WORK THIS WEEK

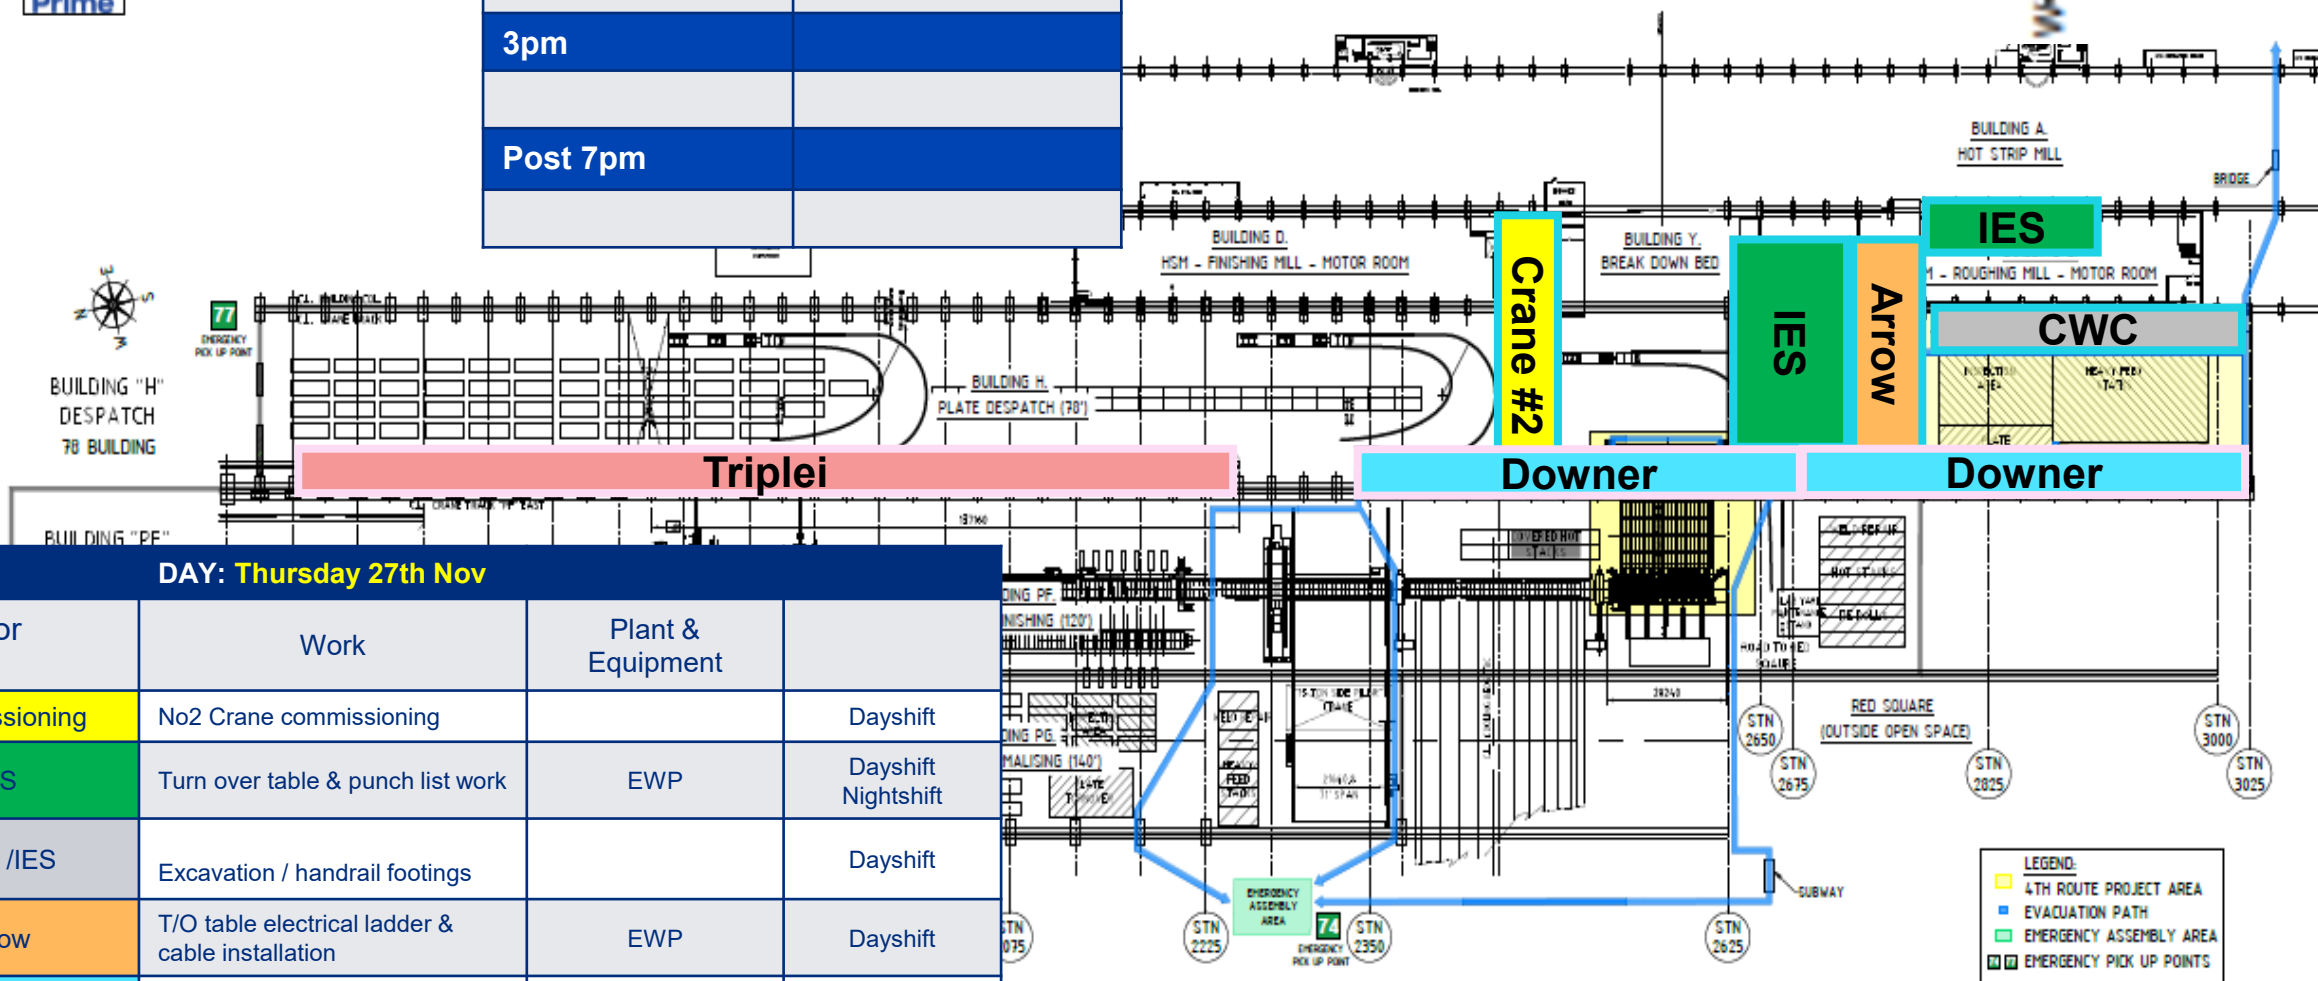


Week 47 DAY: Thursday 27th Nov

Contractor	Work	Plant & Equipment	
Commissioning	No2 Crane commissioning		Dayshift
IES	Turn over table & punch list work	EWP	Dayshift Nightshift
CWC /IES	Excavation / handrail footings		Dayshift
Arrow	T/O table electrical ladder & cable installation	EWP	Dayshift
Downer	Emergency lighting installation	2 x EWP	Dayshift Nightshift
Triple i	Northern rail Isolator terminations Northern rail testing Terminating feeder cables in P72	1 x EWP	Nights



Daily Access	
11am	
3pm	
Post 7pm	

# UPCOMING WORK THIS WEEK

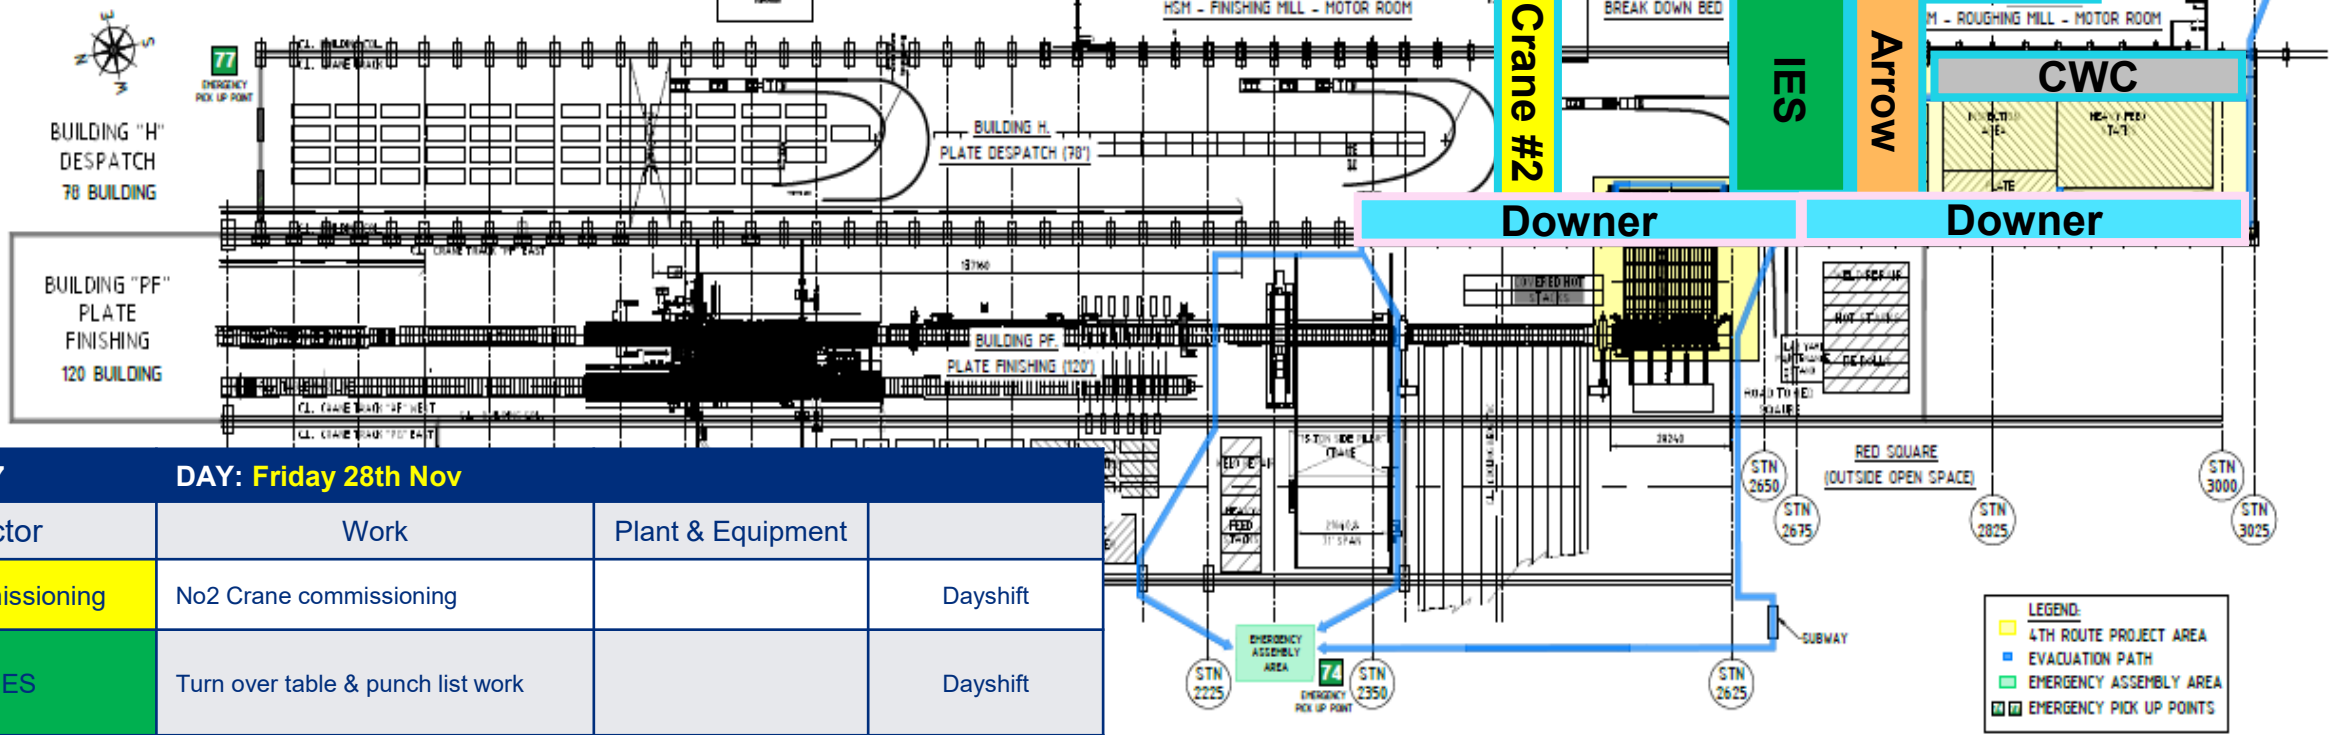

Week 47 DAY: Friday 28th Nov			
Contractor	Work	Plant & Equipment	
Commissioning	No2 Crane commissioning		Dayshift
IES	Turn over table & punch list work		Dayshift
IES / CWC			
Arrow	T/O table electrical ladder & cable installation	EWP	Dayshift
Downer	Emergency lighting installation	2 x EWP	Dayshift




## Daily Access

11am

3pm

Post 7pm

## UPCOMING WORK THIS WEEK

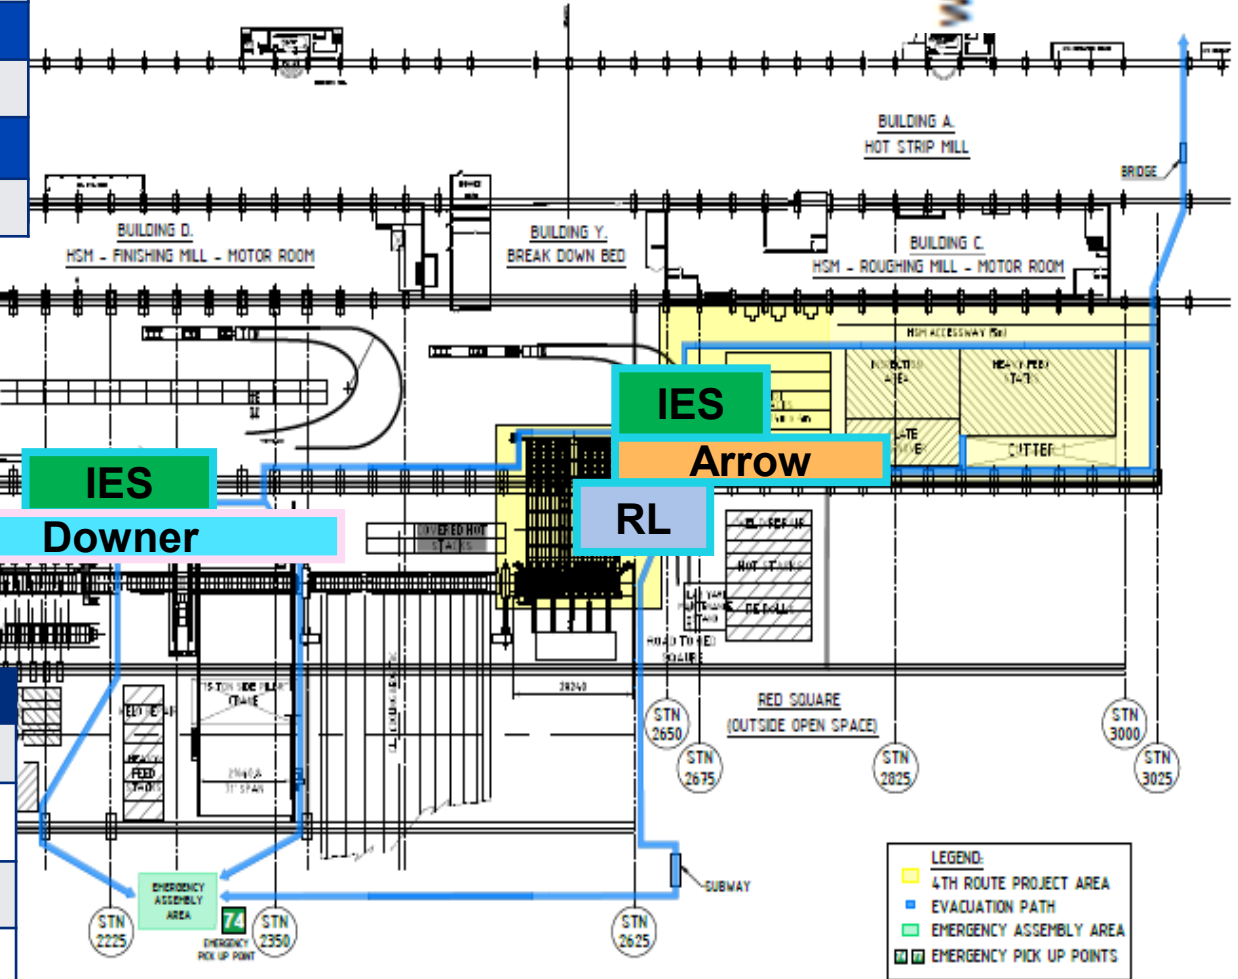


Week 47 DAY: Saturday 29th Nov			
Contractor	Work	Plant & Equipment	
IES	Turn over table & punch list work		
Rob lemme	Fire services cut in		Dayshift
Arrow	T/O table electrical ladder & cable installation		Dayshift
DOWNER	120 building P72 emergency lighting	EWP	Dayshift



Daily Access	
11am	
3pm	
Post 7pm	

# UPCOMING WORK THIS WEEK

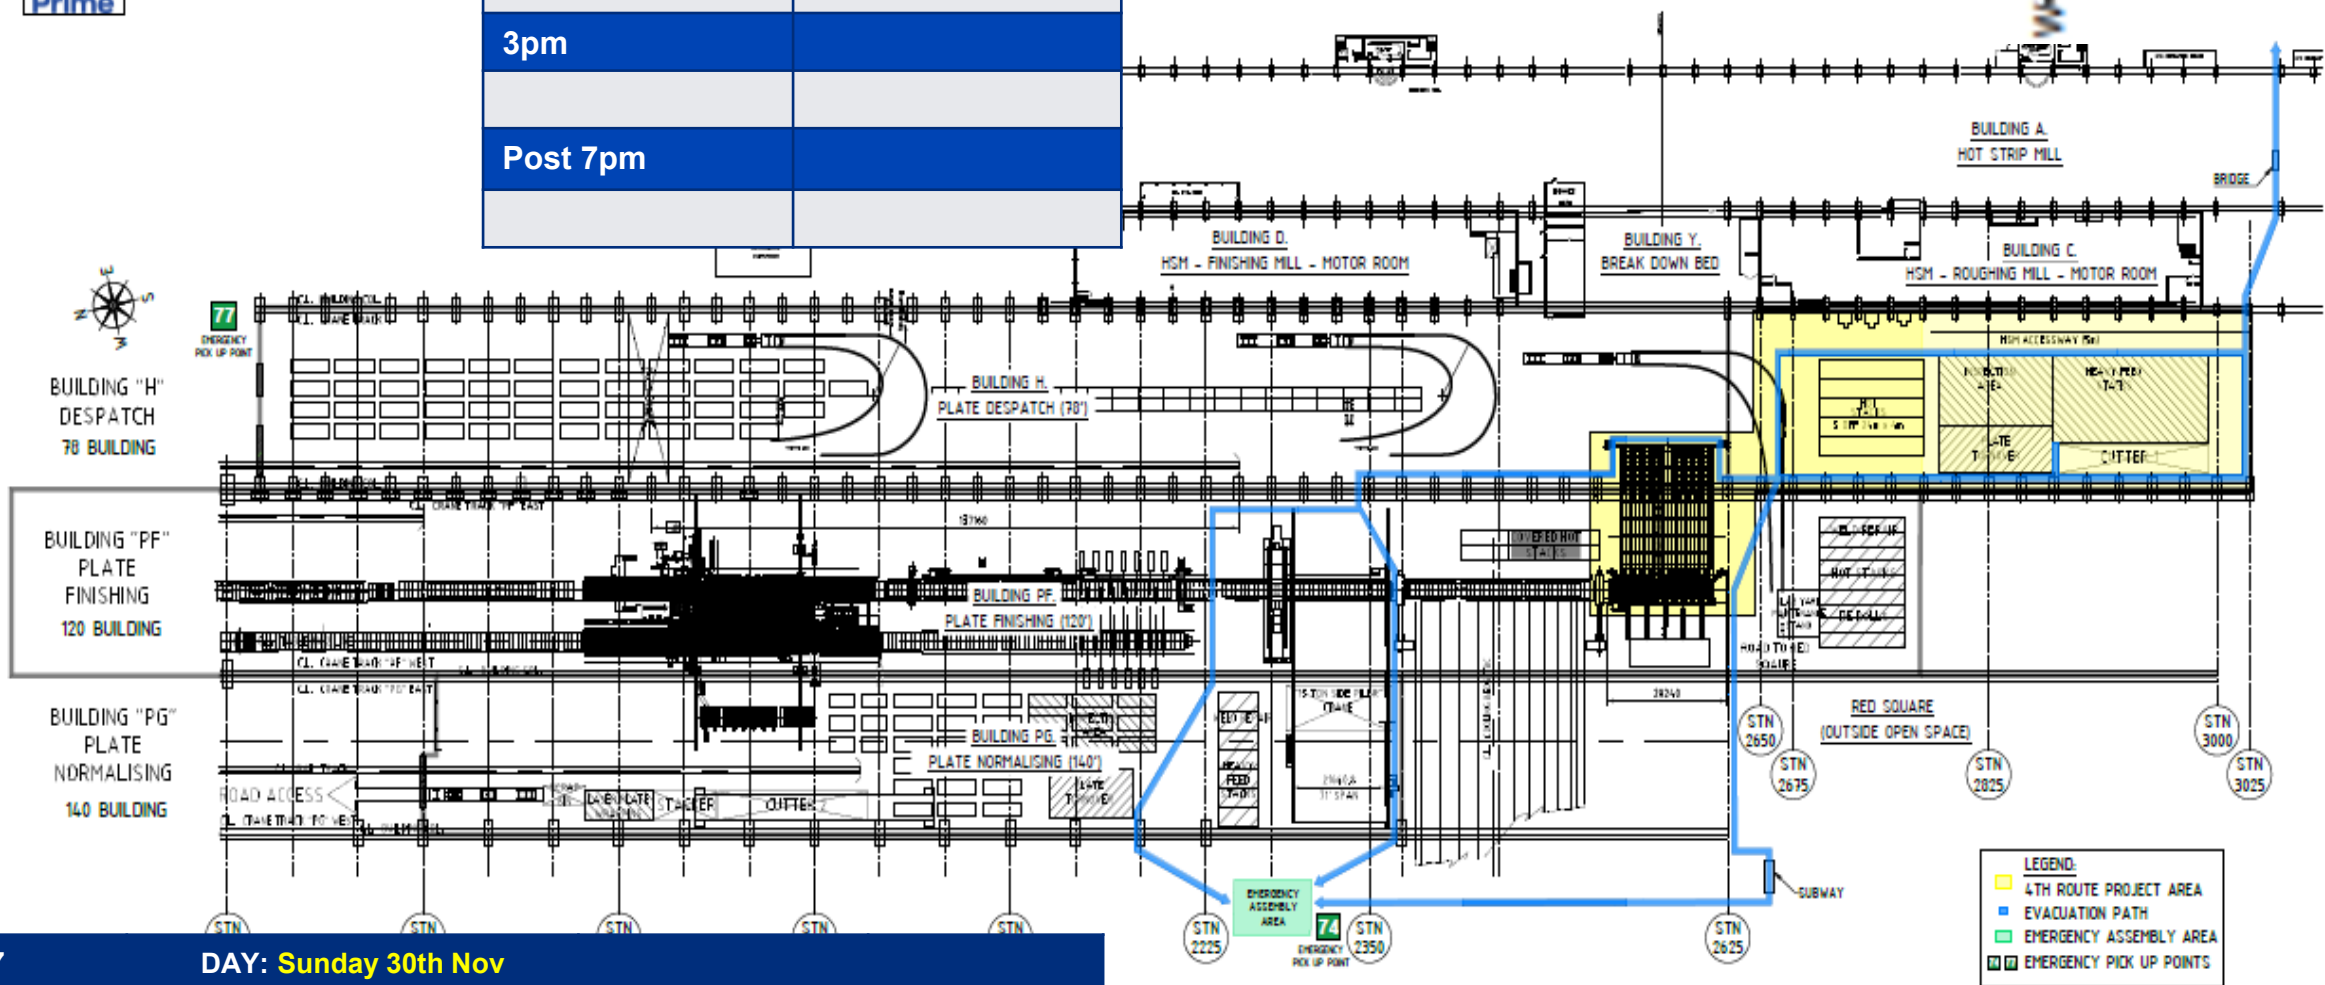

Week 47 DAY: Sunday 30th Nov			
Contractor	Work	Plant & Equipment	
IES			
Rob Lehme			





Daily Access	
11am	
3pm	
Post 7pm	

# UPCOMING WORK THIS WEEK



BUILDING "H"  
DESPATCH  
78 BUILDING




Triplei

BUILDING H  
PLATE DESPATCH (78)

Crane #2

BUILDING Y  
BREAK DOWN BED



BUILDING A  
HOT STRIP MILL

BUILDING C  
HSM - ROUGHING MILL - MOTOR ROOM

BUILDING D  
HSM - FINISHING MILL - MOTOR ROOM

RED SQUARE  
(OUTSIDE OPEN SPACE)

## Week 48 DAY: Monday 1st Dec


Contractor	Work	Plant & Equipment	
Commissioning	Commissioning / training		Dayshift
IES	Turn over table & punch list work		Dayshift
IES / CWC			
Arrow	T/O table electrical ladder, cable installation & cutter punch list		Dayshift
Downer	Emergency lighting installation	2 x EWP	Nightshift
Triplei	Northern rail Isolator terminations	1 x EWP	nightshift
ARA	Turnover table MCC install	Franna	dayshift



## UPCOMING WORK THIS WEEK



Daily Access	
11am	
3pm	
Post 7pm	

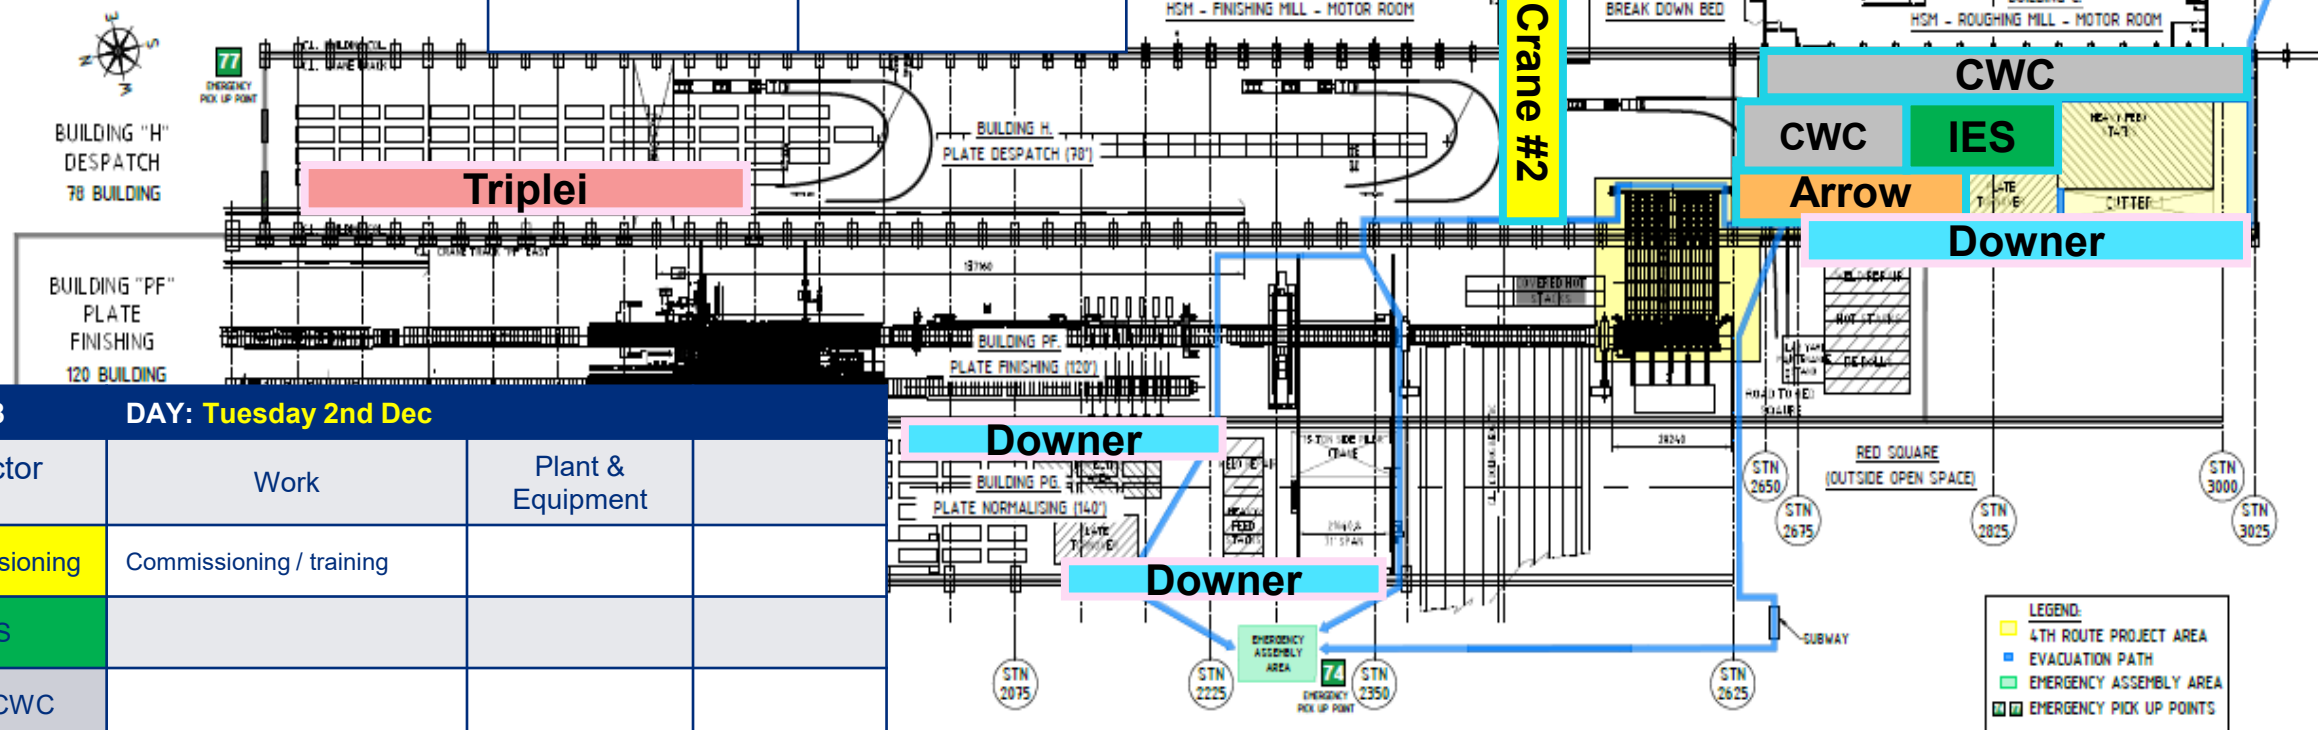


Week 48 DAY: Tuesday 2nd Dec			
Contractor	Work	Plant & Equipment	
Commissioning	Commissioning / training		
IES			
IES / CWC			
Arrow	T/O table electrical ladder, cable installation & cutter punch list	EWP	Dayshift
Downer	Emergency lighting installation	2 x EWP	Dayshift nightshift



Daily Access	
11am	
3pm	
Post 7pm	

UPCOMING WORK THIS WEEK

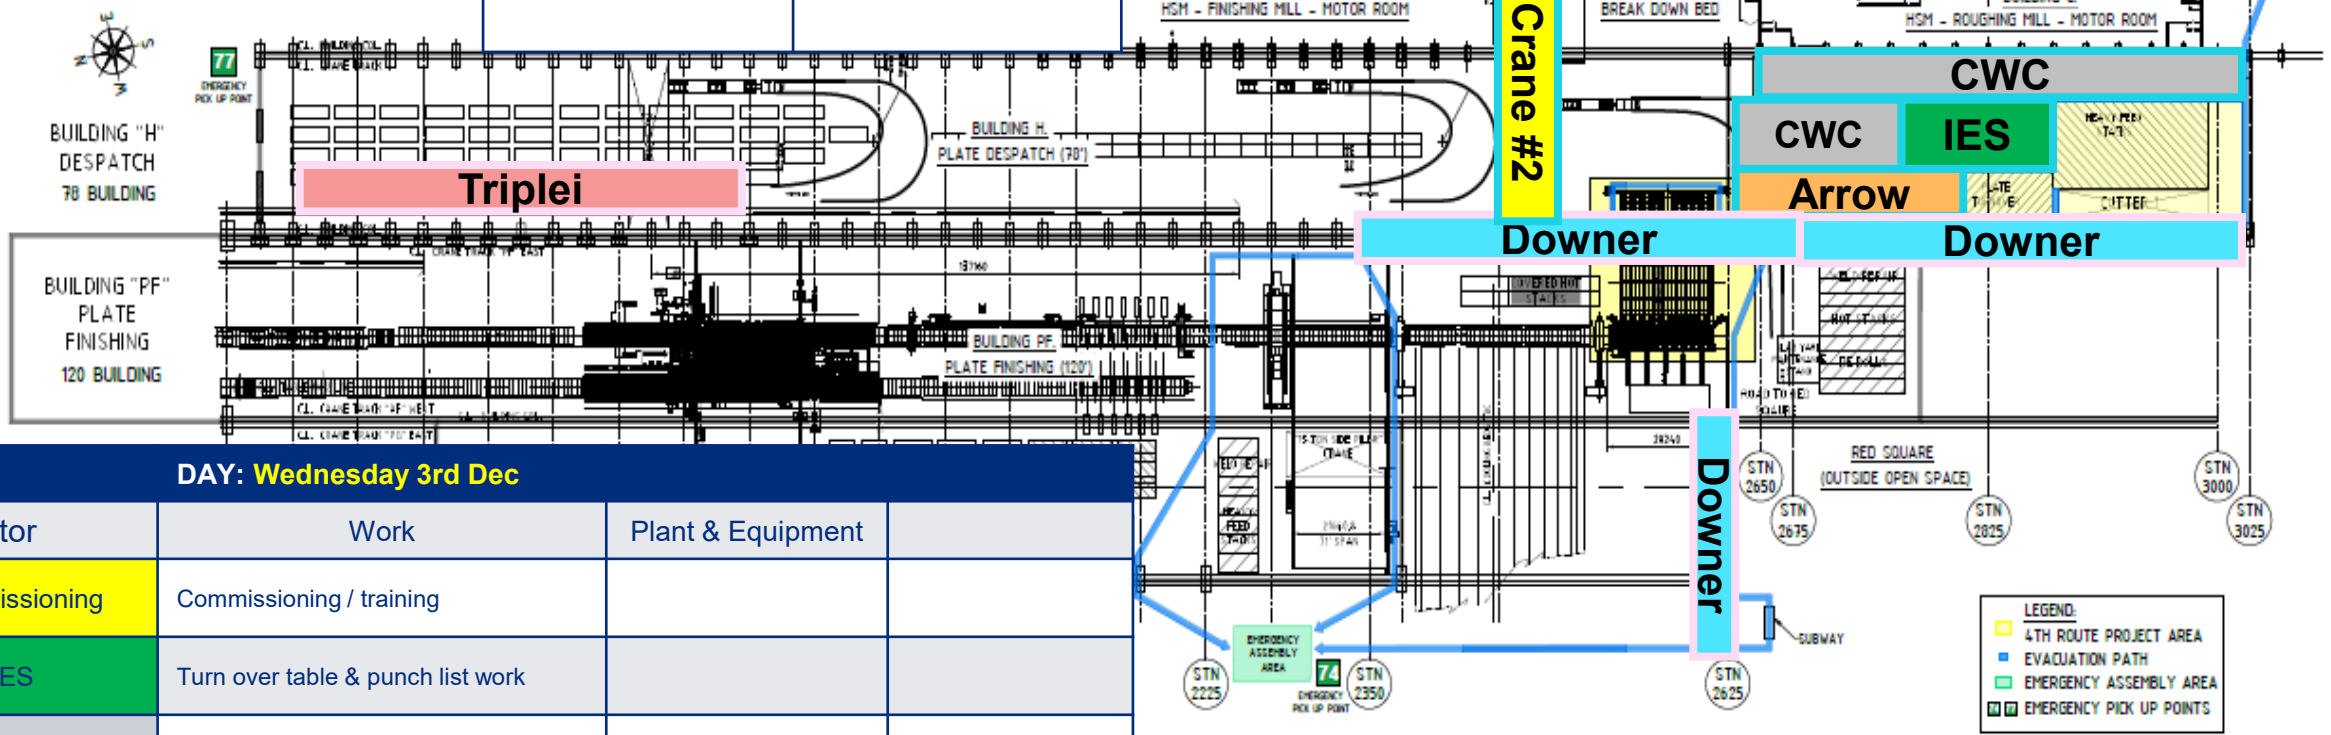

Week 48 DAY: Wednesday 3rd Dec			
Contractor	Work	Plant & Equipment	
Commissioning	Commissioning / training		
IES	Turn over table & punch list work		
IES / CWC			
Arrow	T/O table electrical ladder, cable installation & cutter punch list	EWP	Dayshift
Downer	Emergency lighting installation	2 x EWP	Dayshift nightshift
