



Daily Access	
11am	
3pm	
Post 7pm	

UPCOMING WORK THIS WEEK



BUILDING "H"
DESPATCH
78 BUILDING



EMERGENCY
PICK UP POINT

Rail extension

Crane #2

CWC

FREDON

Crane 7

ARA

Crane #3

RED SQUARE
(OUTSIDE OPEN SPACE)

STN 2625

STN 3000

STN 3025

STN 2625

STN 2025

STN 2350

EMERGENCY
PICK UP POINT

EMERGENCY
PICK UP POINT

LEGEND:	
	4TH ROUTE PROJECT AREA
—	EVACUATION PATH
	EMERGENCY ASSEMBLY AREA
	EMERGENCY PICK UP POINTS


Week 41 DAY: Wednesday 15th Oct

Contractor	Work	Plant & Equipment	
IES/JCS	Rope work		
FREDON	Cutter Electrical commissioning		Days
Fredon	Crane #3 cabin mods	In crane	
CWC	Finalising pour on Turnover Table	Excavator	Days and Nights
ARA	Punchlist items		
Ventia/Coastwide	Rail extension		



Daily Access	
Concrete Trucks	
11am	
3pm	
Post 7pm	

UPCOMING WORK THIS WEEK

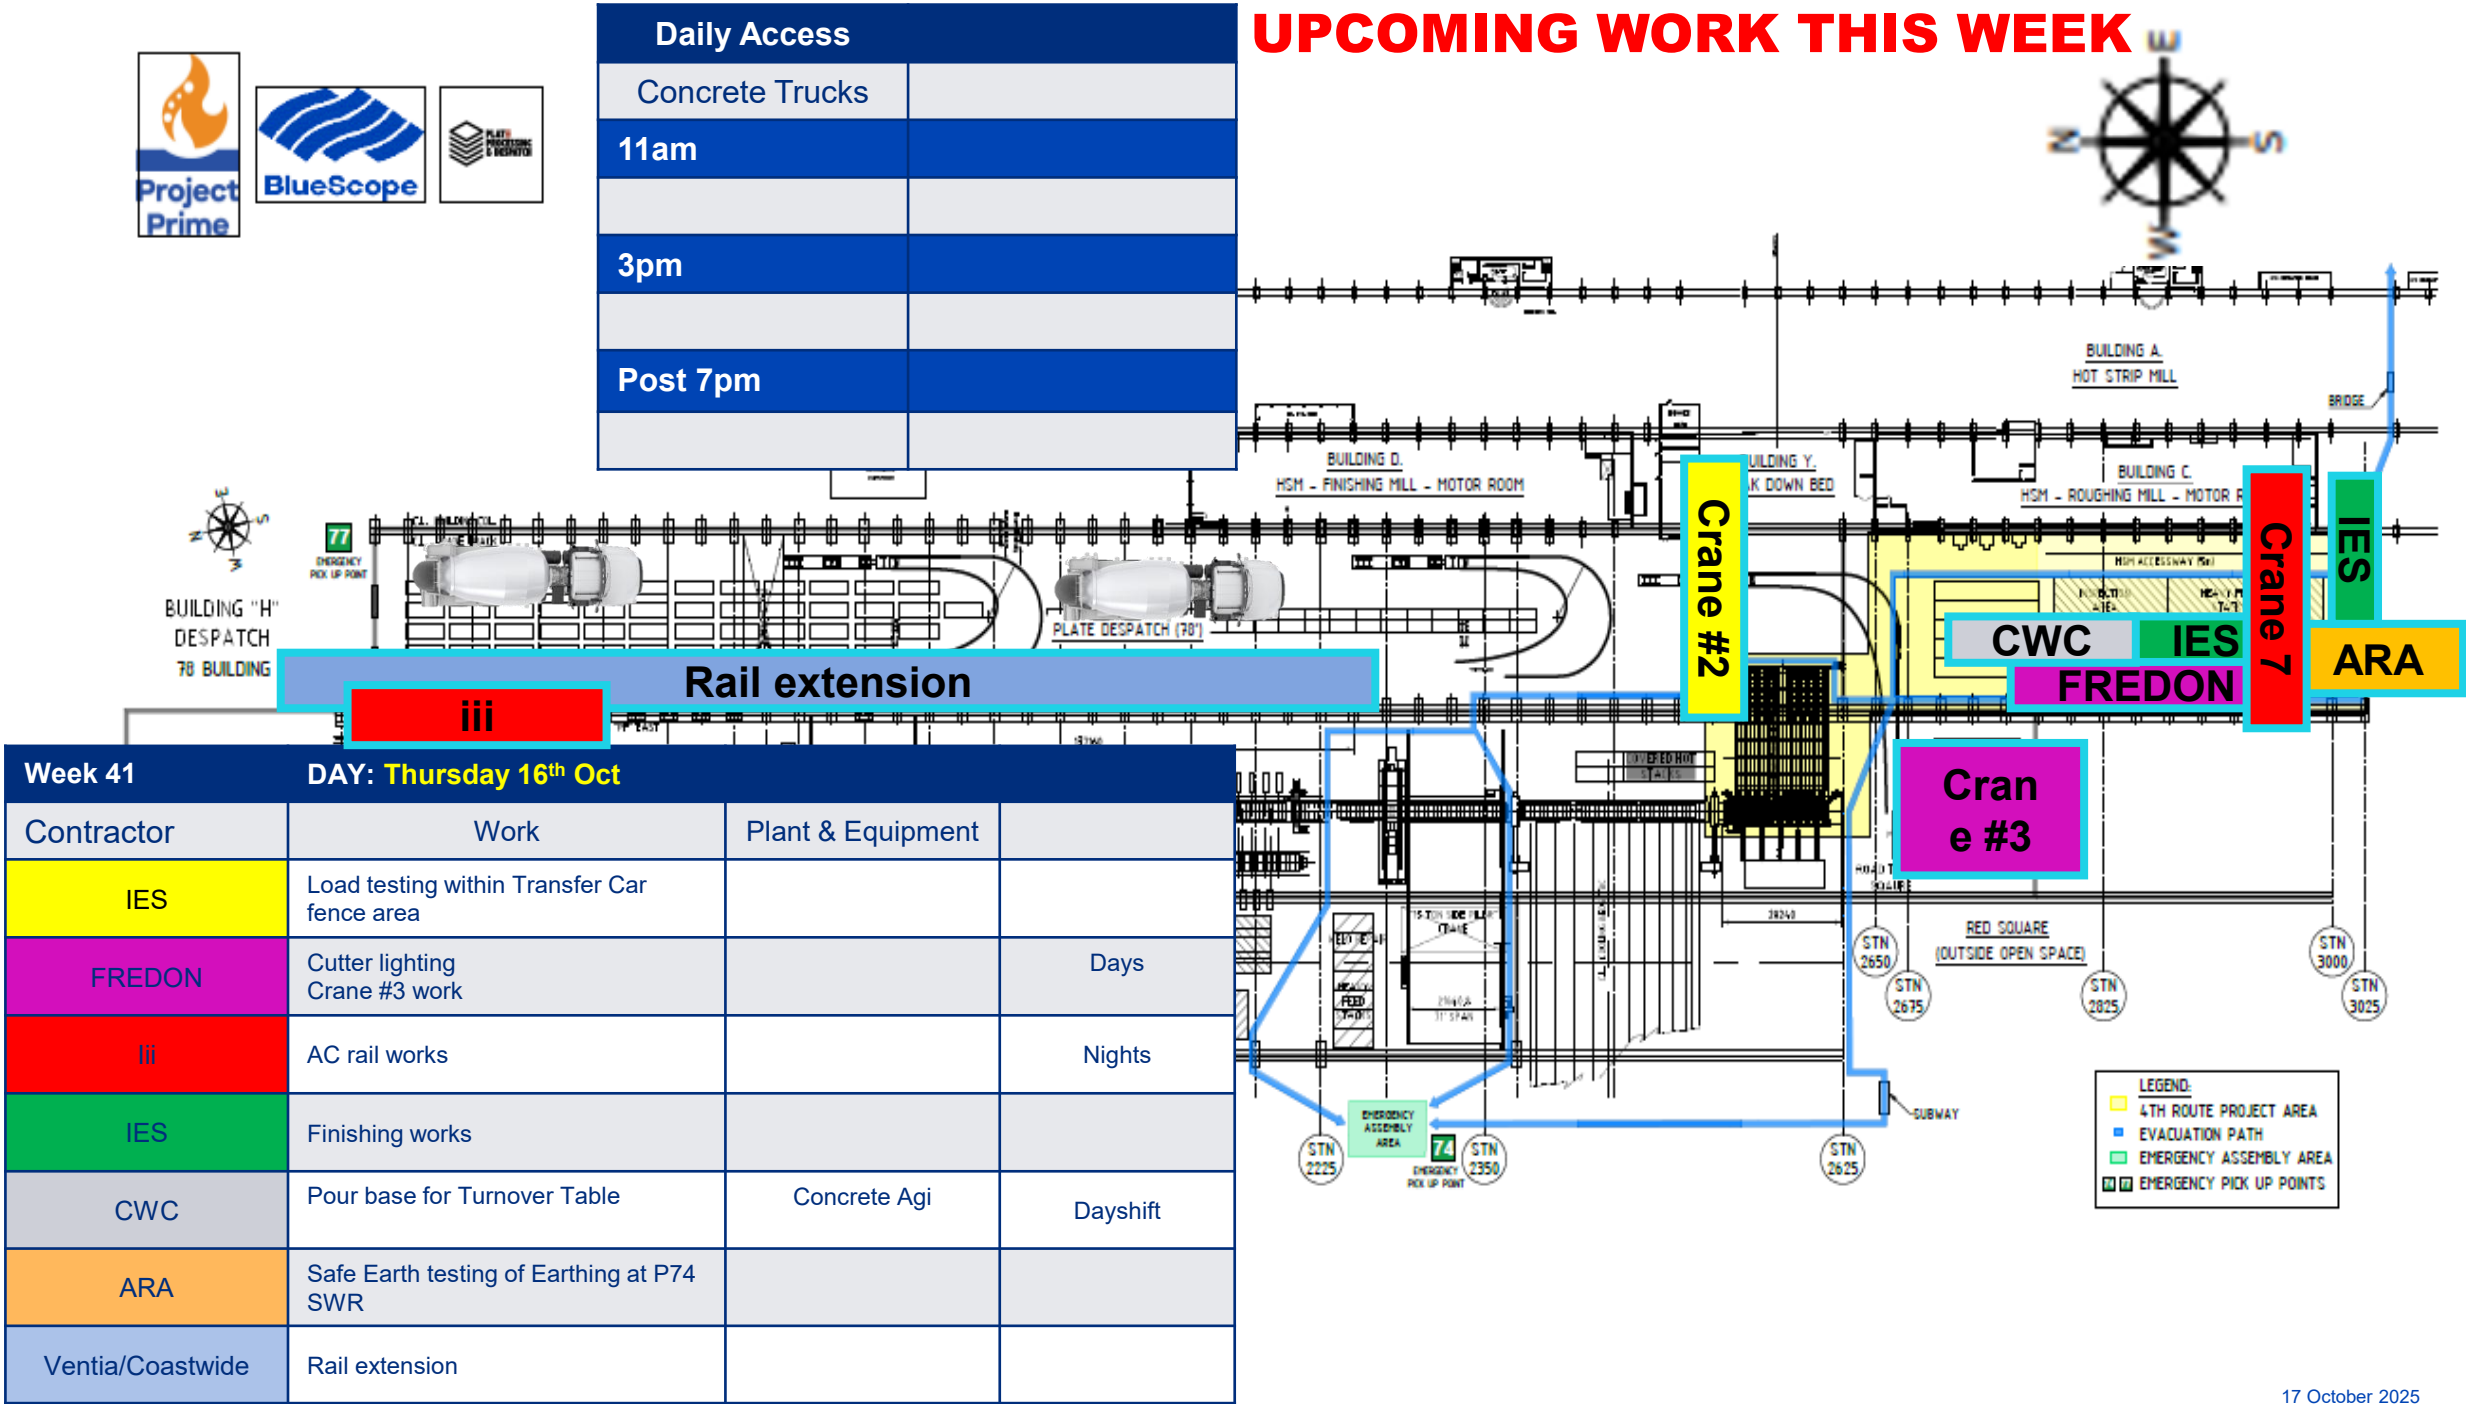


Week 41 DAY: Thursday 16 th Oct			
Contractor	Work	Plant & Equipment	
IES	Load testing within Transfer Car fence area		
FREDON	Cutter lighting Crane #3 work		Days
iii	AC rail works		Nights
IES	Finishing works		
CWC	Pour base for Turnover Table	Concrete Agi	Dayshift
ARA	Safe Earth testing of Earthing at P74 SWR		
Ventia/Coastwide	Rail extension		



Daily Access	
11am	
HSM come in	
3pm	
Post 7pm	

UPCOMING WORK THIS WEEK

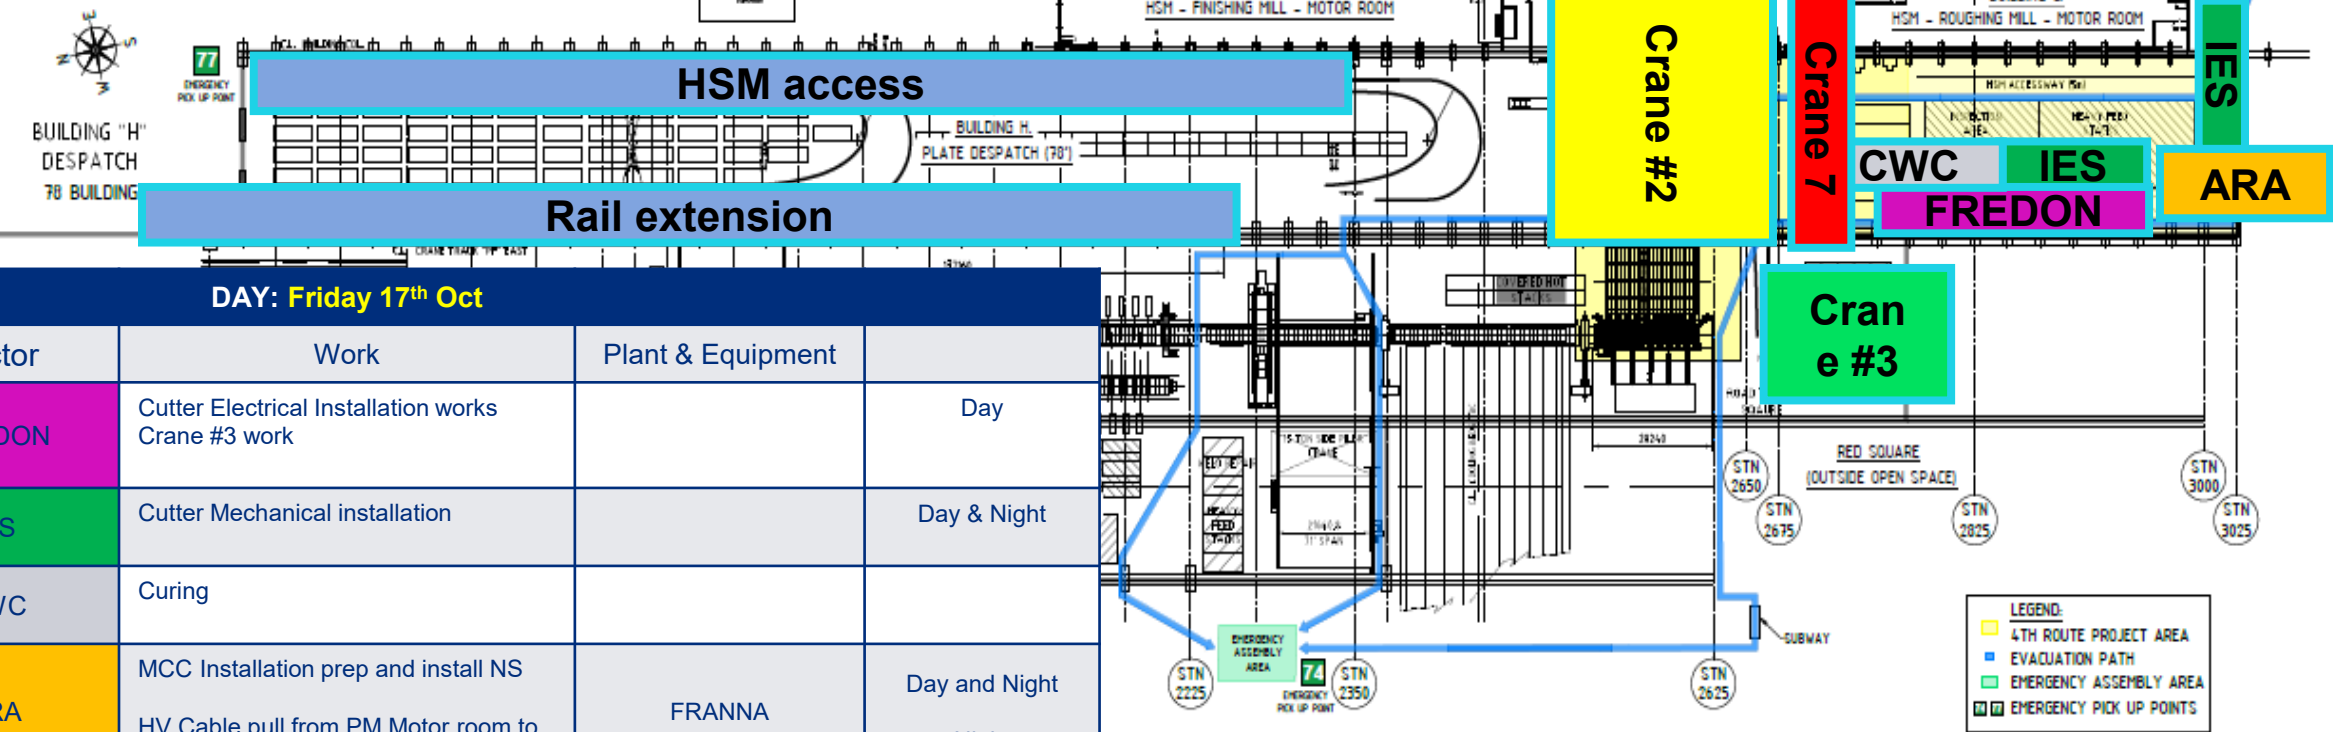


Week 41 DAY: Friday 17 th Oct			
Contractor	Work	Plant & Equipment	
FREDON	Cutter Electrical Installation works Crane #3 work		Day
IES	Cutter Mechanical installation		Day & Night
CWC	Curing		
ARA	MCC Installation prep and install NS	FRANNA	Day and Night
	HV Cable pull from PM Motor room to P74 SWR		Night
Ventia/Coastwide	Rail work		
Crane #2	Later in day expand area for load area at full speed – 80m clear		Day & Night



Daily Access	
11am	
3pm	
Post 7pm	

UPCOMING WORK THIS WEEK

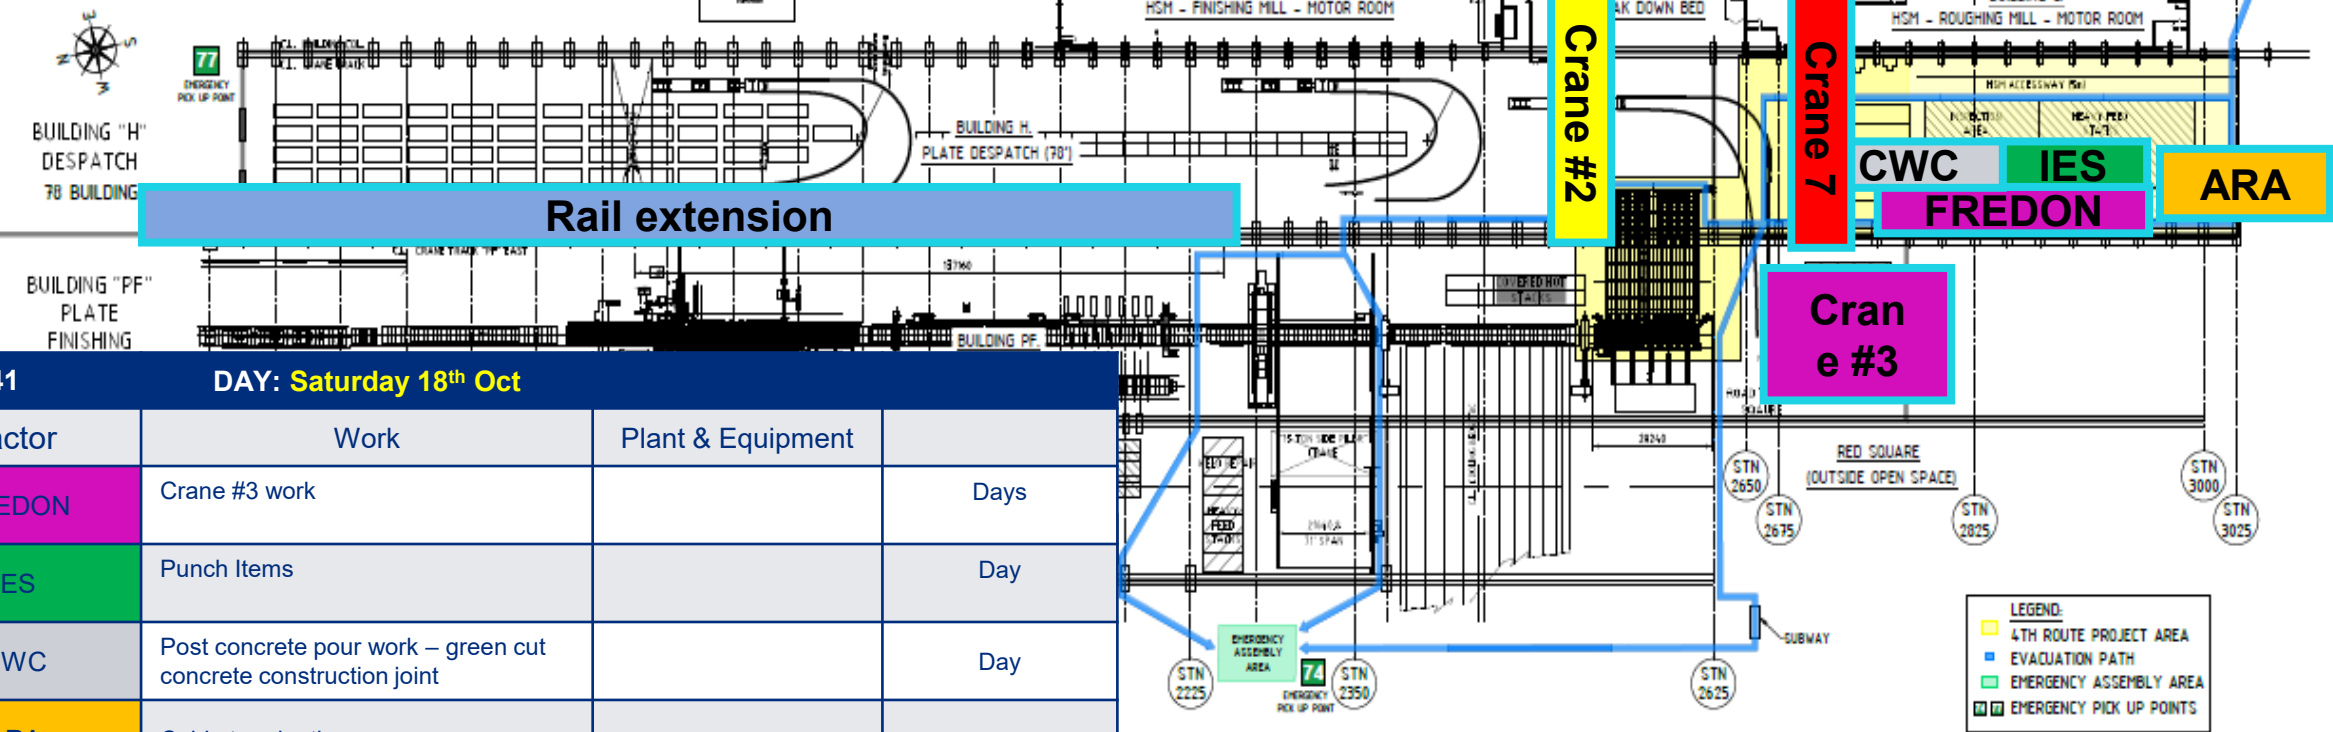


Week 41 DAY: Saturday 18 th Oct			
Contractor	Work	Plant & Equipment	
FREDON	Crane #3 work		Days
IES	Punch Items		Day
CWC	Post concrete pour work – green cut concrete construction joint		Day
ARA	Cable terminations		
Ventia/Coastwide	Asphalt - TBC		
Crane #2	Punch Items		



Daily Access	
11am	
3pm	
Post 7pm	

UPCOMING WORK THIS WEEK

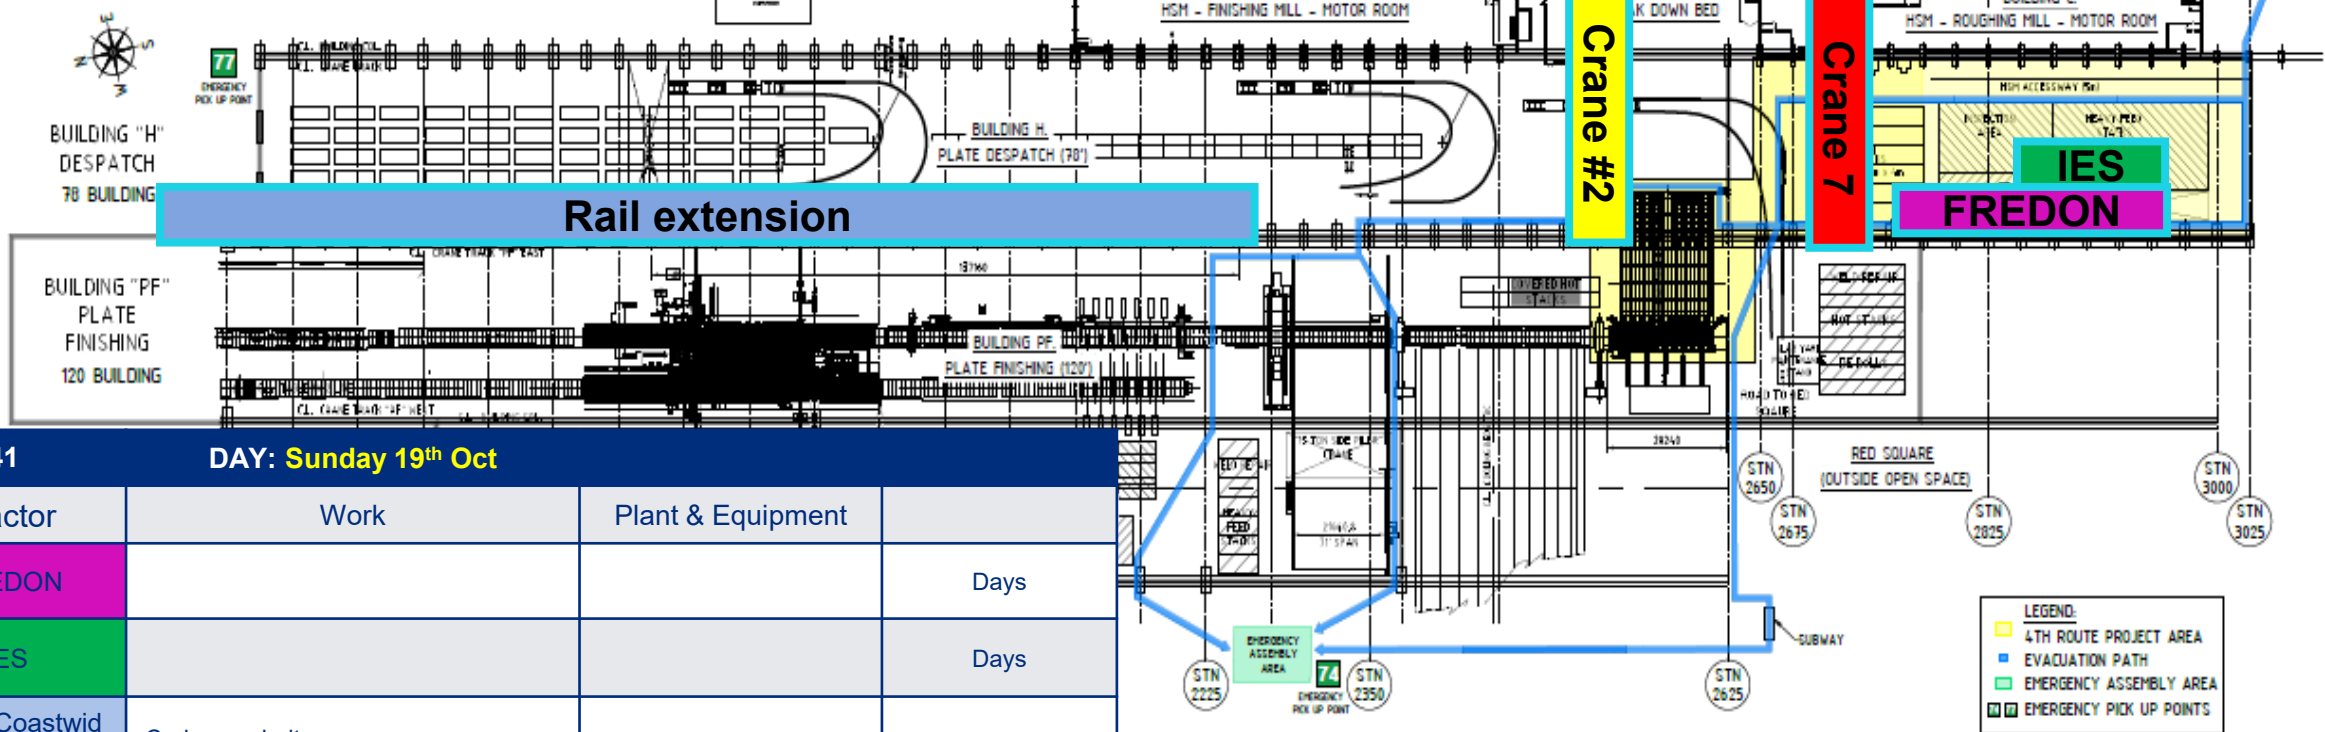


Week 41 DAY: Sunday 19 th Oct			
Contractor	Work	Plant & Equipment	
FREDON			Days
IES			Days
Ventia/Coastwide	Curing asphalt		



Daily Access	
11am	
3pm	
Post 7pm	

UPCOMING WORK THIS WEEK

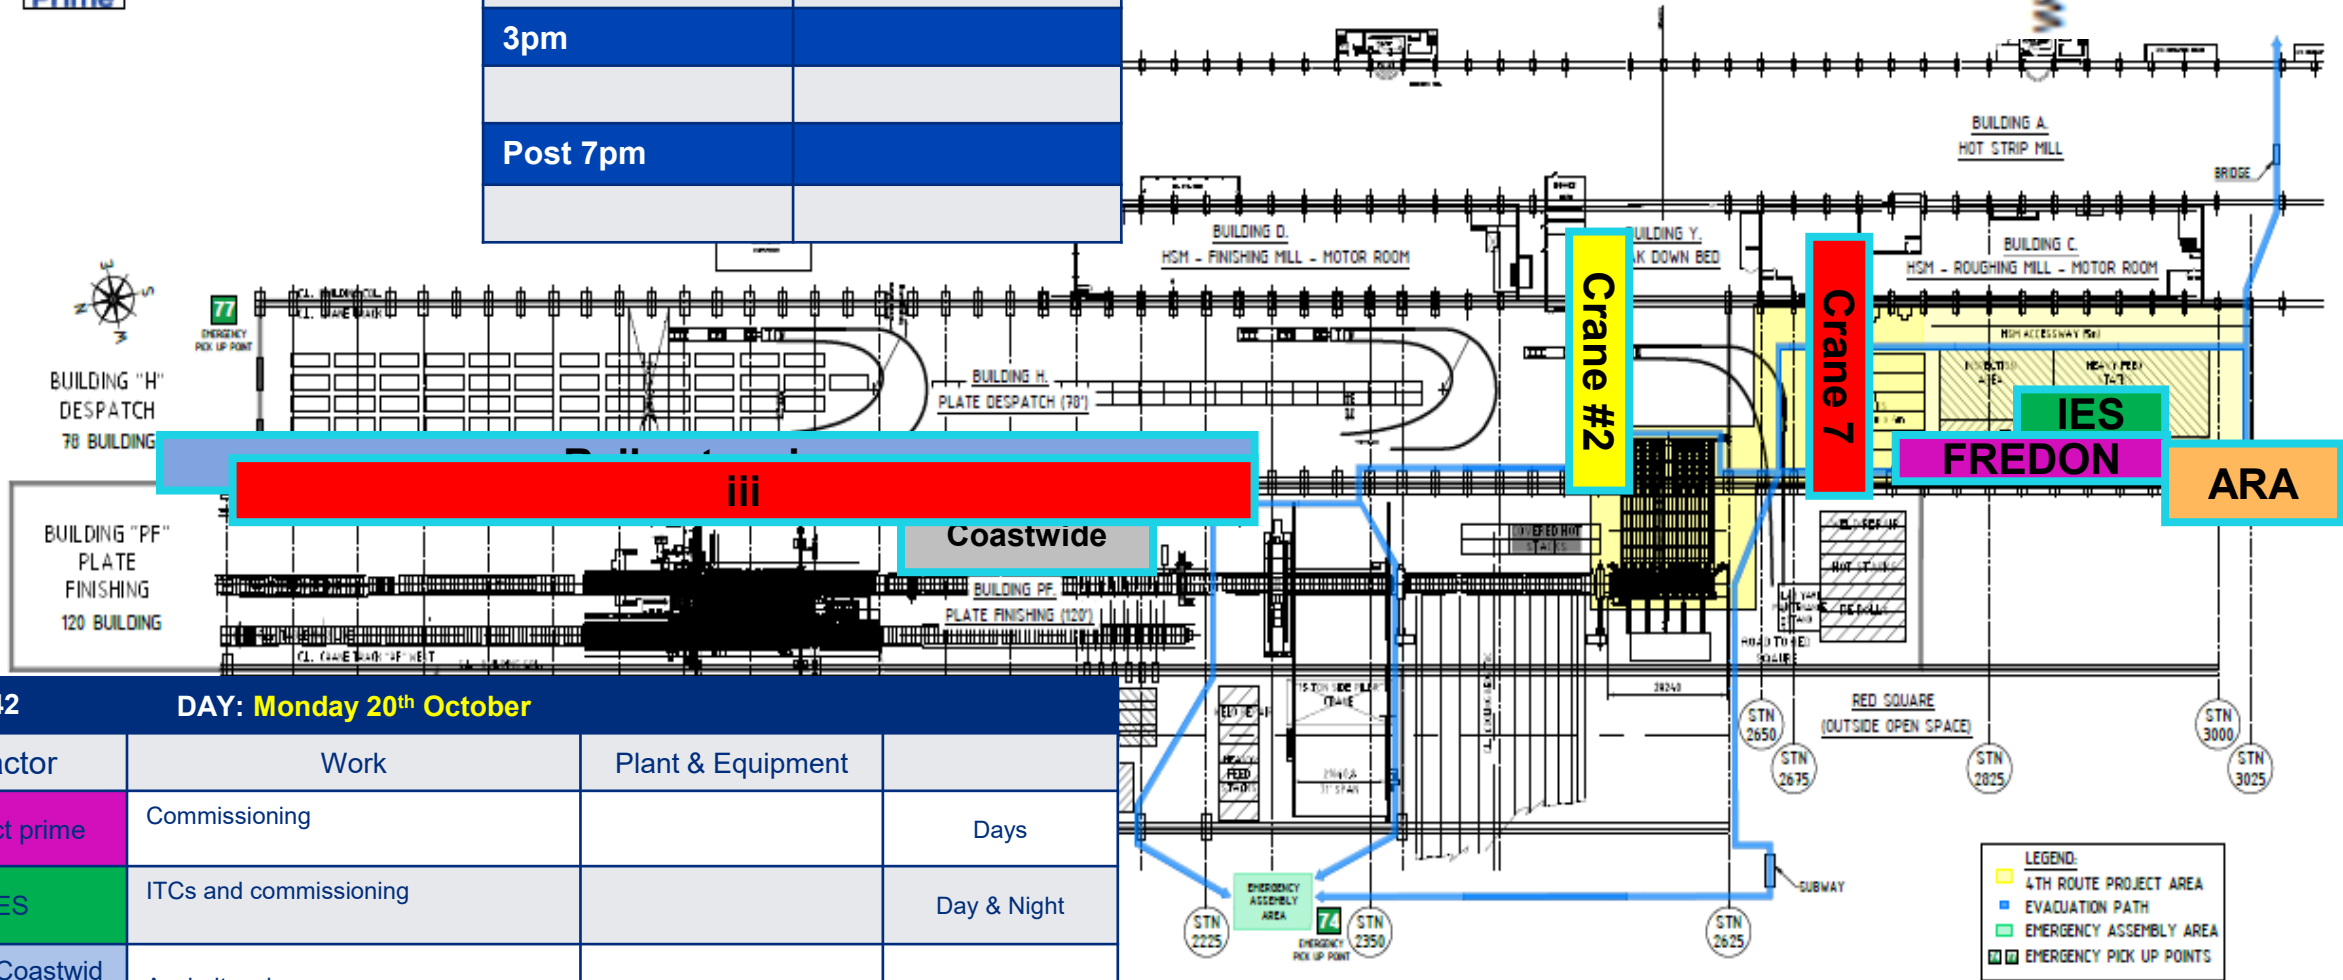

Week 42 DAY: Monday 20 th October			
Contractor	Work	Plant & Equipment	
Project prime	Commissioning		Days
IES	ITCs and commissioning		Day & Night
Ventia/Coastwide	Asphalt curing		
ARA	Power up P74		
Coastwide	Western Protection for P72	Excavator	



Daily Access	
11am	
3pm	
Post 7pm	

UPCOMING WORK THIS WEEK



BUILDING "H"
DESPATCH
78 BUILDING


BUILDING "PF"
PLATE
FINISHING
120 BUILDING



EMERGENCY
PICK UP POINT



Coastwide

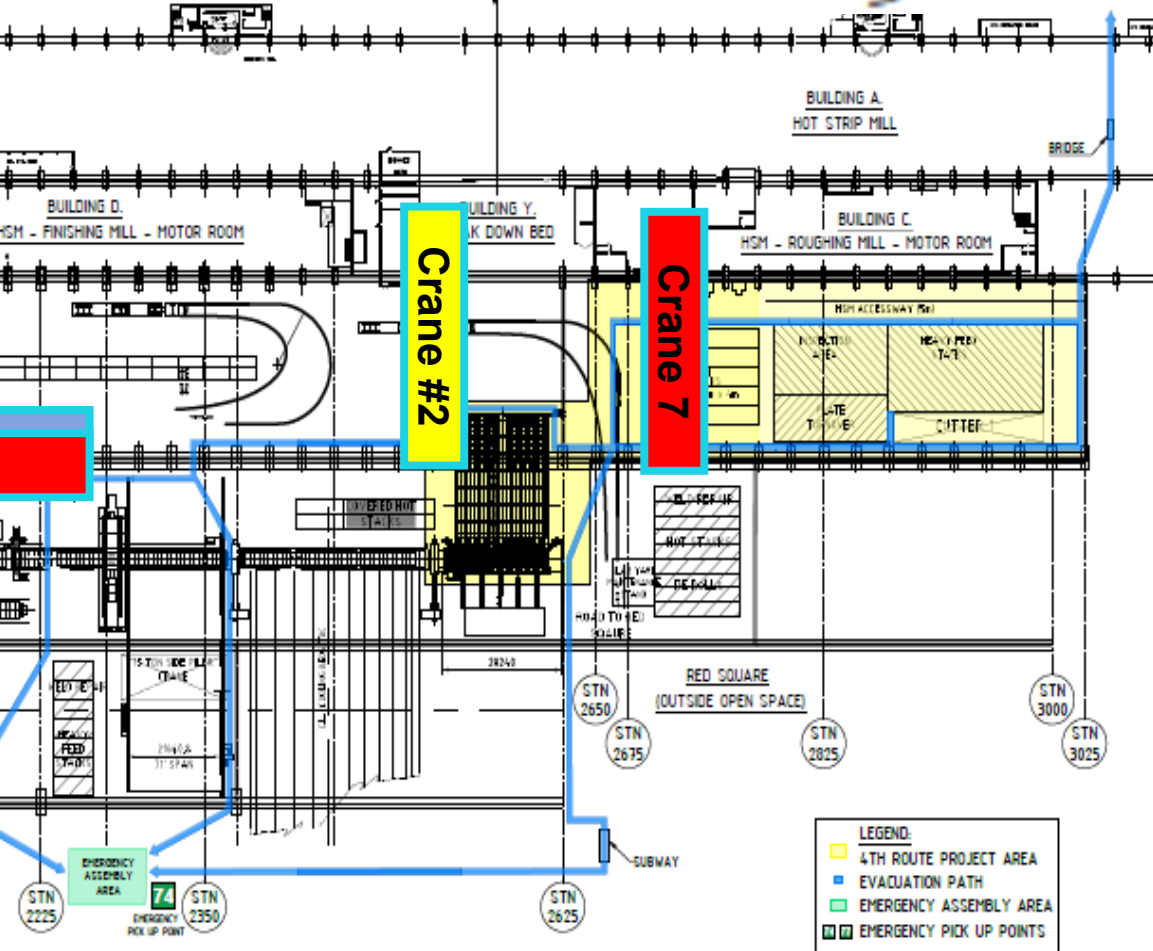

Week 42 DAY: Tuesday 21 st October			
Contractor	Work	Plant & Equipment	
Ventia/Coastwide	Rail extension		
