



October Shut Day 11 Day Shift

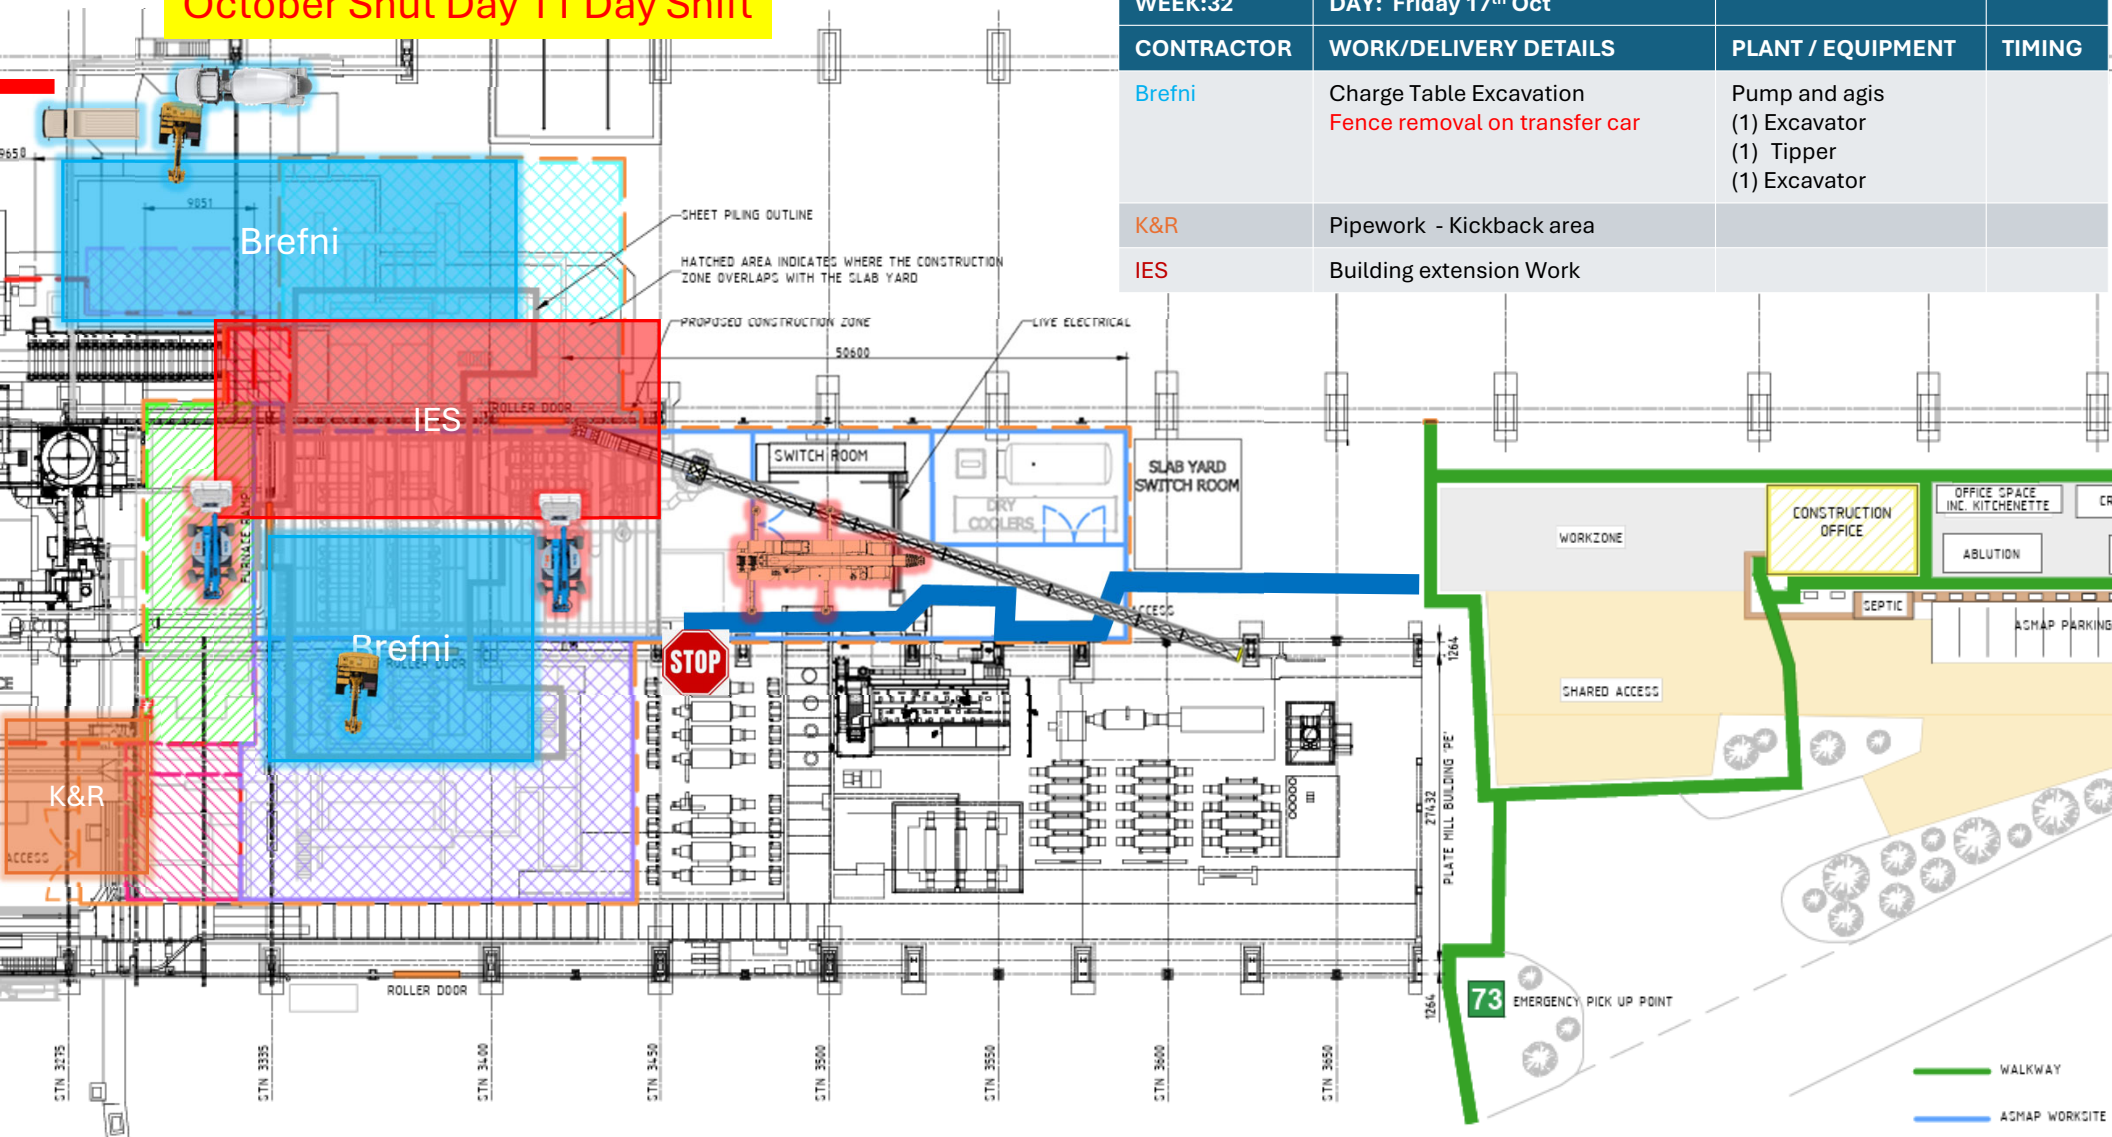


WEEK:32	DAY: Friday 17 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation Fence removal on transfer car	Pump and agis (1) Excavator (1) Tipper (1) Excavator	
K&R	Pipework - Kickback area		
IES	Building extension Work		

October Shut Day 11 Night Shift

WEEK:32	DAY: Friday 17 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation	(1) Excavator (1) Tipper (1) Excavator	
	Plate Mill Crane - Excavator - Prop removal		
IES	End Stop Install		

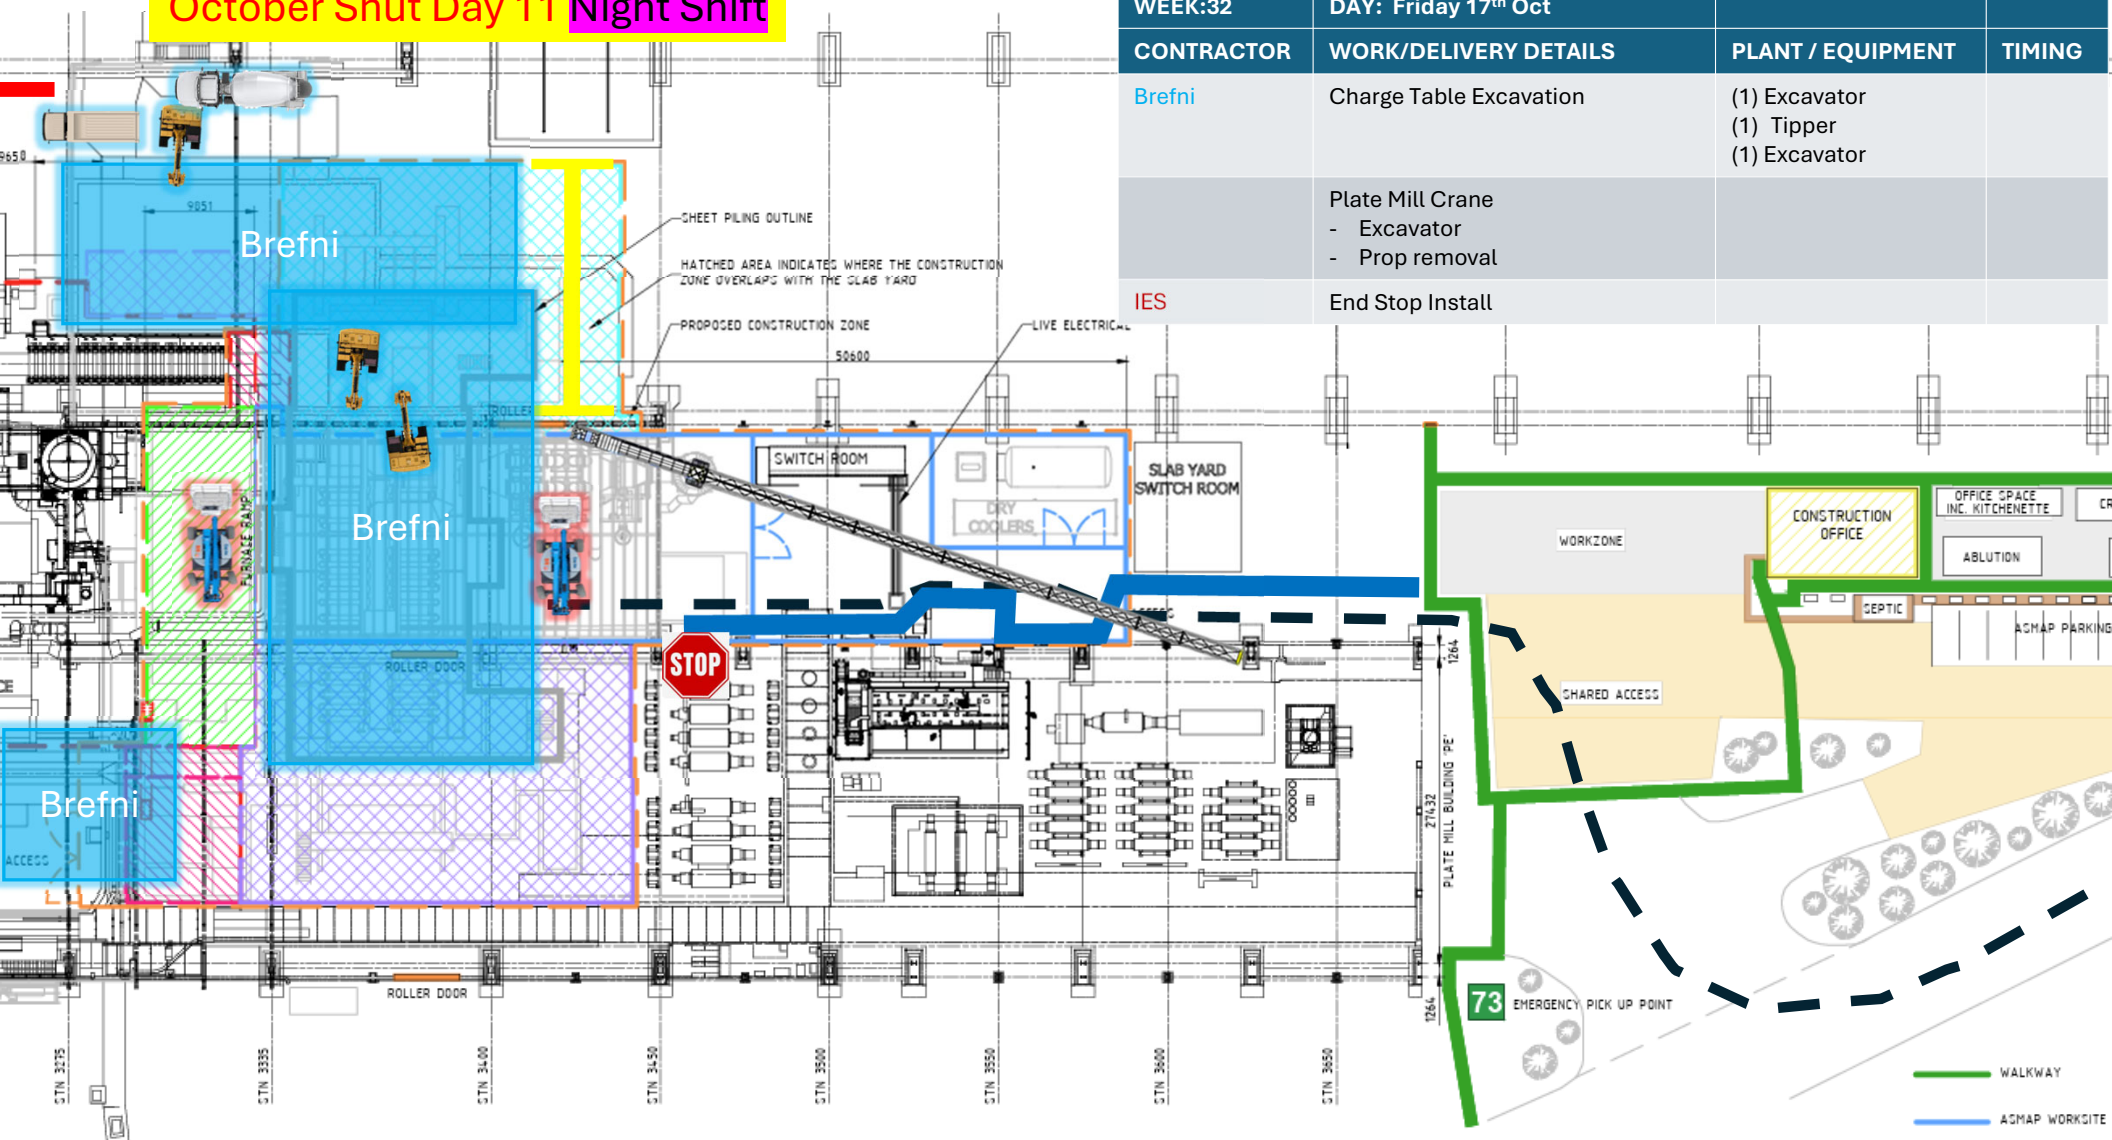


October Shut Day 12 Day Shift

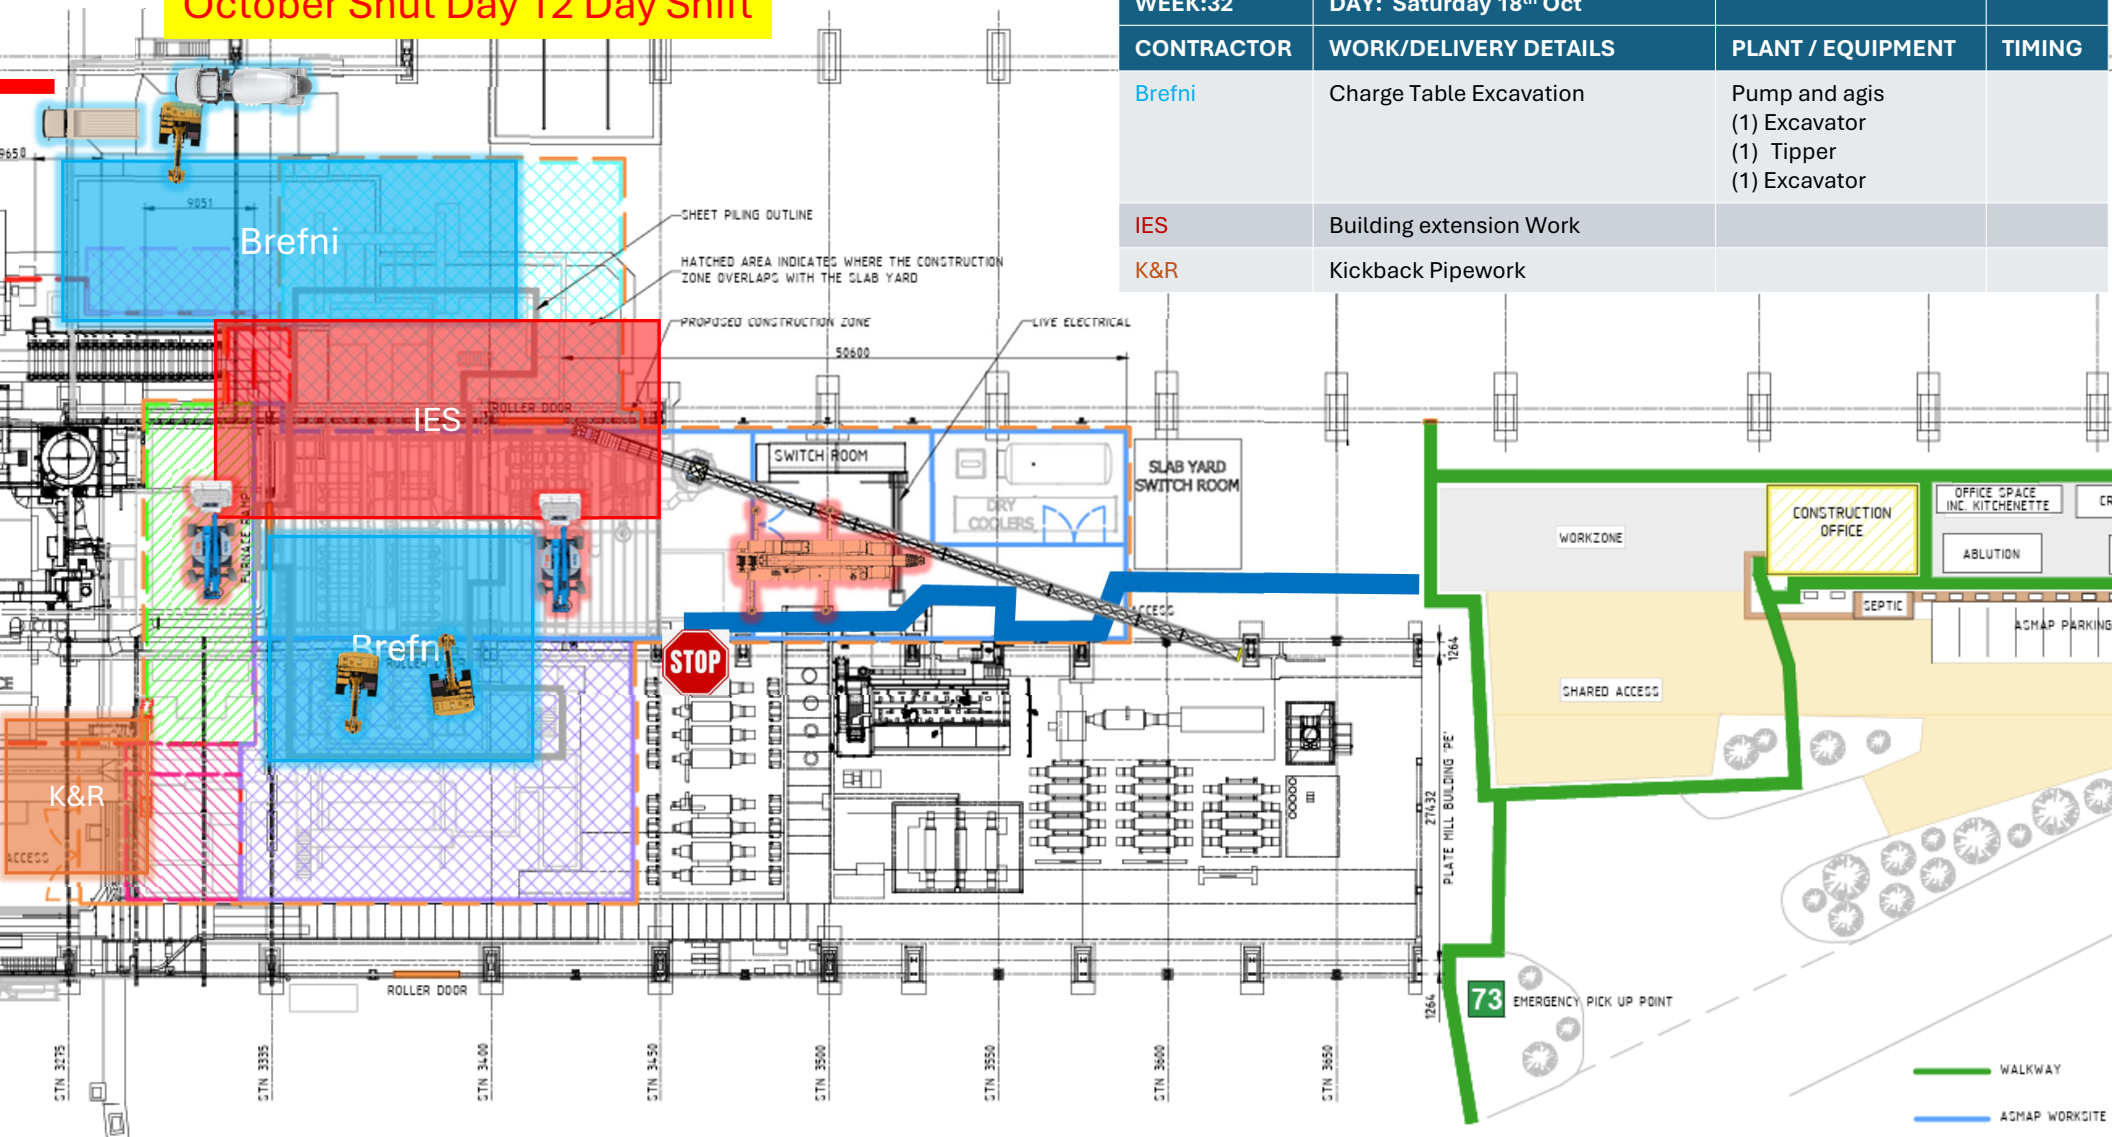


WEEK:32	DAY: Saturday 18 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation	Pump and agis (1) Excavator (1) Tipper (1) Excavator	
IES	Building extension Work		
K&R	Kickback Pipework		

October Shut Day 12 Night Shift

WEEK:32	DAY: Saturday 18 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation	(1) Excavator (1) Tipper (1) Excavator	

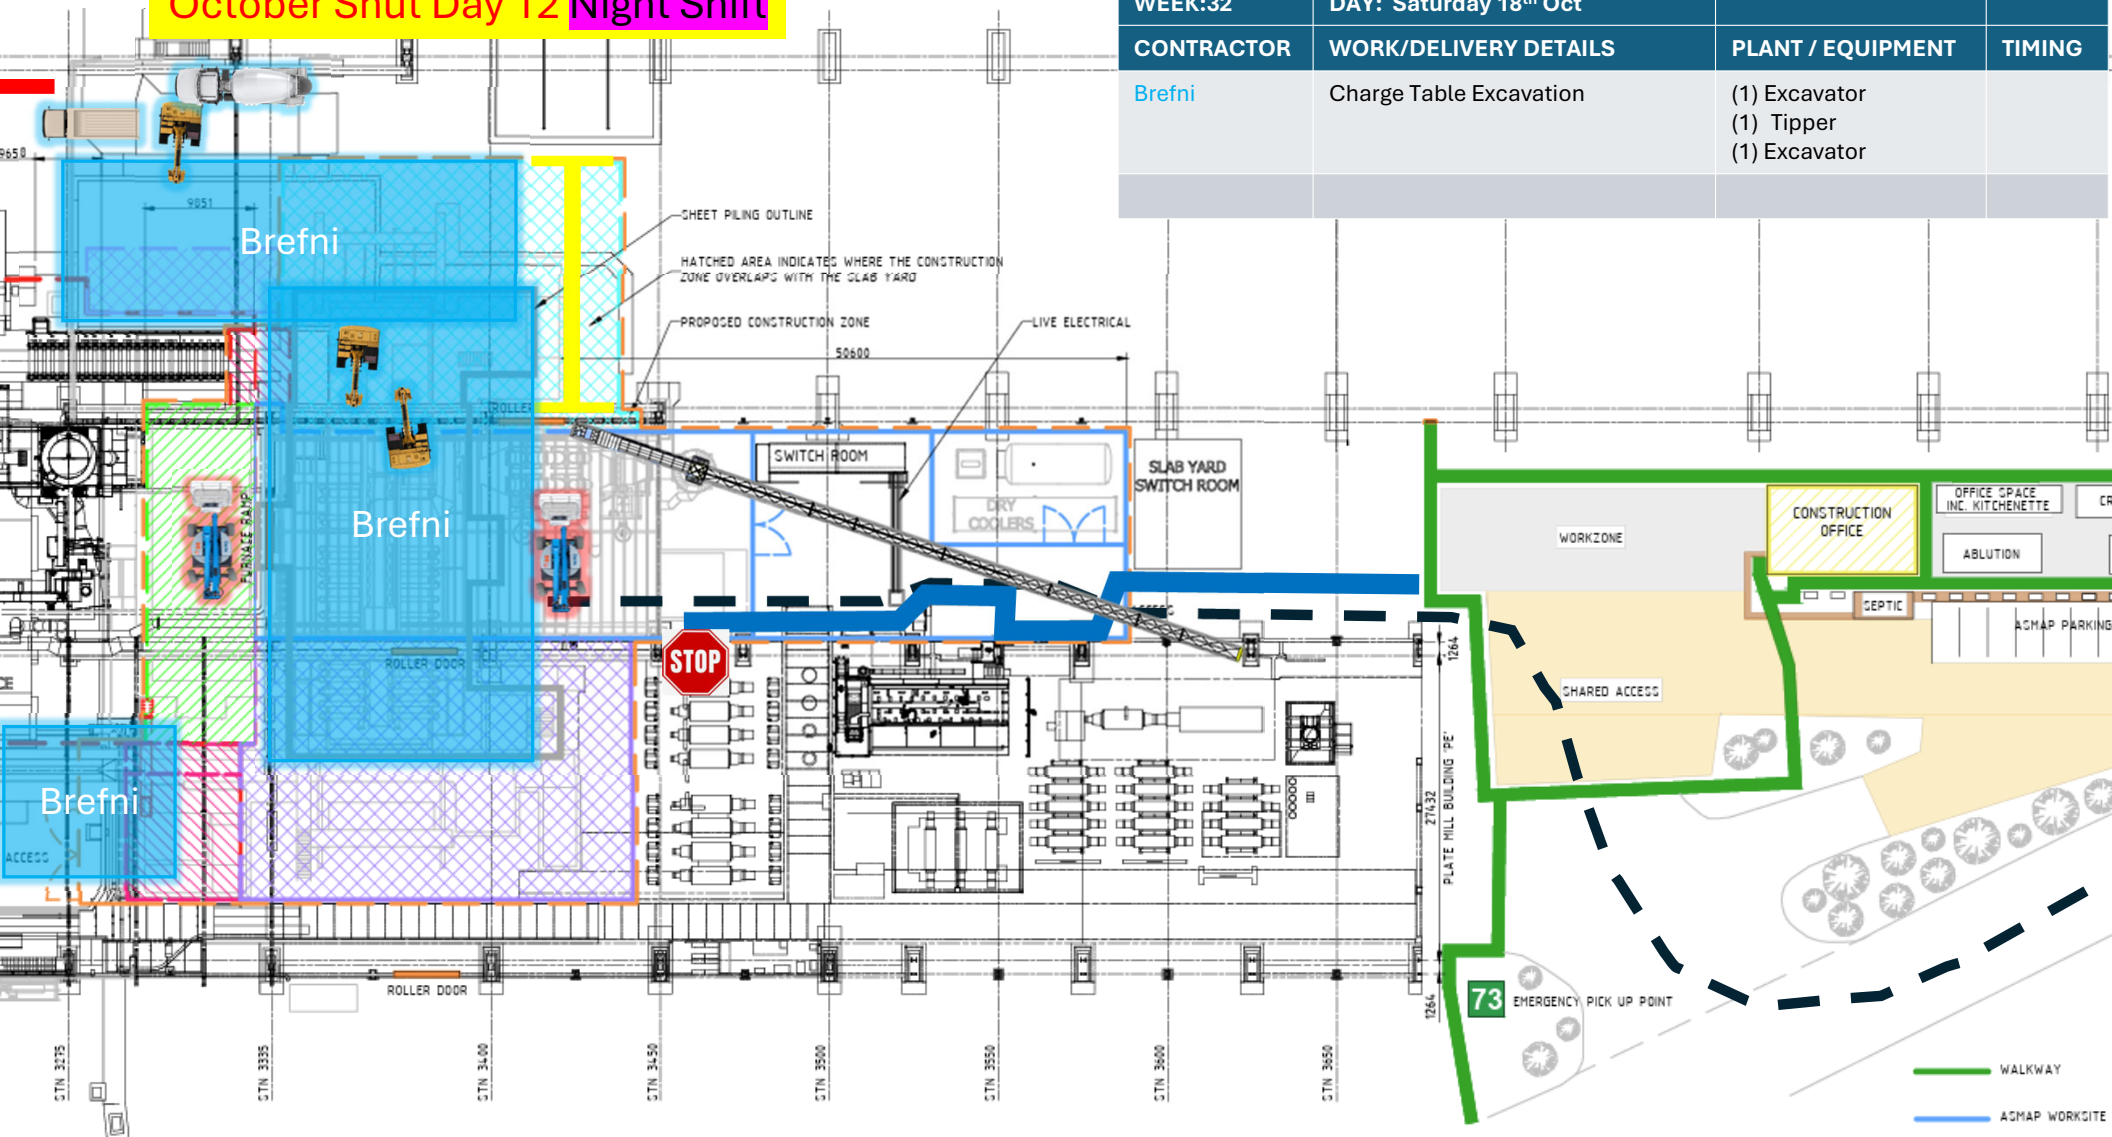


October Shut Day 13 Day Shift

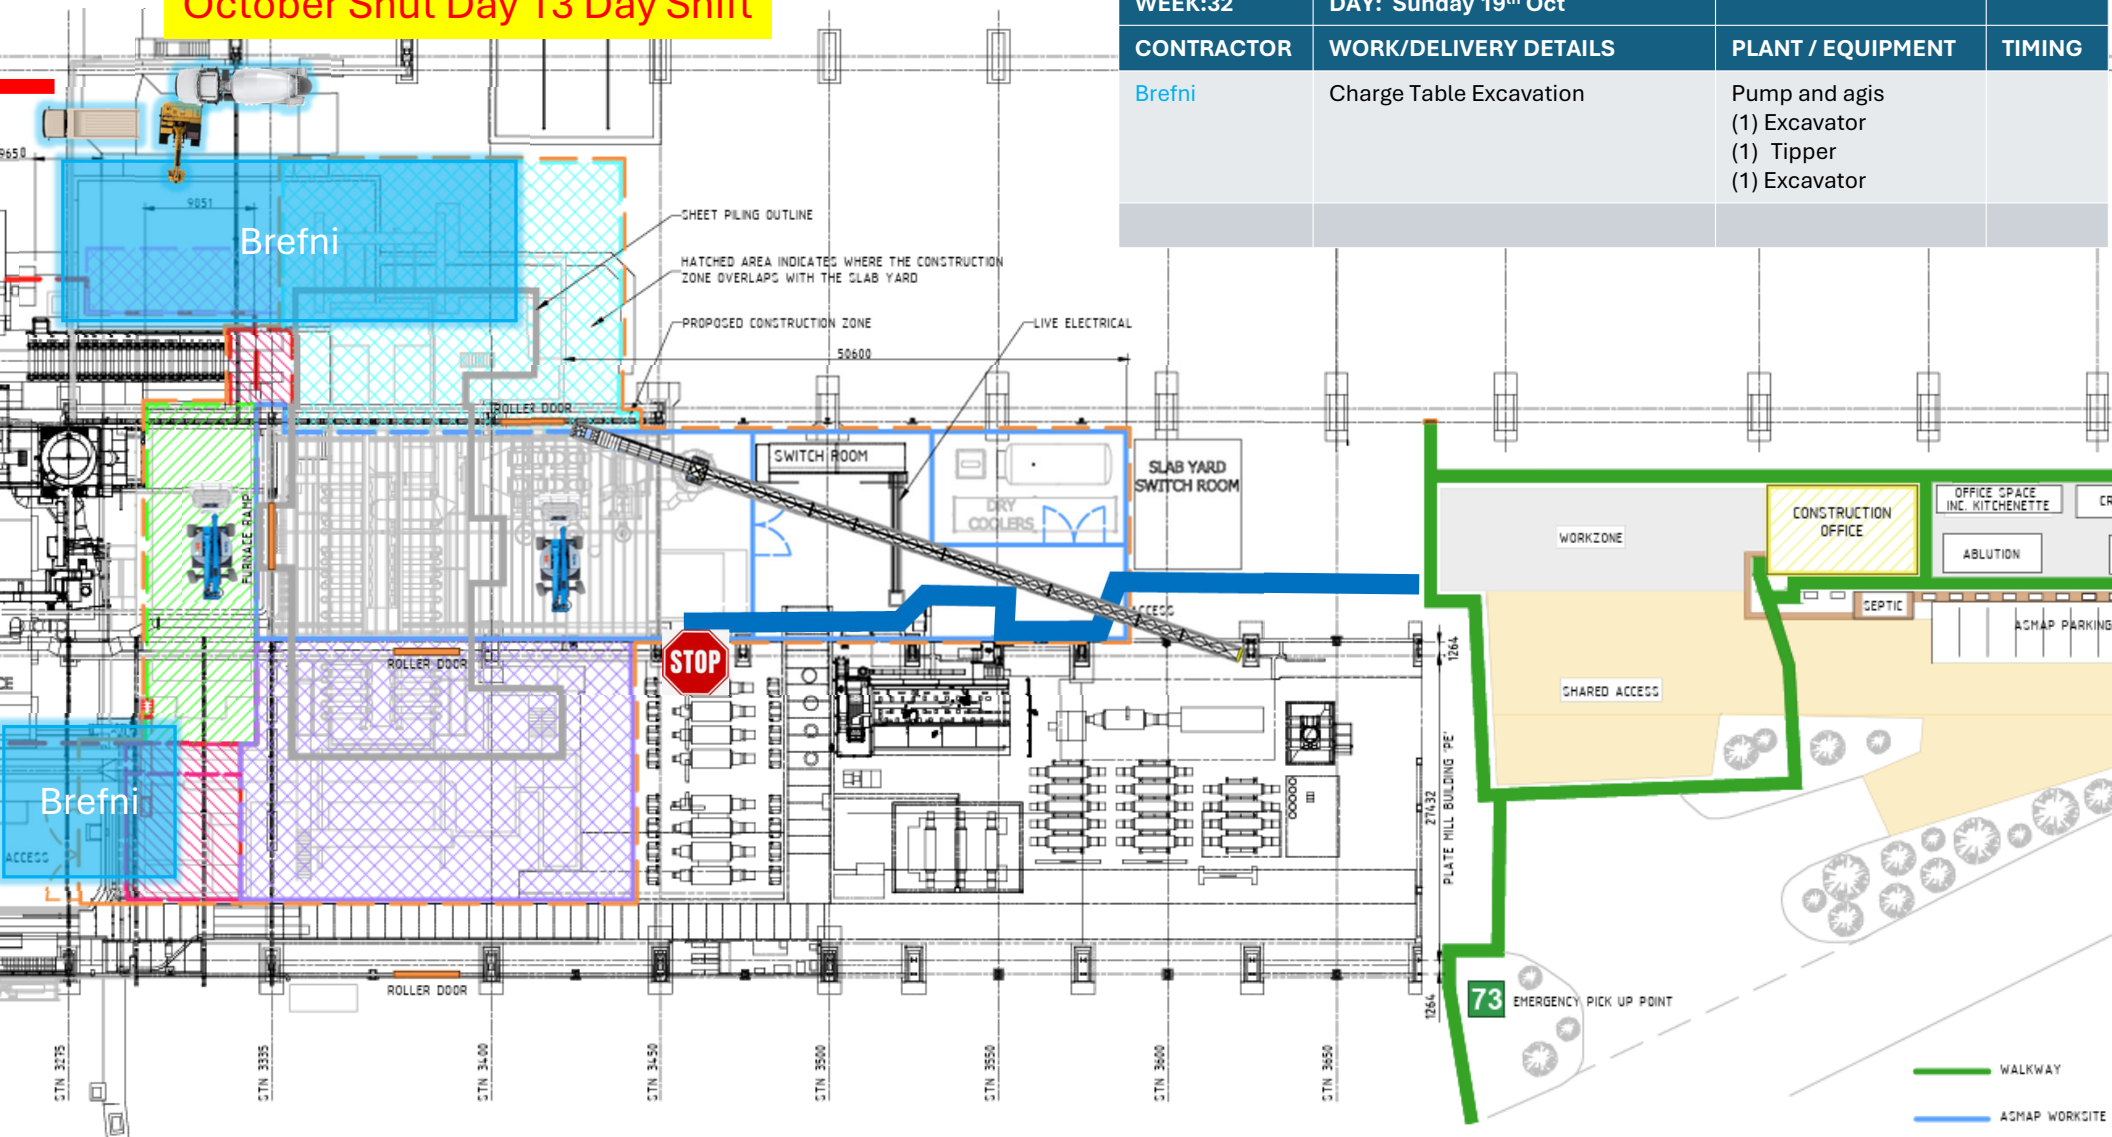


October Shut Day 13 Night Shift


WEEK:32	DAY: Sunday 19 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation	(1) Excavator (1) Tipper (1) Excavator	
IES	End Stop Install		

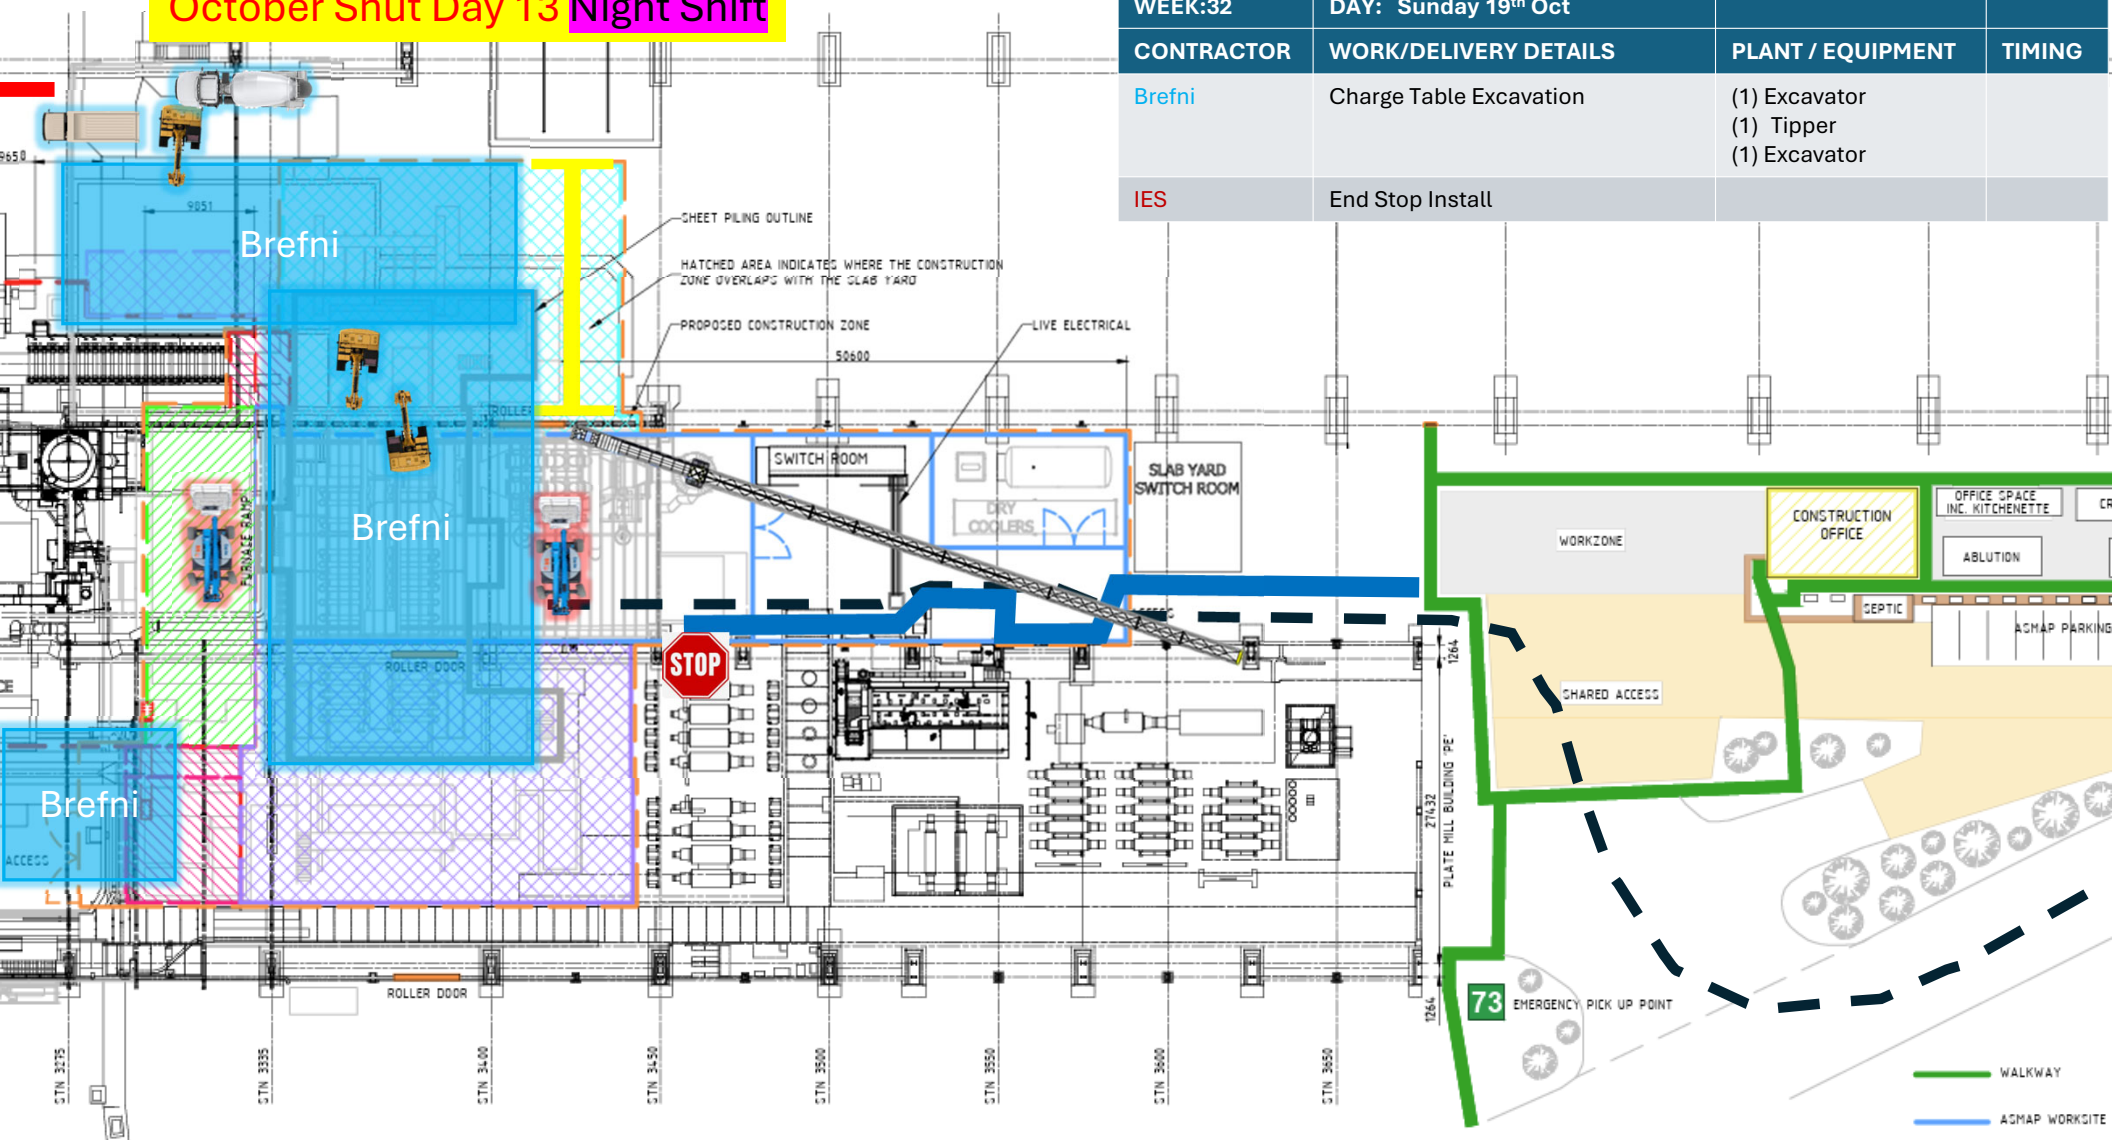

October Shut Day 14 Day Shift

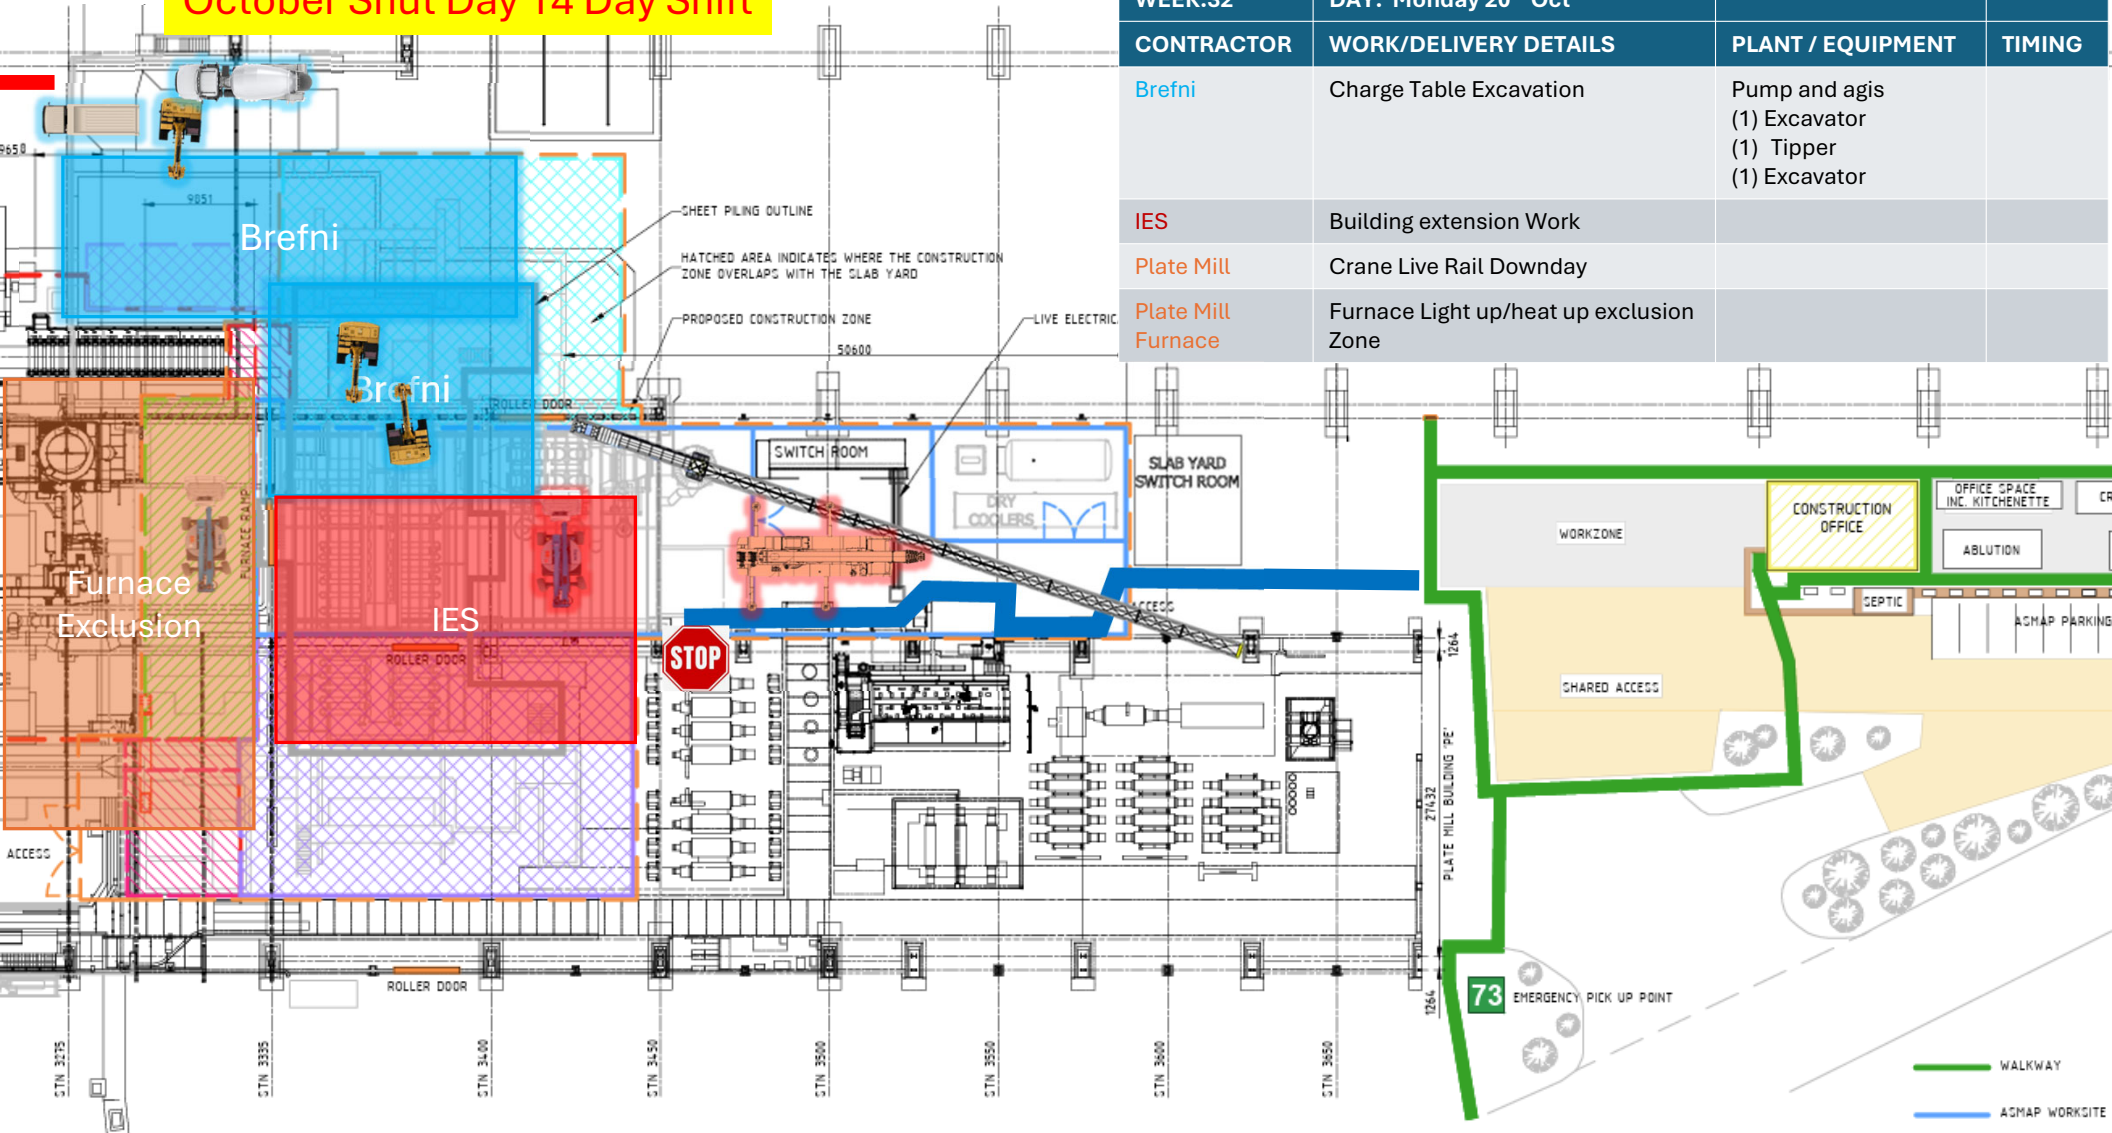

October Shut Day 14 Night Shift

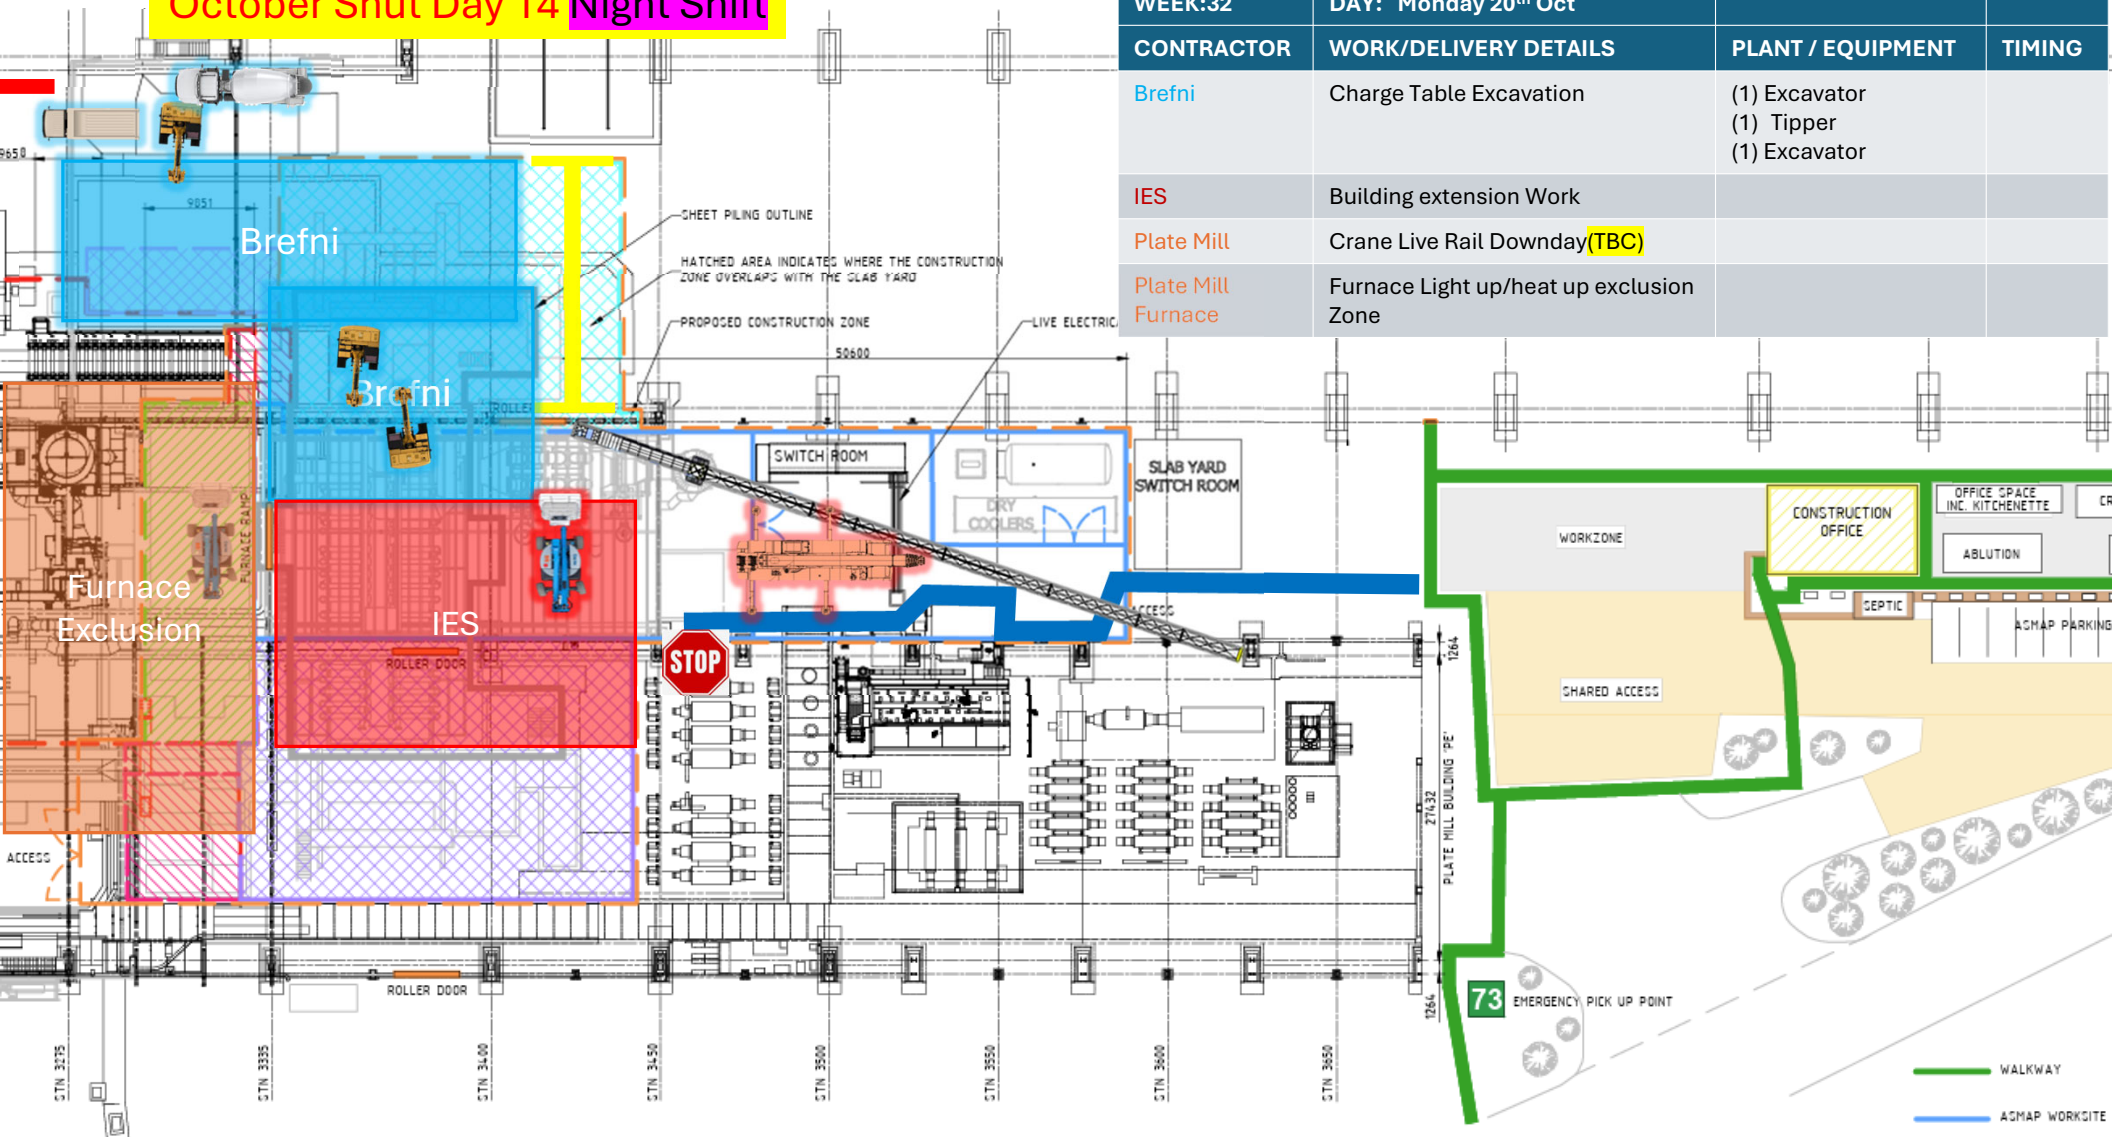


WEEK:32	DAY: Monday 20 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation	(1) Excavator (1) Tipper (1) Excavator	
IES	Building extension Work		
Plate Mill	Crane Live Rail Downday(TBC)		
Plate Mill Furnace	Furnace Light up/heat up exclusion Zone		

WALKWAY


ASMAP WORKSITE

October Shut Day 15 Day Shift

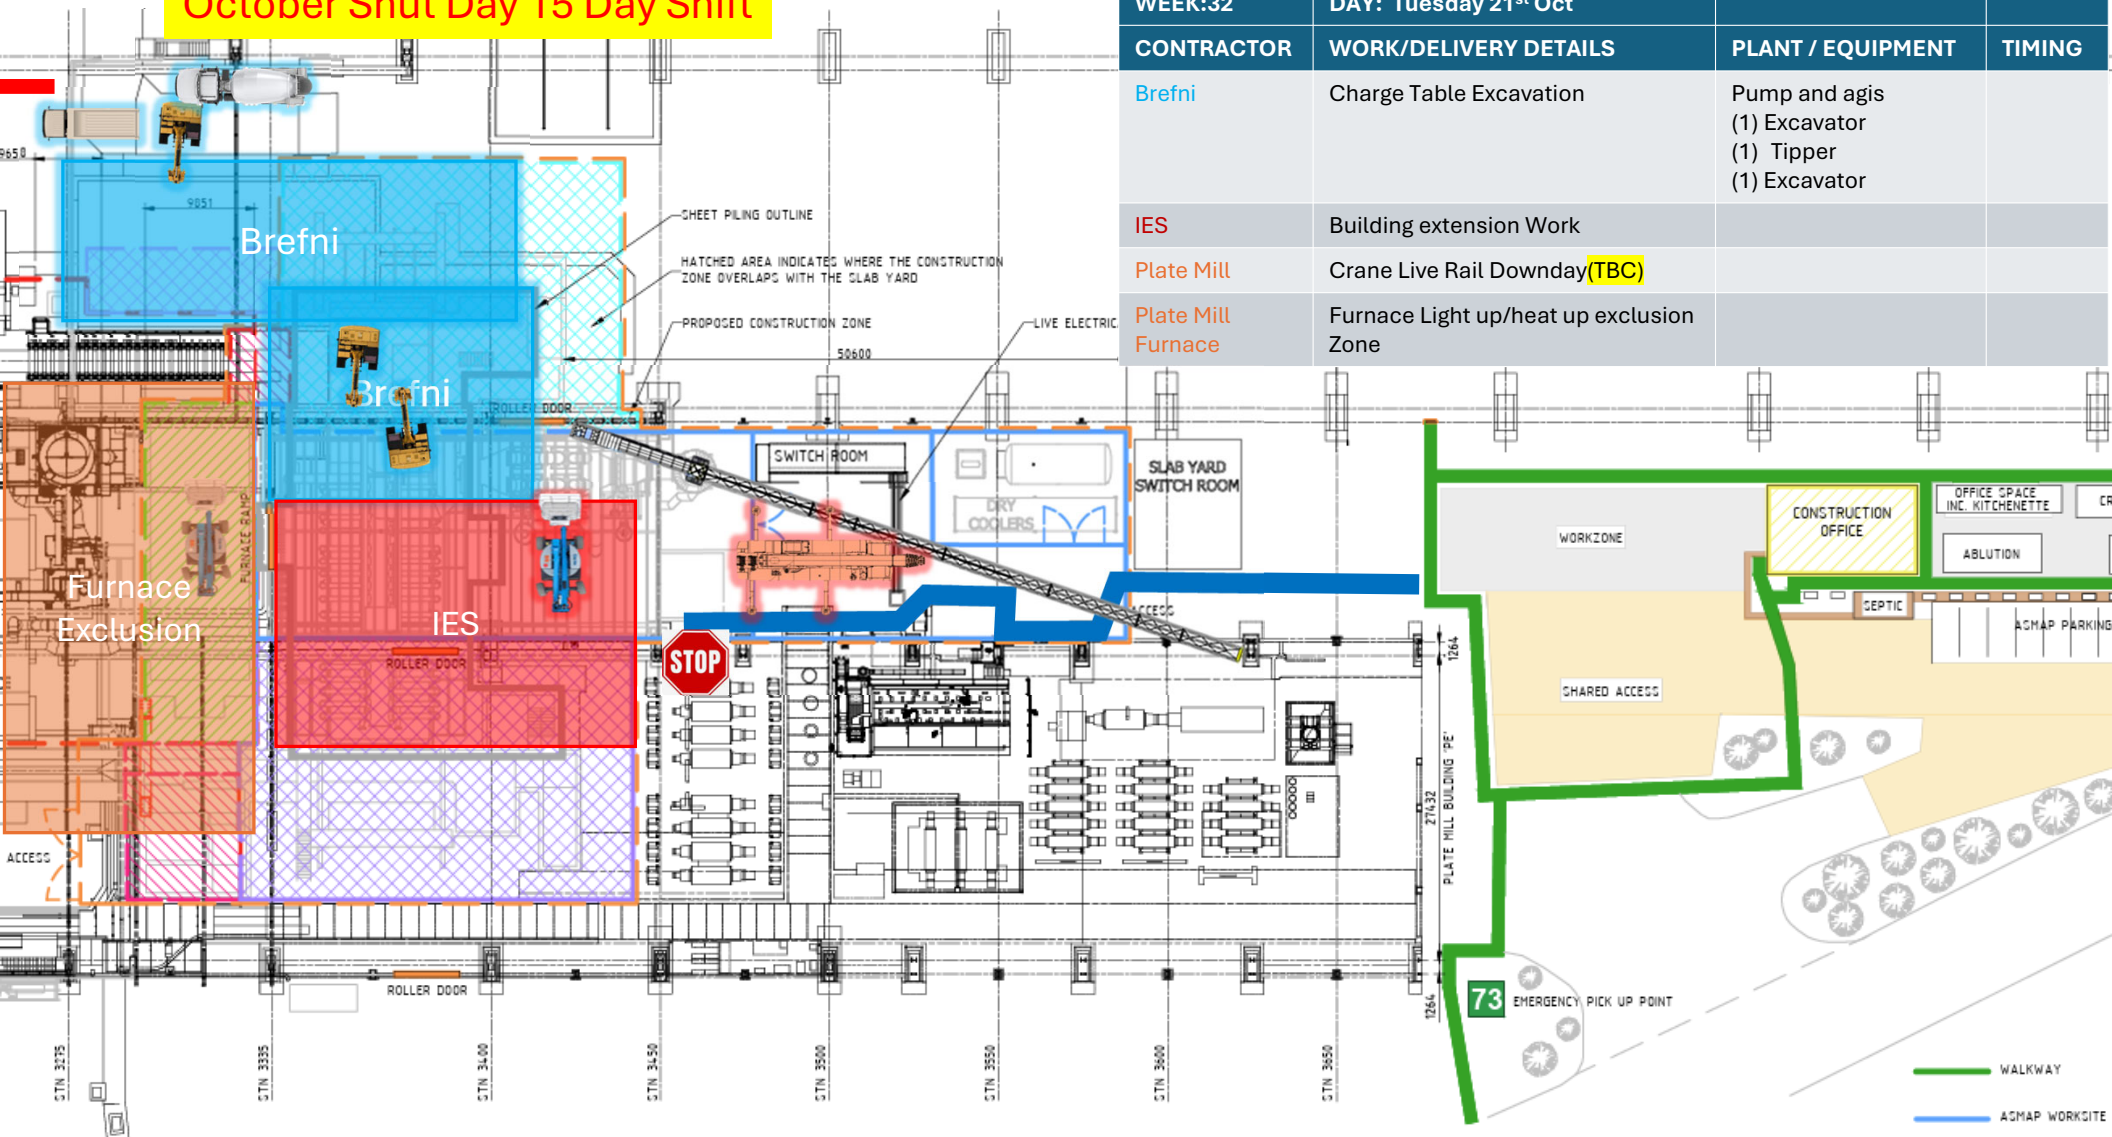


WEEK:32	DAY: Tuesday 21 st Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation	Pump and agis (1) Excavator (1) Tipper (1) Excavator	
IES	Building extension Work		
Plate Mill	Crane Live Rail Downday(TBC)		
Plate Mill Furnace	Furnace Light up/heat up exclusion Zone		

October Shut Day 15 Night Shift

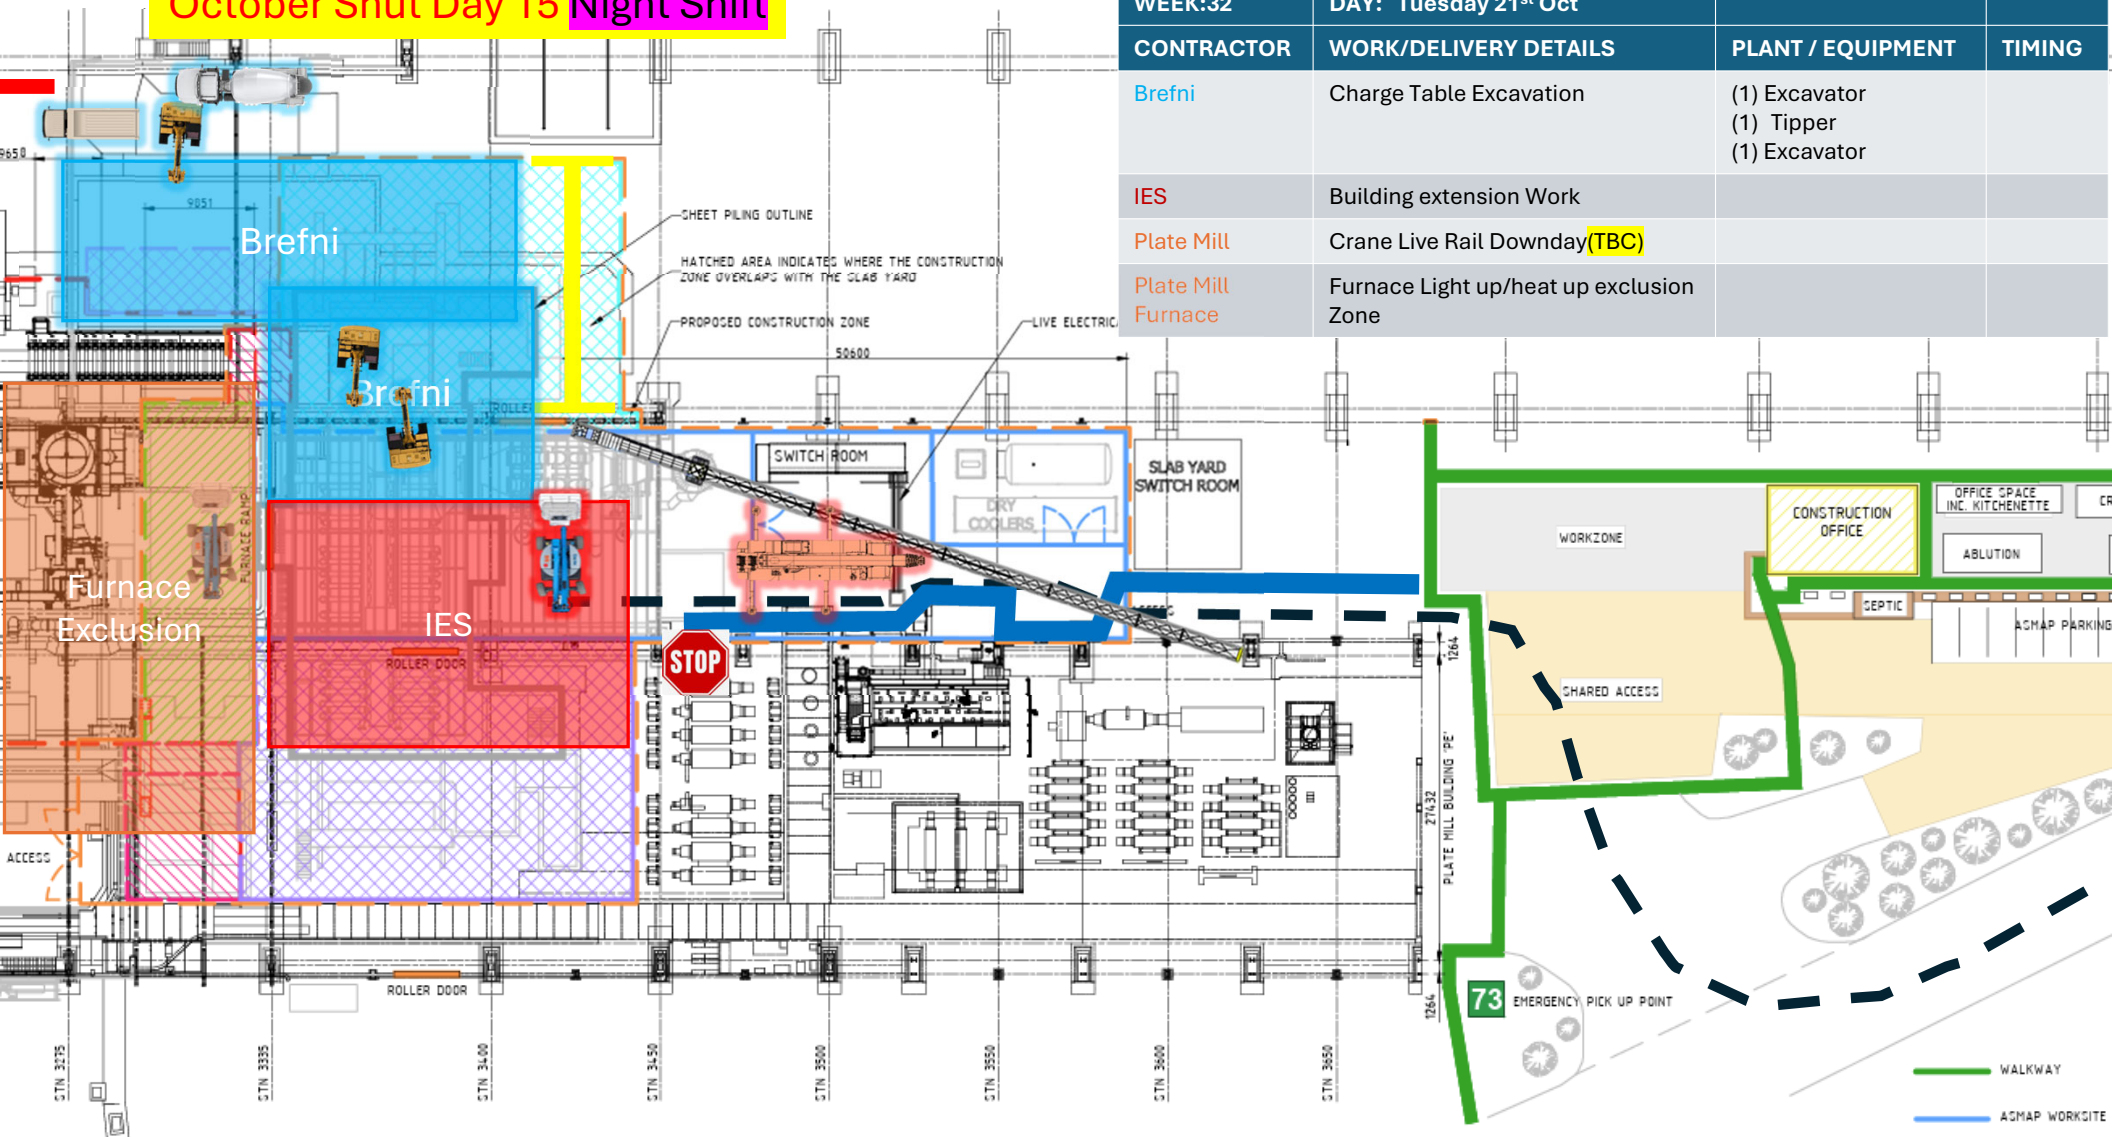


WEEK:32	DAY: Tuesday 21 st Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation	(1) Excavator (1) Tipper (1) Excavator	
IES	Building extension Work		
Plate Mill	Crane Live Rail Downday(TBC)		
Plate Mill Furnace	Furnace Light up/heat up exclusion Zone		

October Shut Day 16 Day Shift

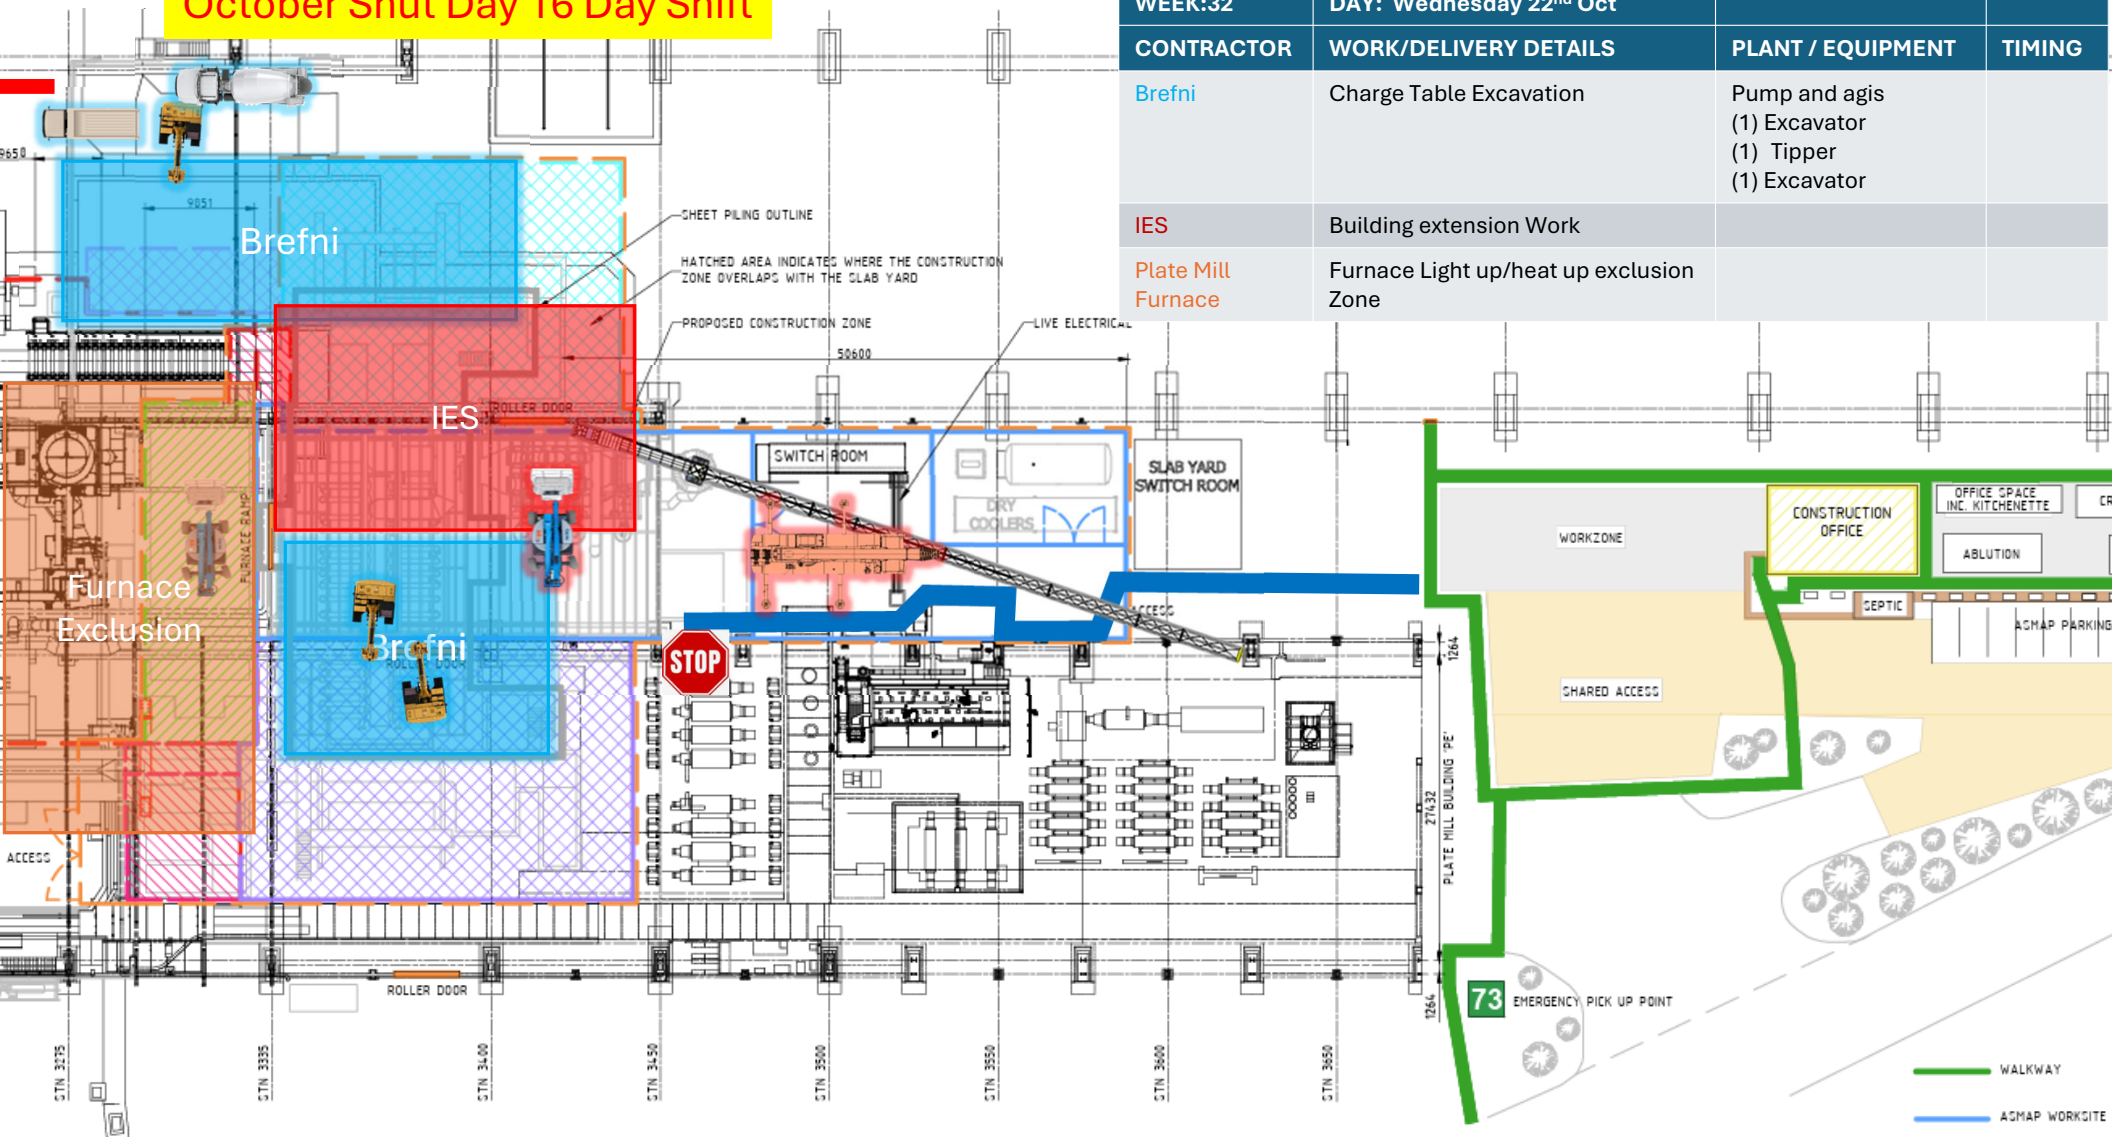


October Shut Day 16 Night Shift

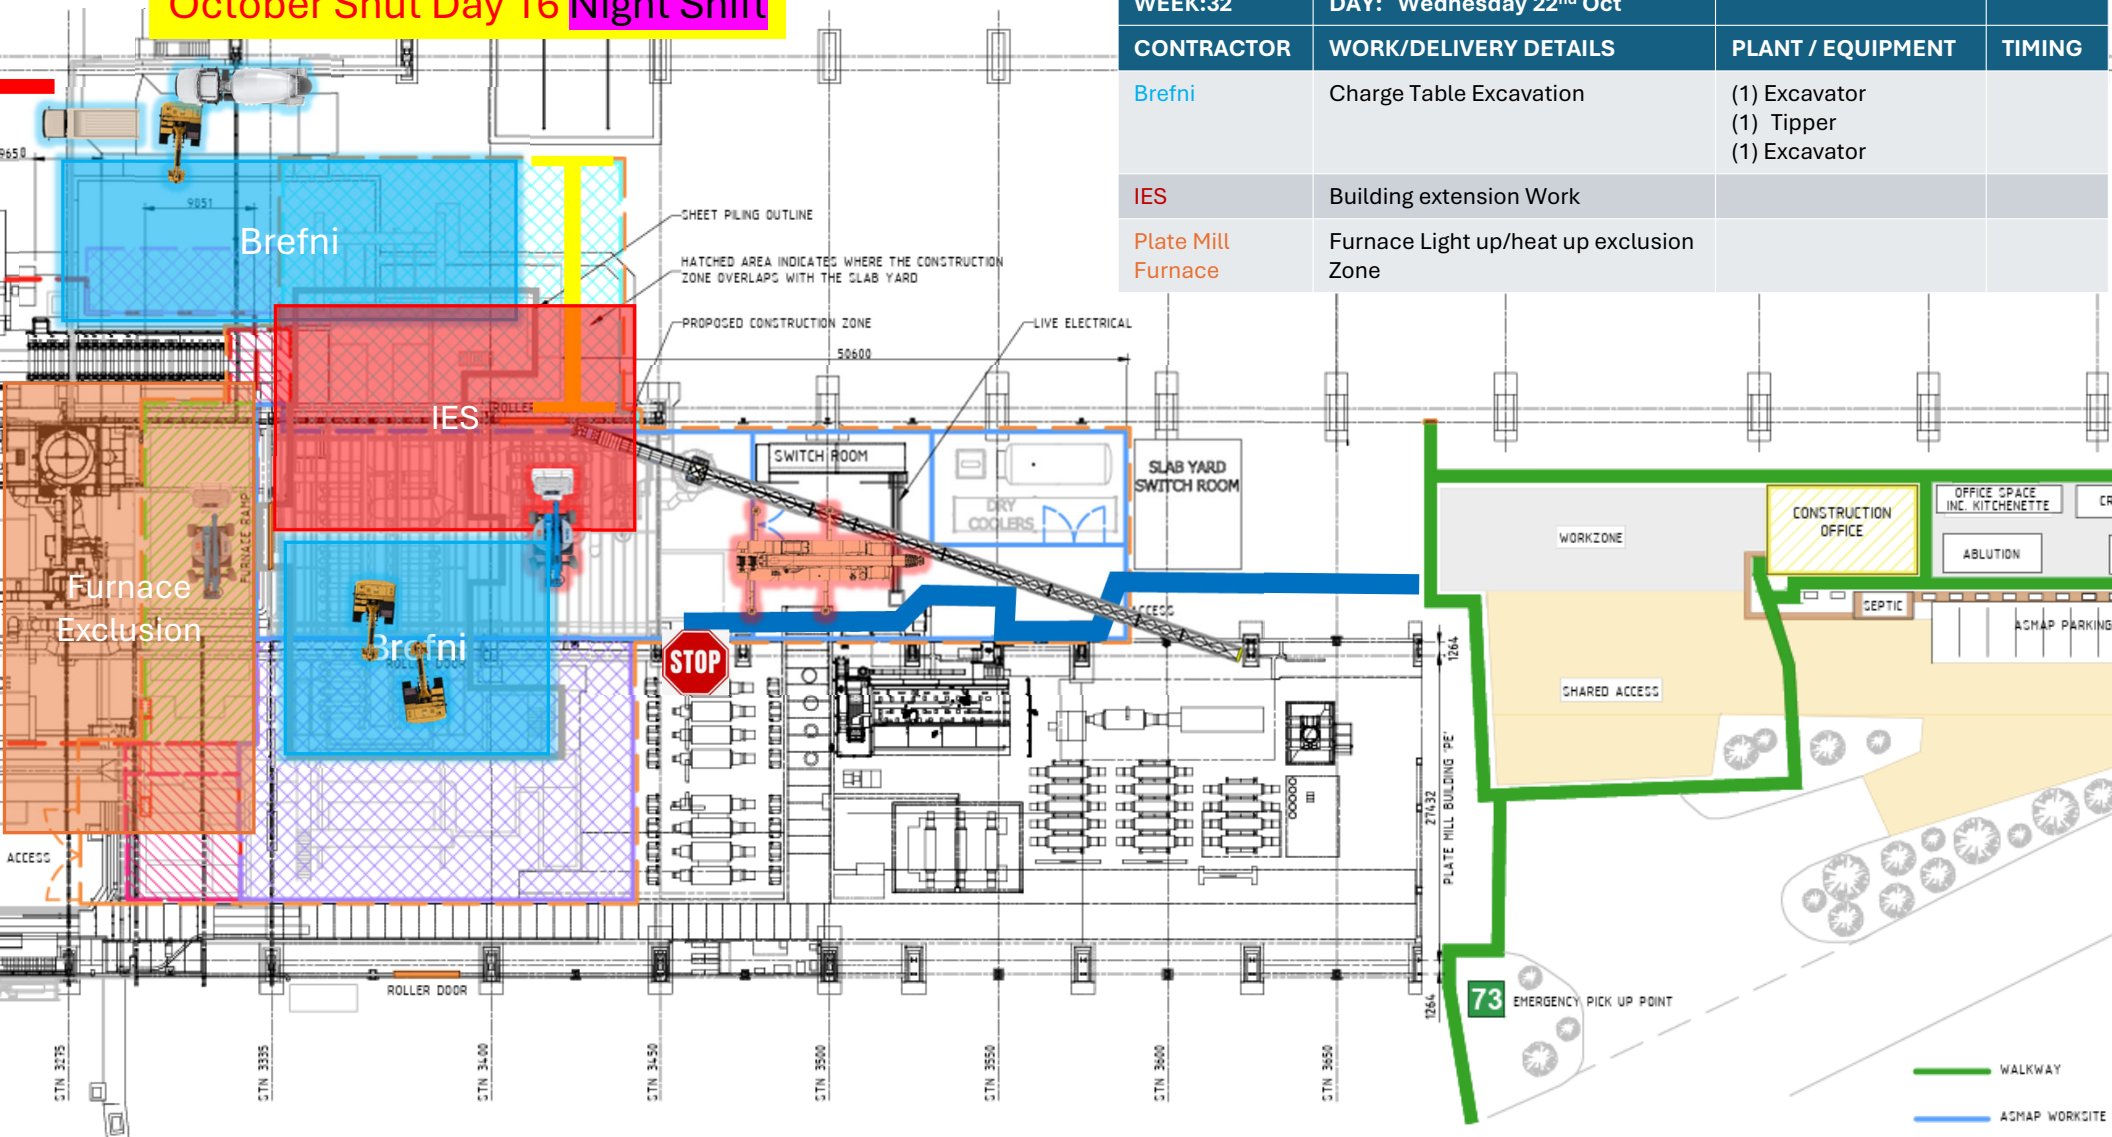


WEEK:32	DAY: Wednesday 22 nd Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation	(1) Excavator (1) Tipper (1) Excavator	
IES	Building extension Work		
Plate Mill Furnace	Furnace Light up/heat up exclusion Zone		


October Shut Day 17 Day Shift

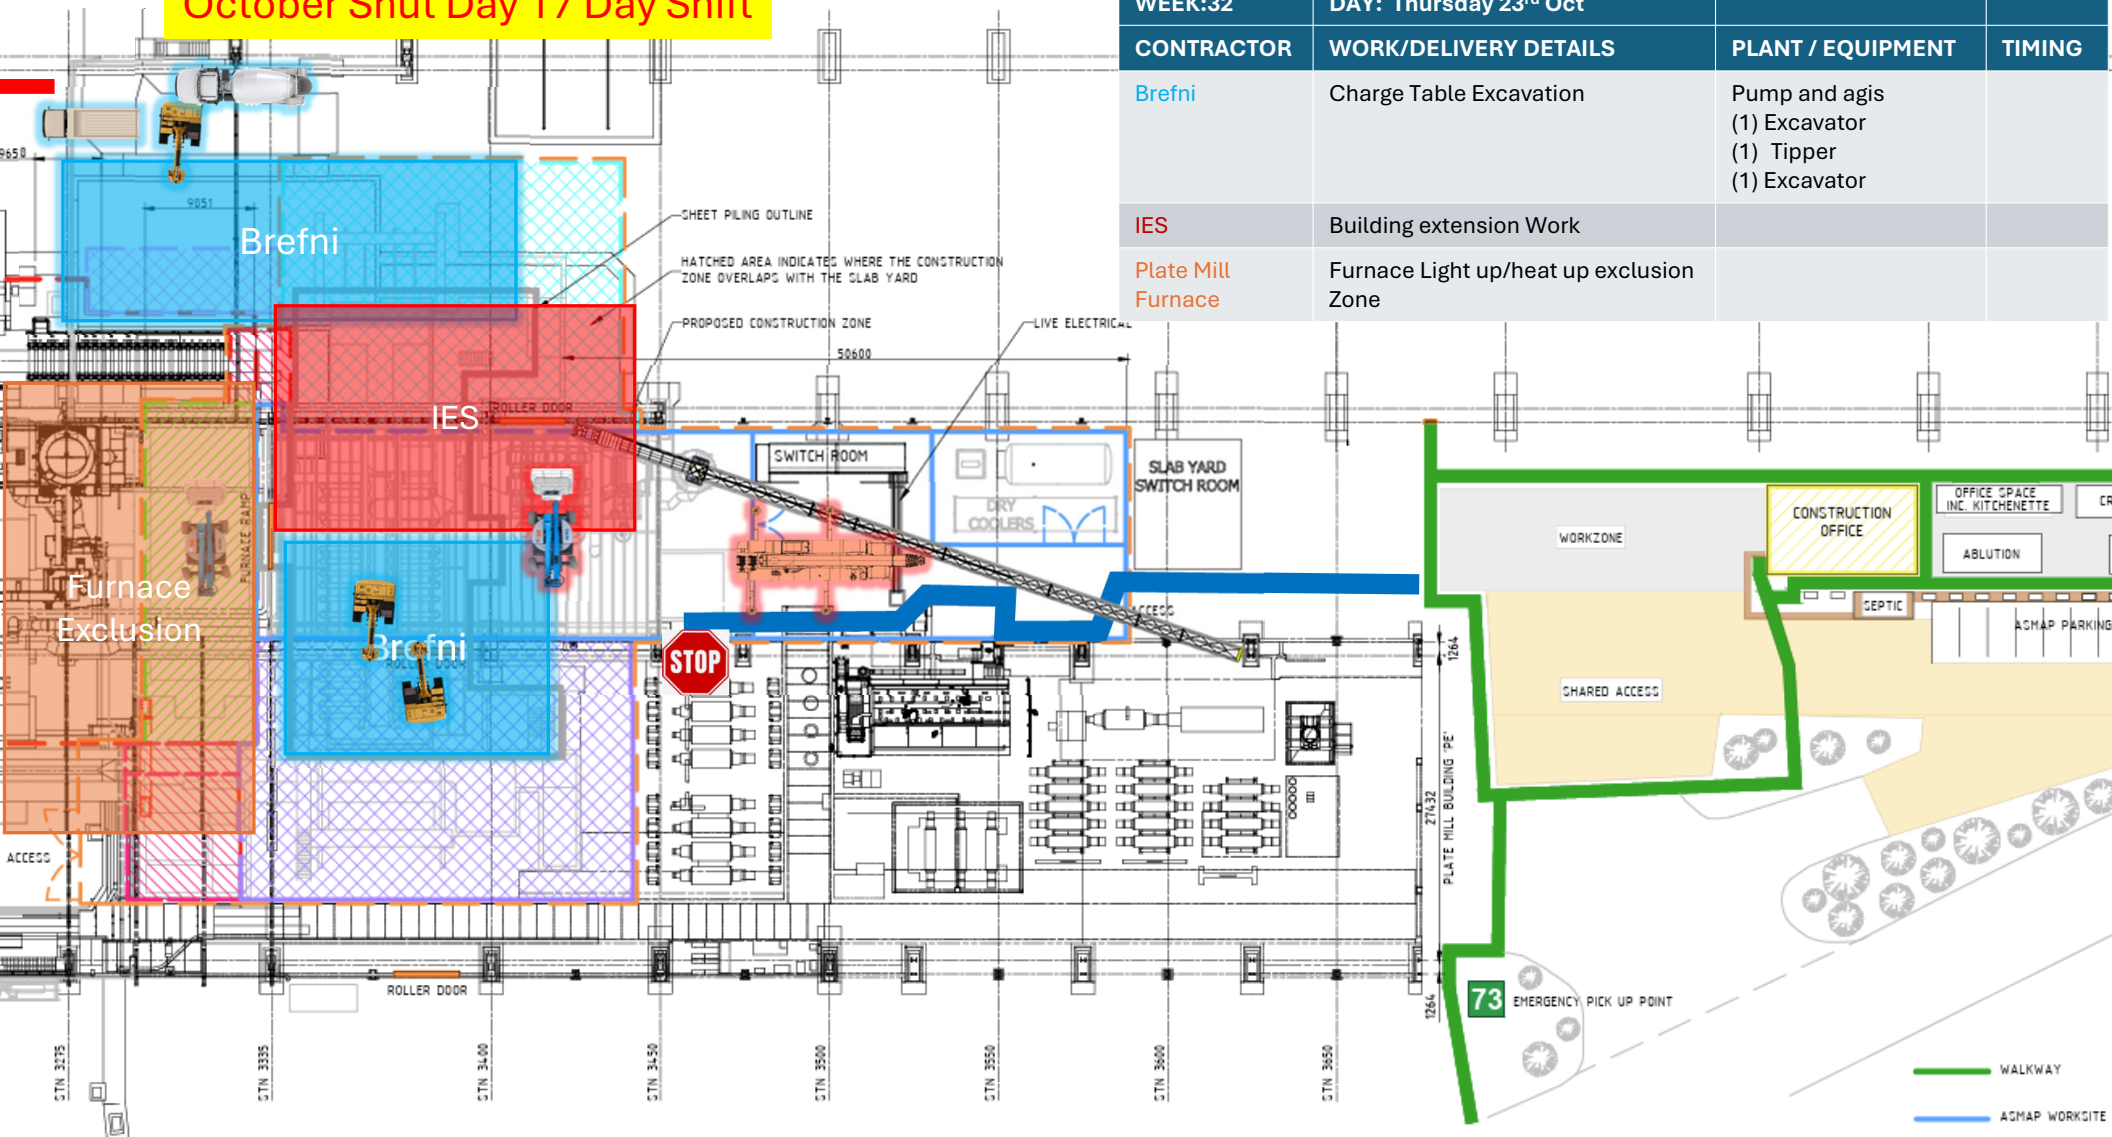

October Shut Day 17 Night Shift

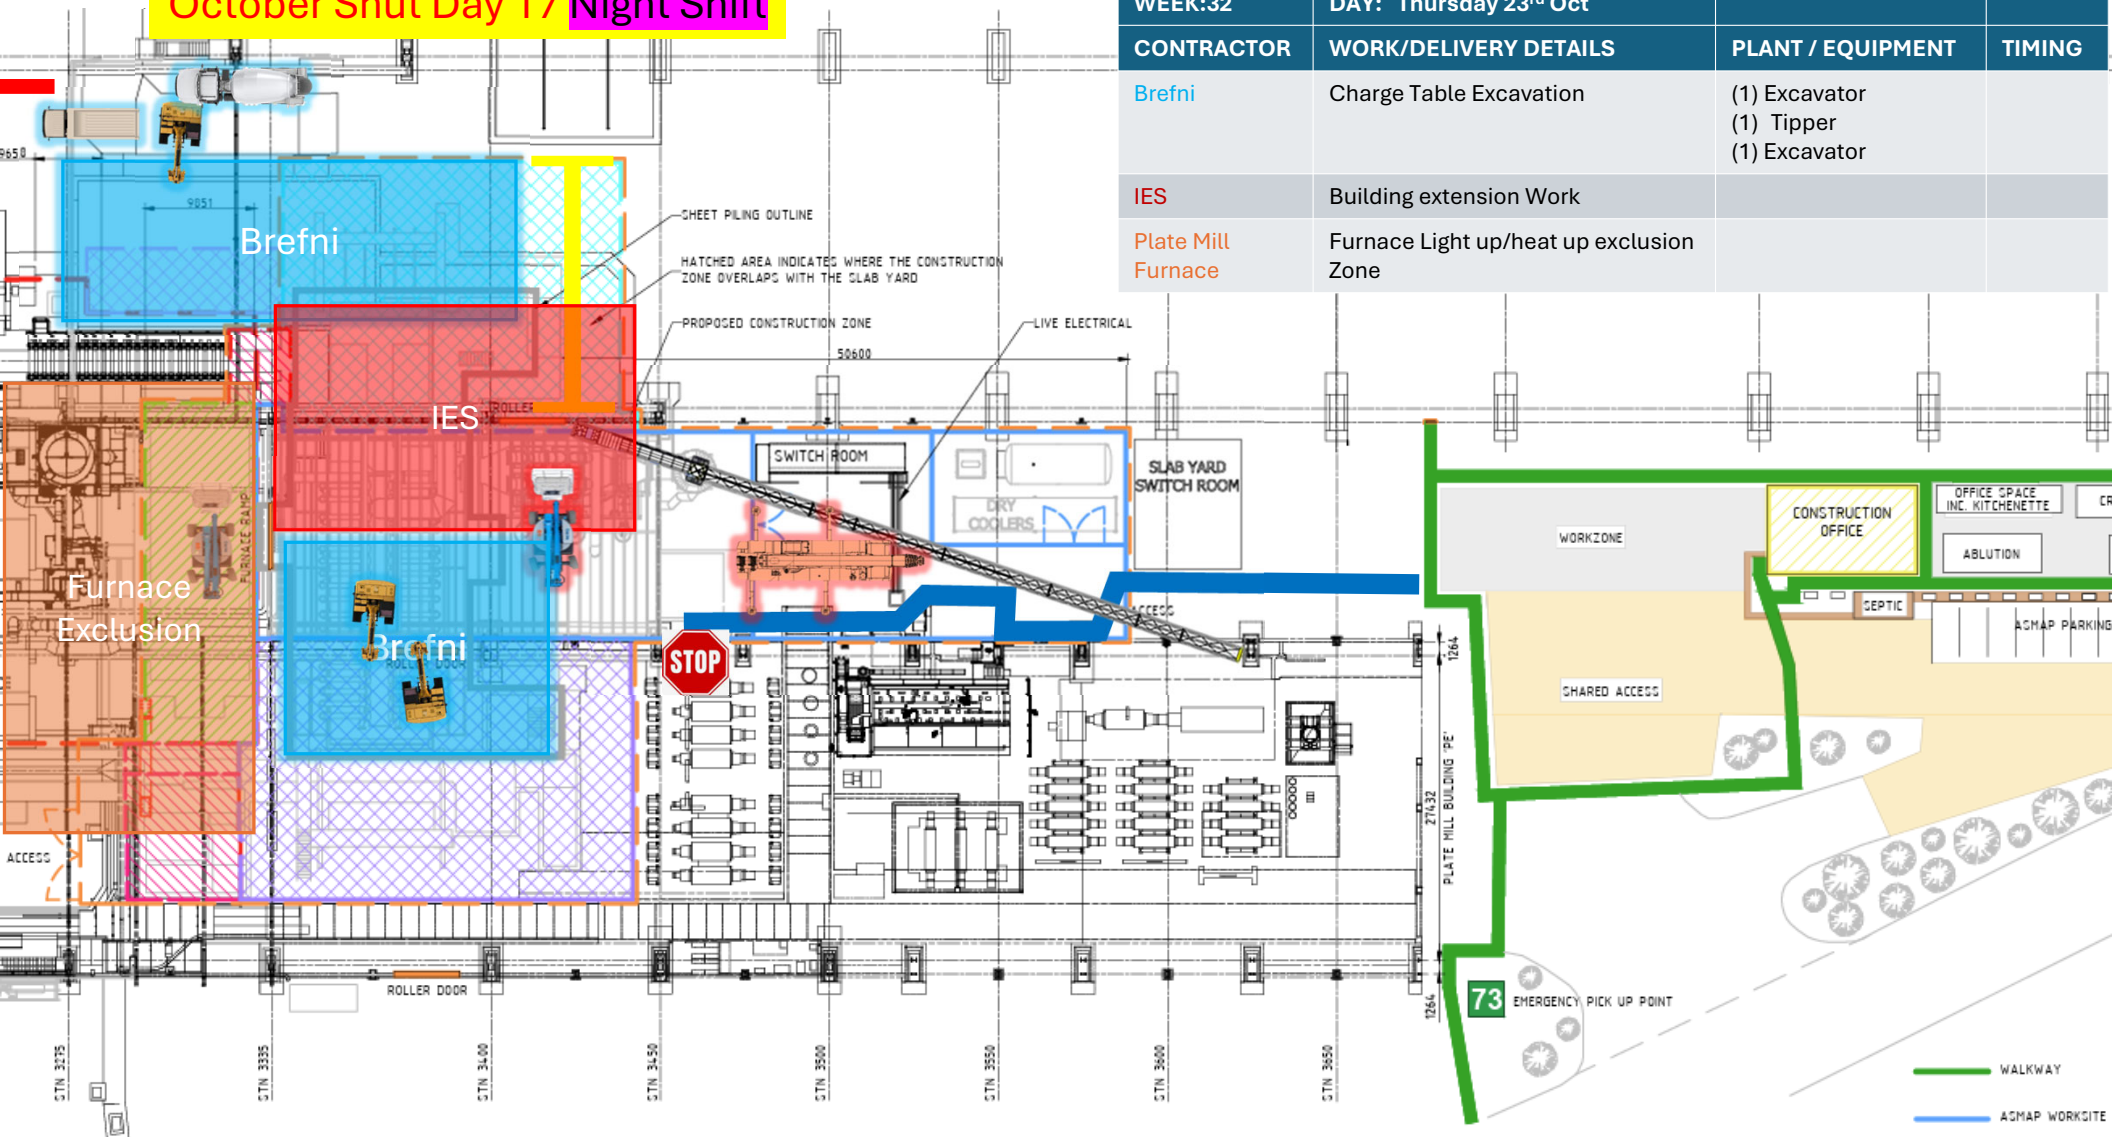


October Shut Day 18 Day Shift

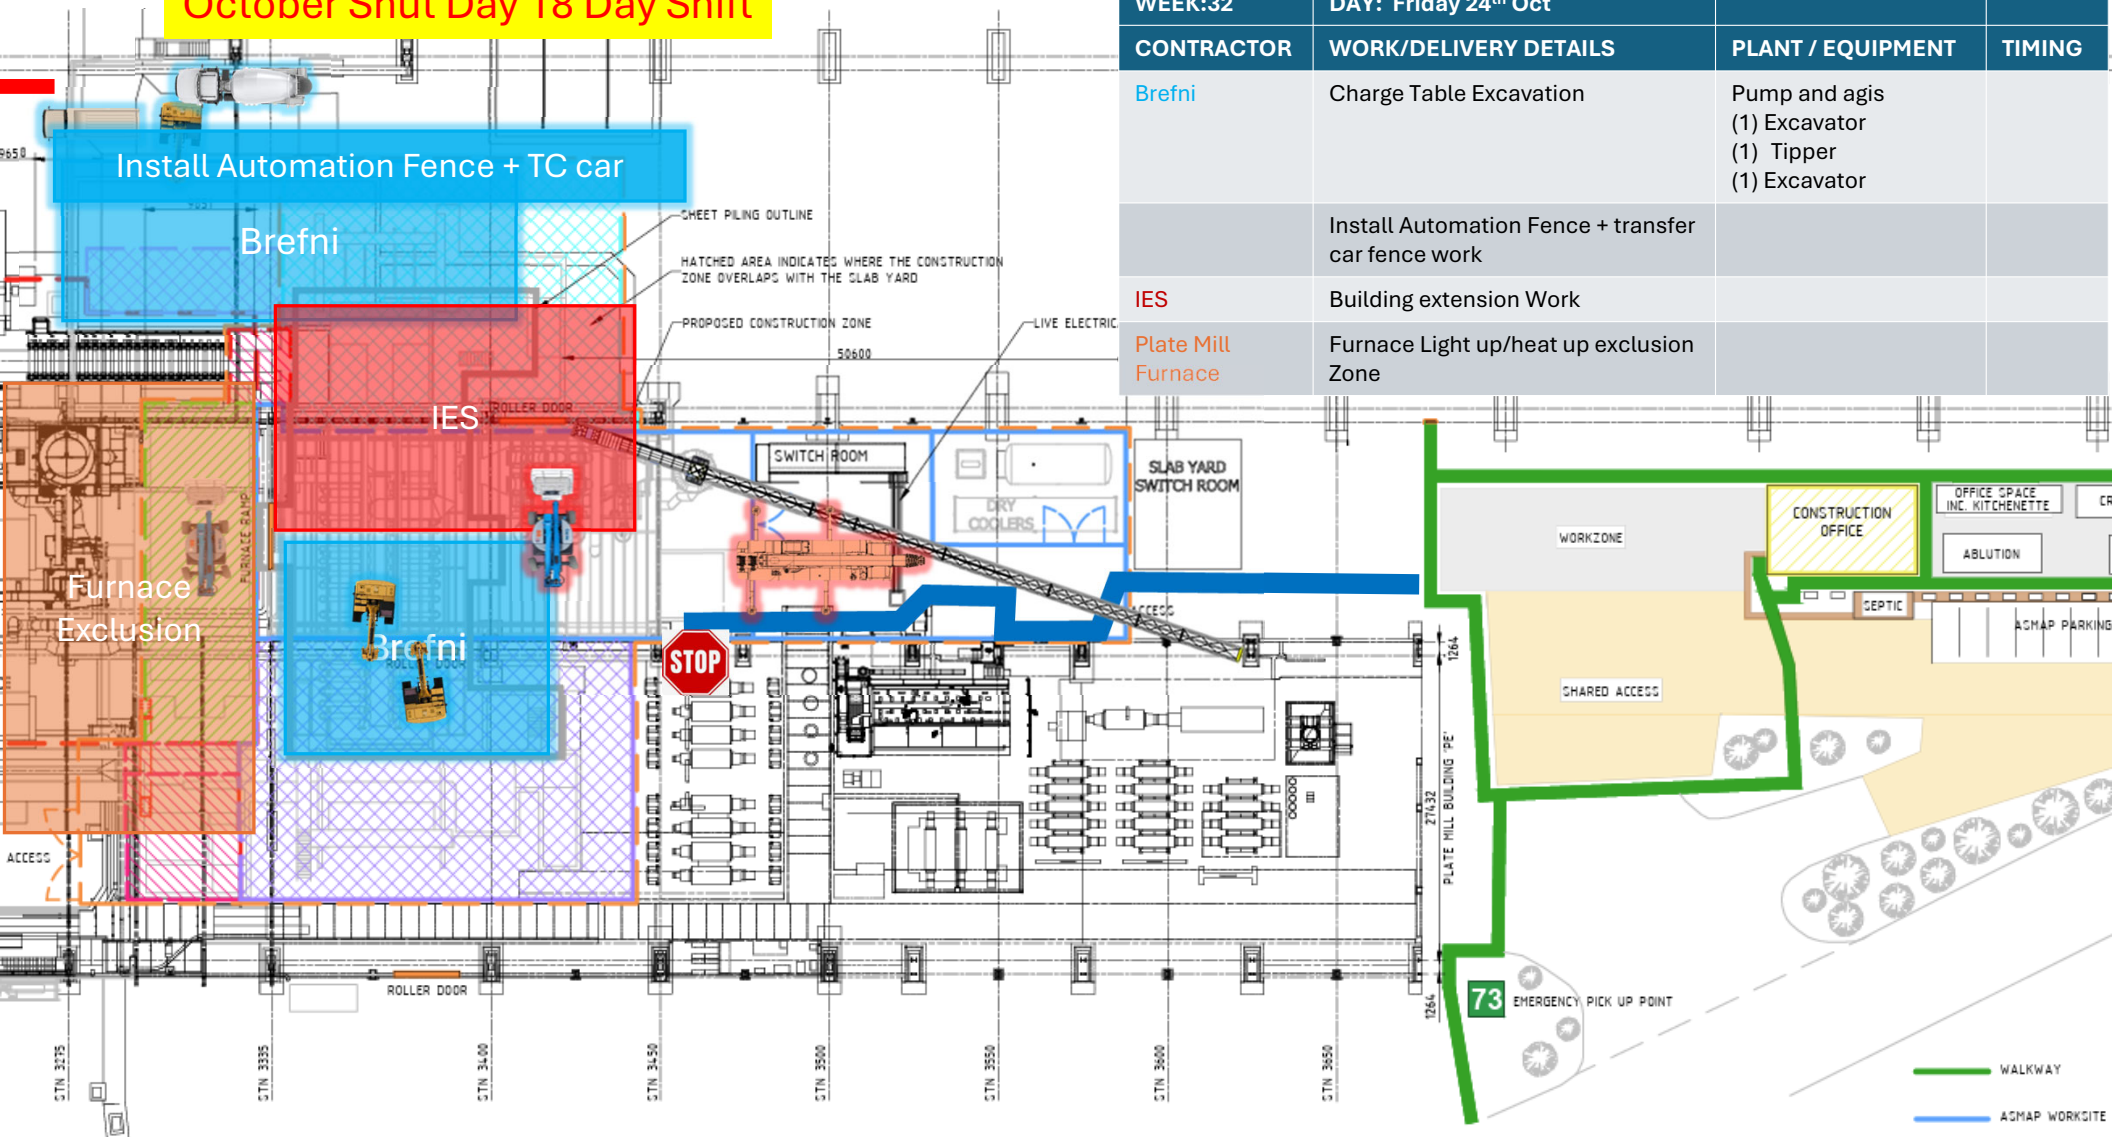

WEEK:32	DAY: Friday 24 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation	Pump and agis (1) Excavator (1) Tipper (1) Excavator	
	Install Automation Fence + transfer car fence work		
IES	Building extension Work		
Plate Mill Furnace	Furnace Light up/heat up exclusion Zone		


October Shut Day 18 Night Shift

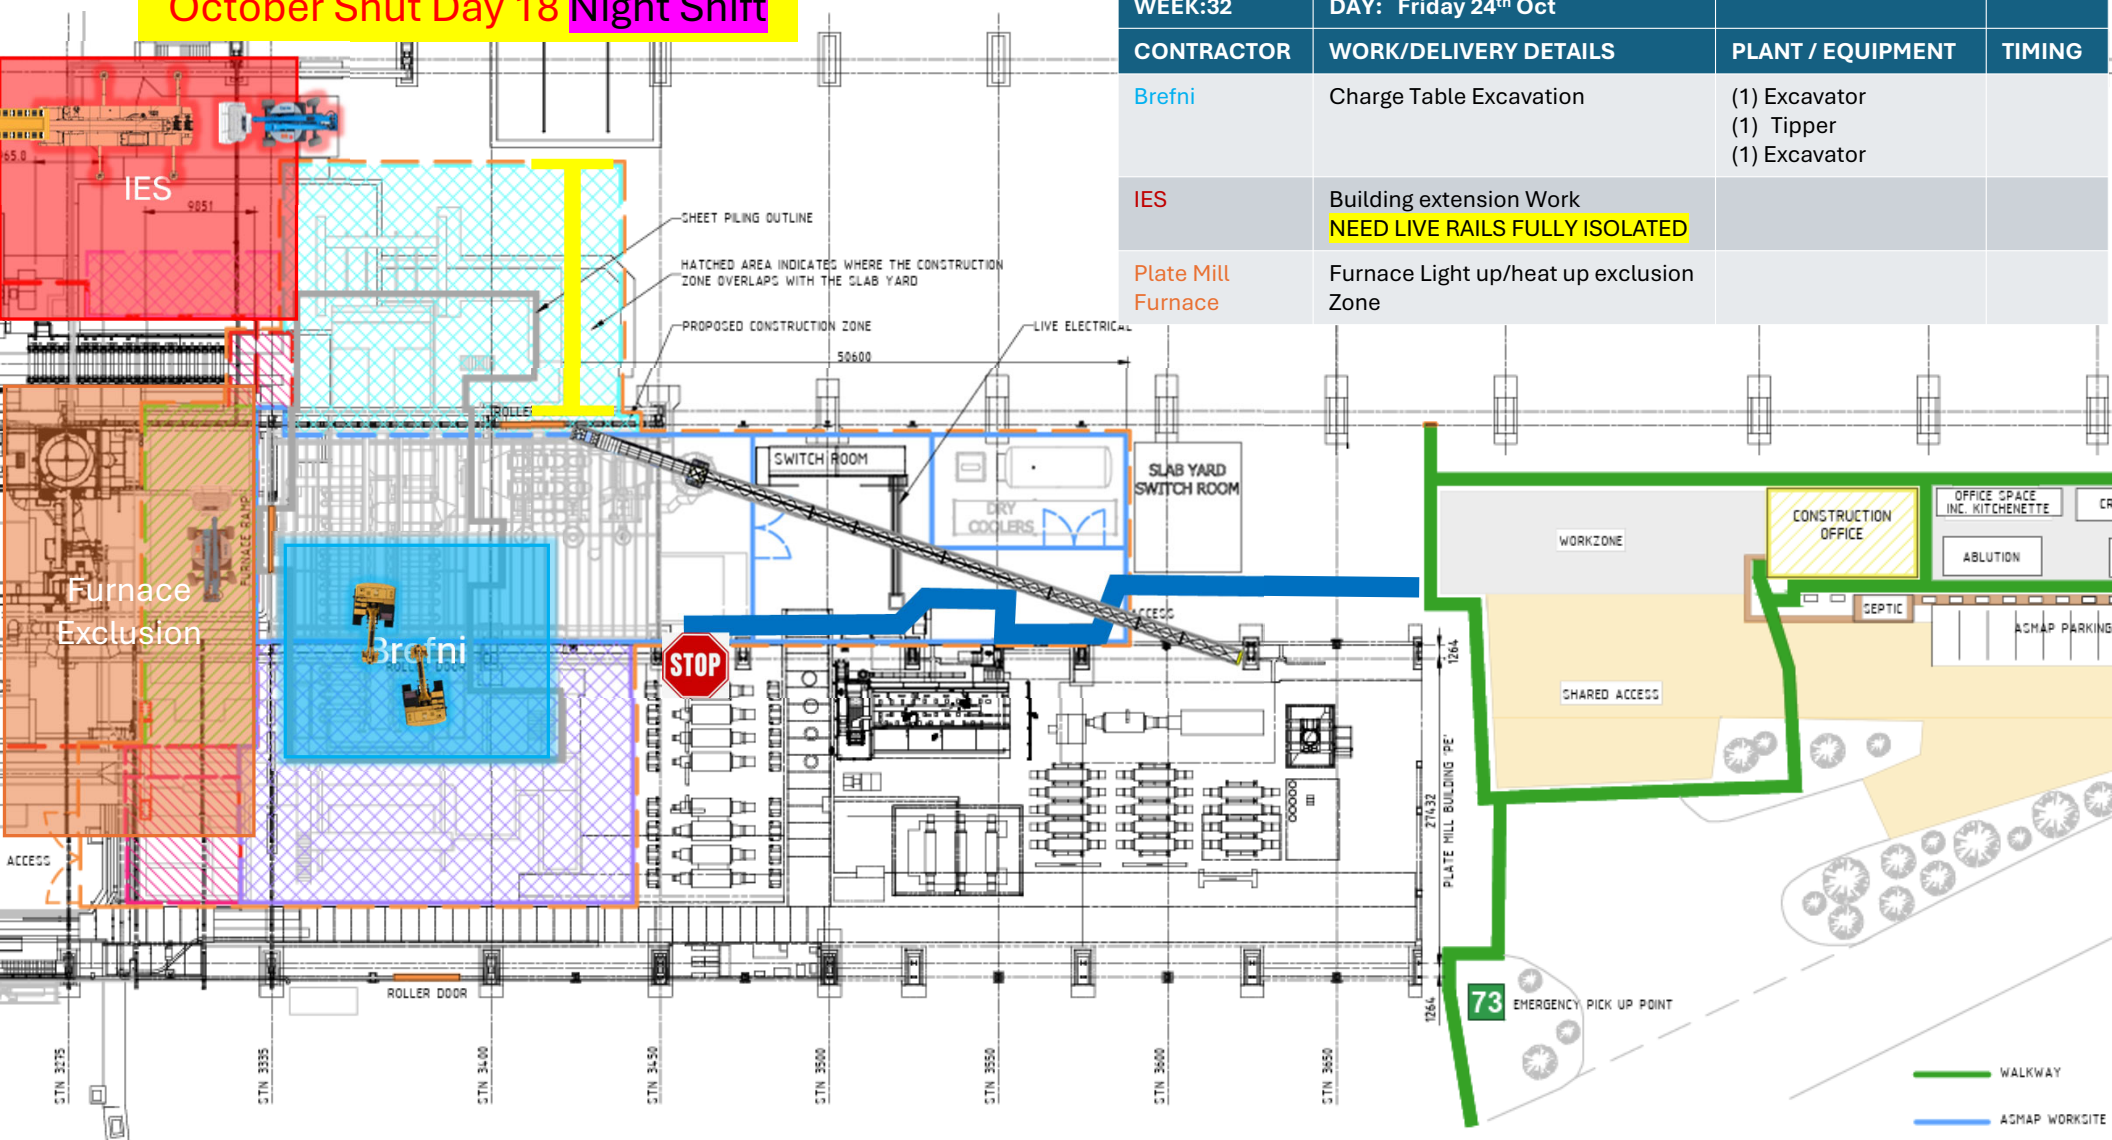

WEEK:32	DAY: Friday 24 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	Charge Table Excavation	(1) Excavator (1) Tipper (1) Excavator	
IES	Building extension Work NEED LIVE RAILS FULLY ISOLATED		
Plate Mill Furnace	Furnace Light up/heat up exclusion Zone		

October Shut Day 19 Day Shift


WEEK:32	DAY: Saturday 25 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Slabyard	Crane Testing		
Brefni	Discharge Area Works		

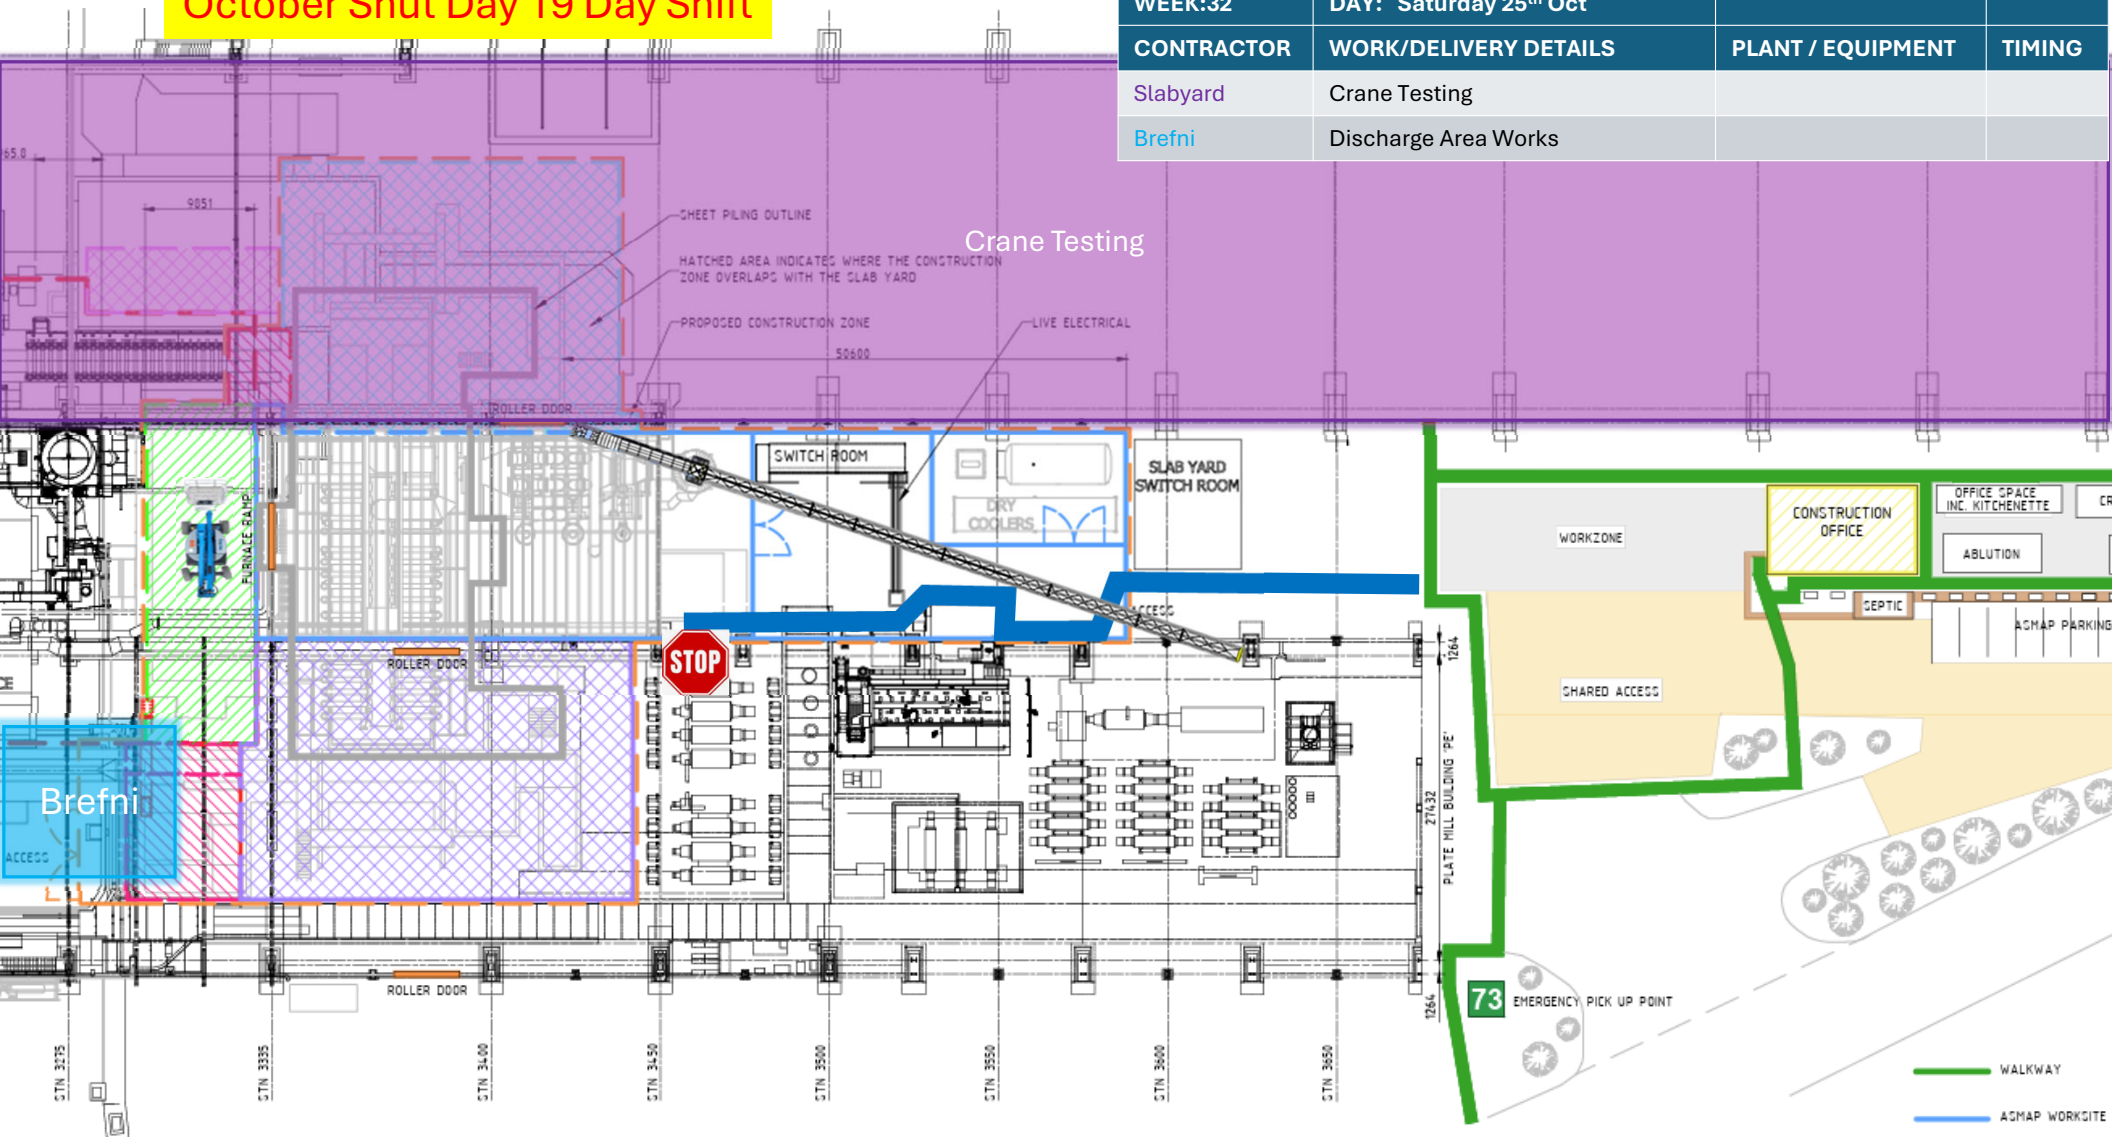

— WALKWAY
— ASMAP WORKSITE


October Shut Day 19 Night Shift

WEEK:32	DAY: Saturday 25 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Slabyard	Crane Testing		
Brefni	Discharge Area Works		

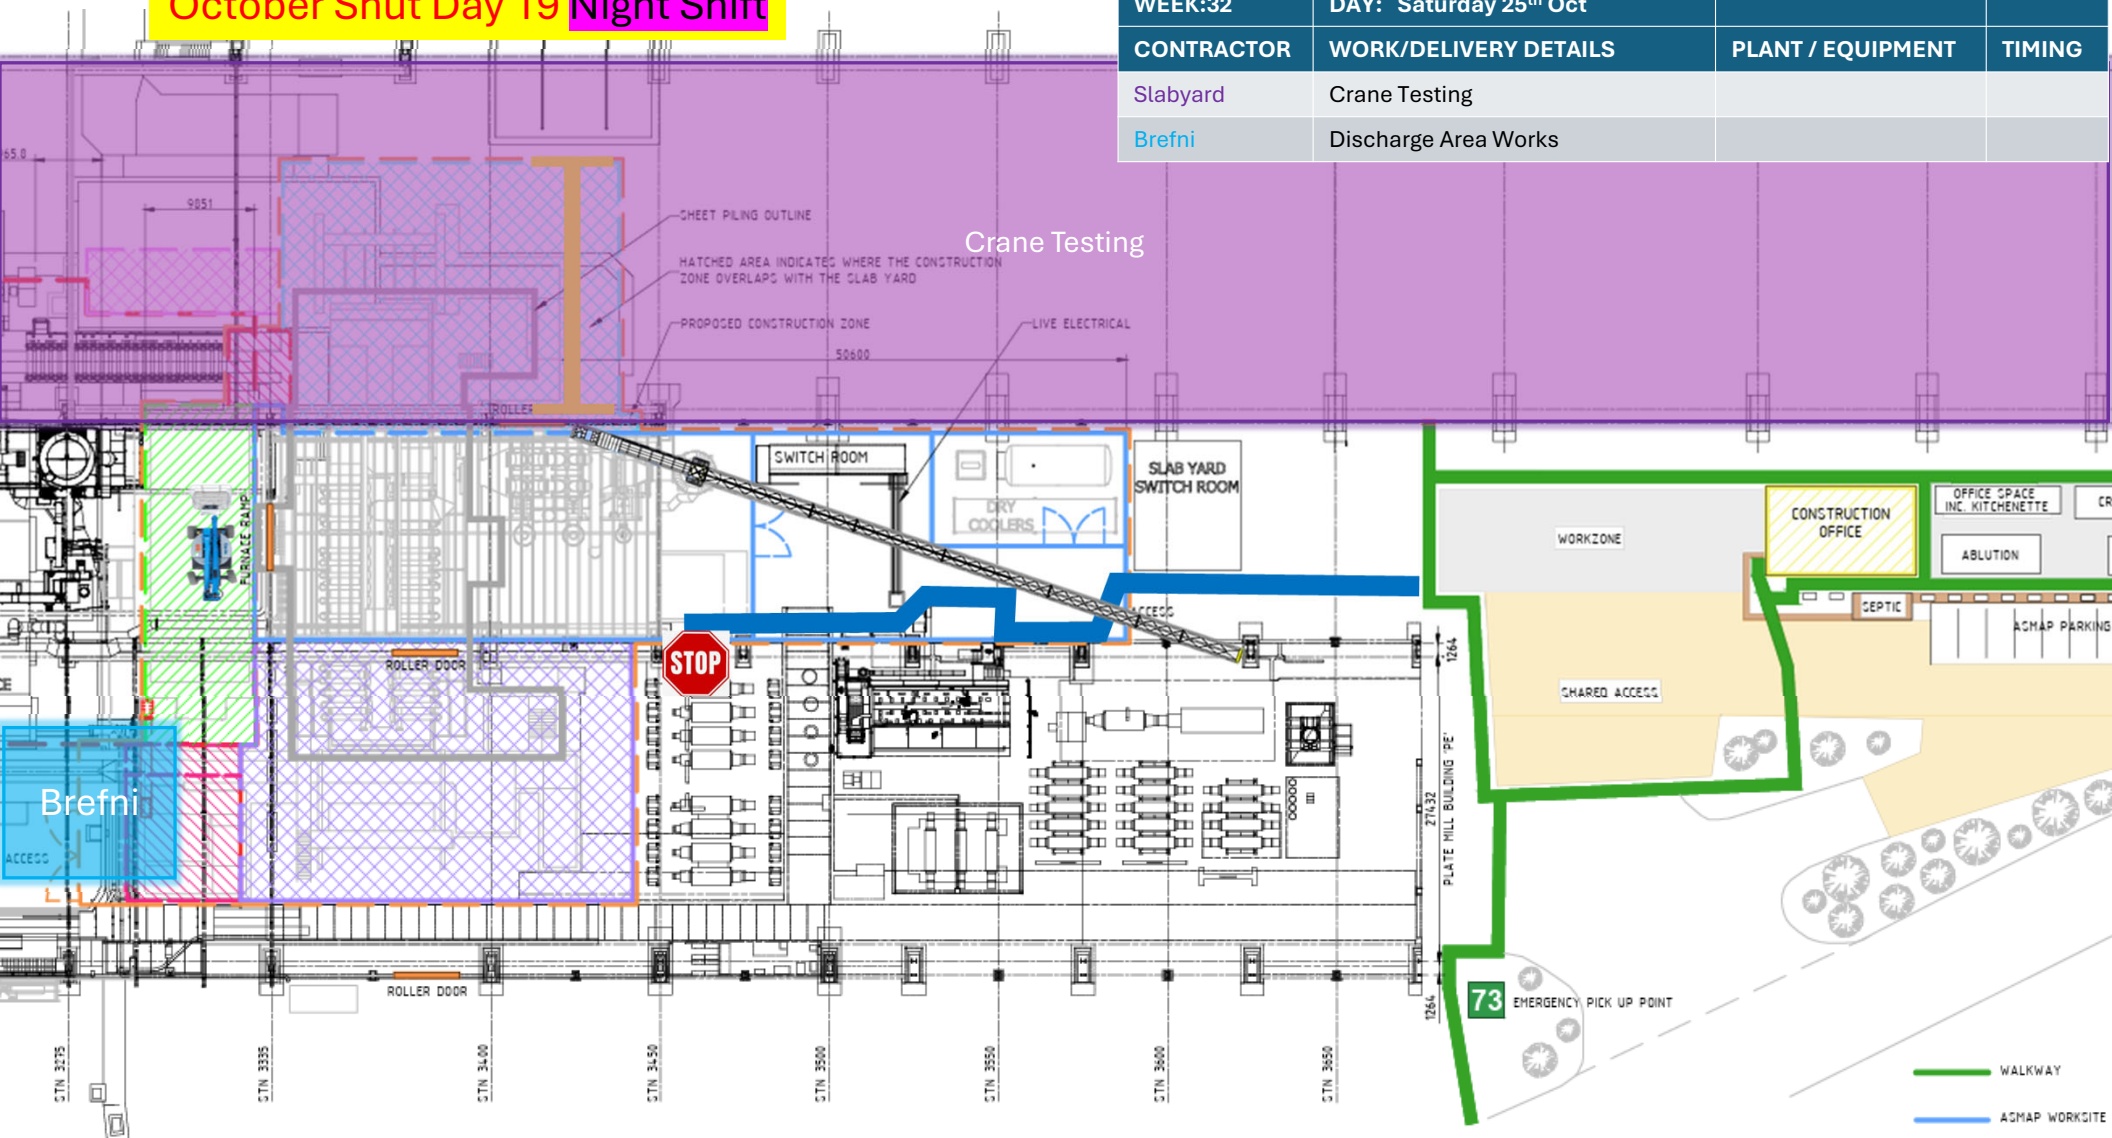

October Shut Day 20 Day Shift

WEEK:32	DAY: Sunday 26 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Slabyard	Crane Testing		
Brefni	Discharge Area Works		

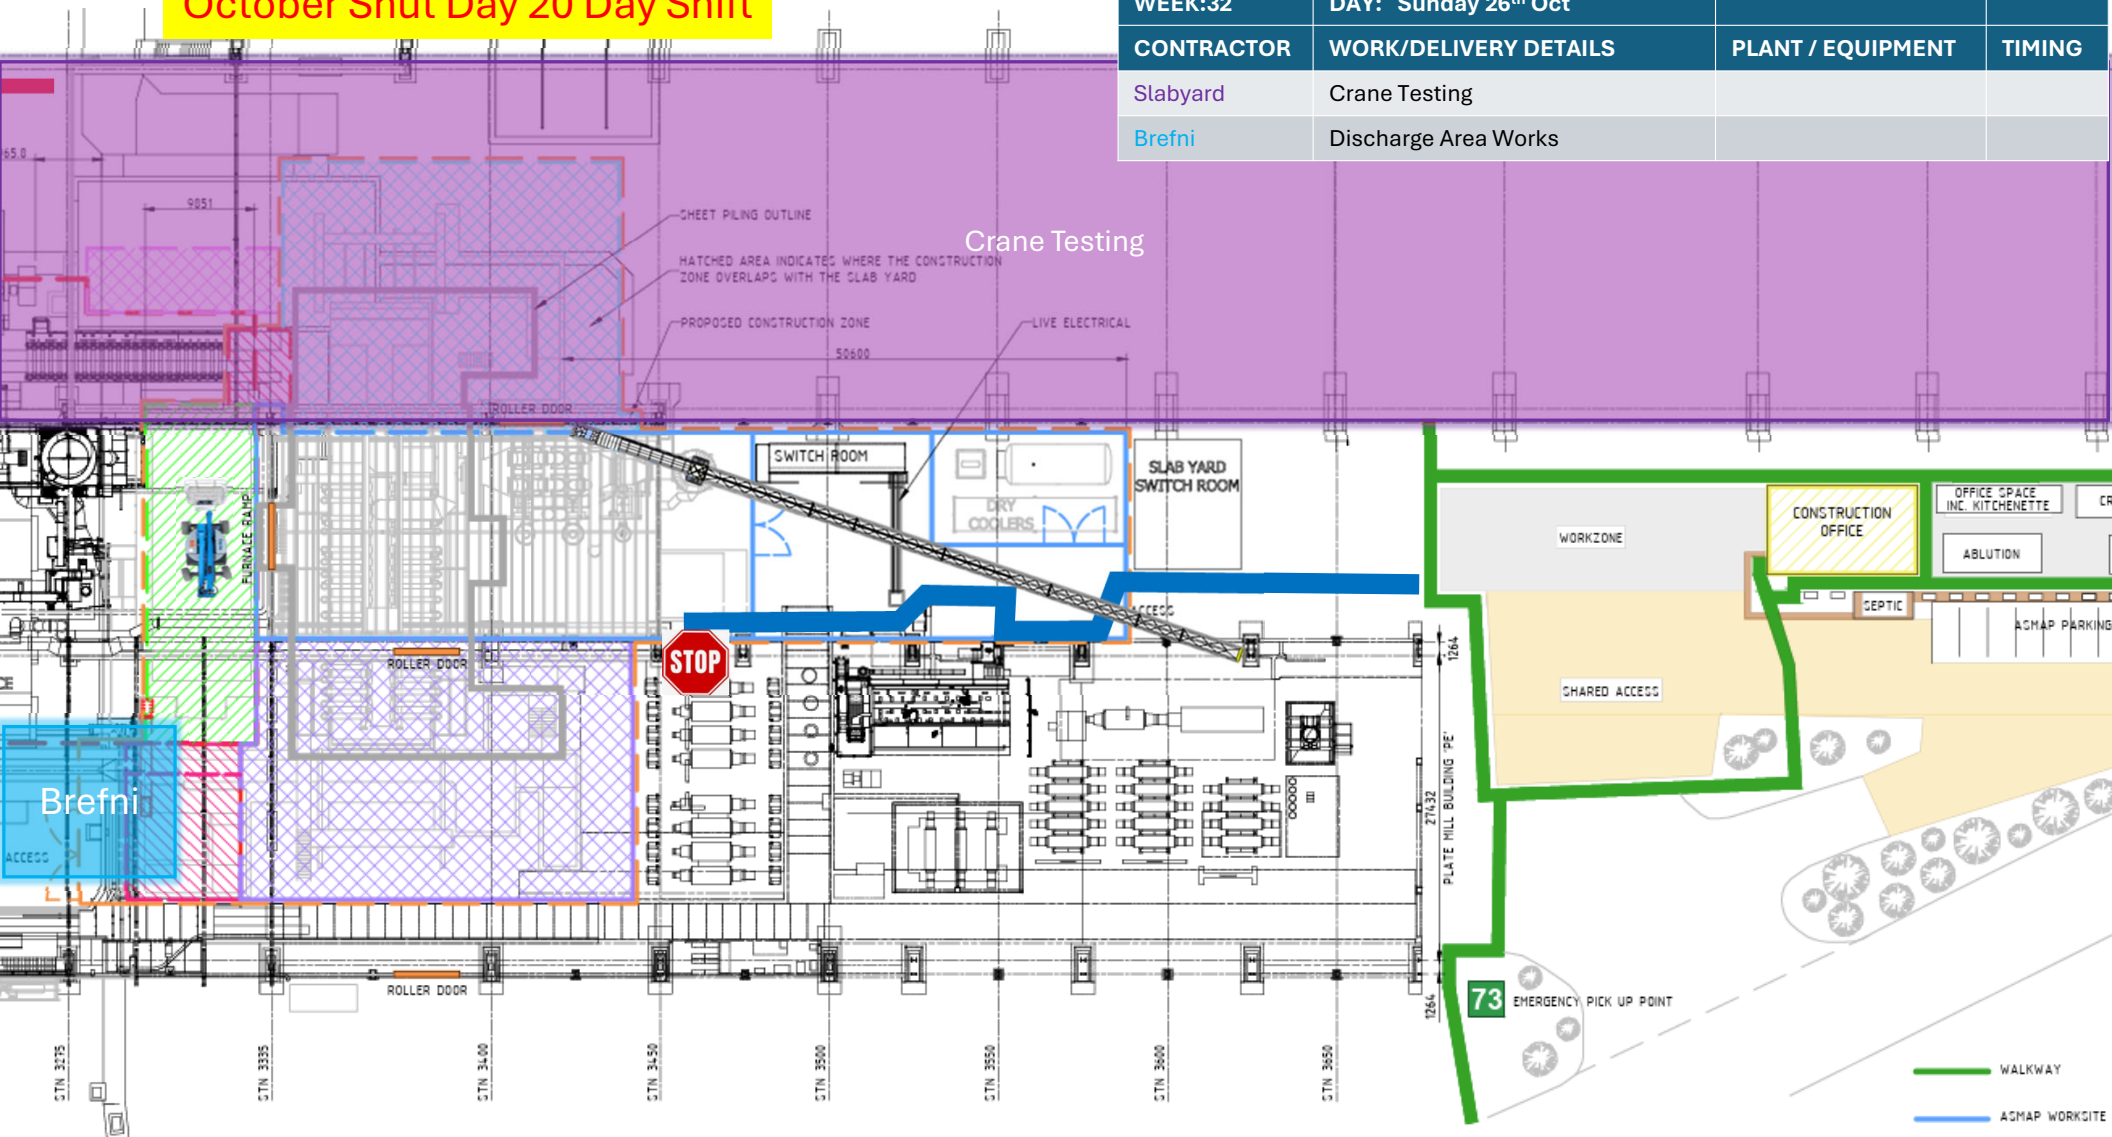

October Shut Day 20 Night Shift

WEEK:32	DAY: Sunday 26 th Oct		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Slabyard	Crane Testing		
Brefni	Discharge Area Works		

