


Day Shift

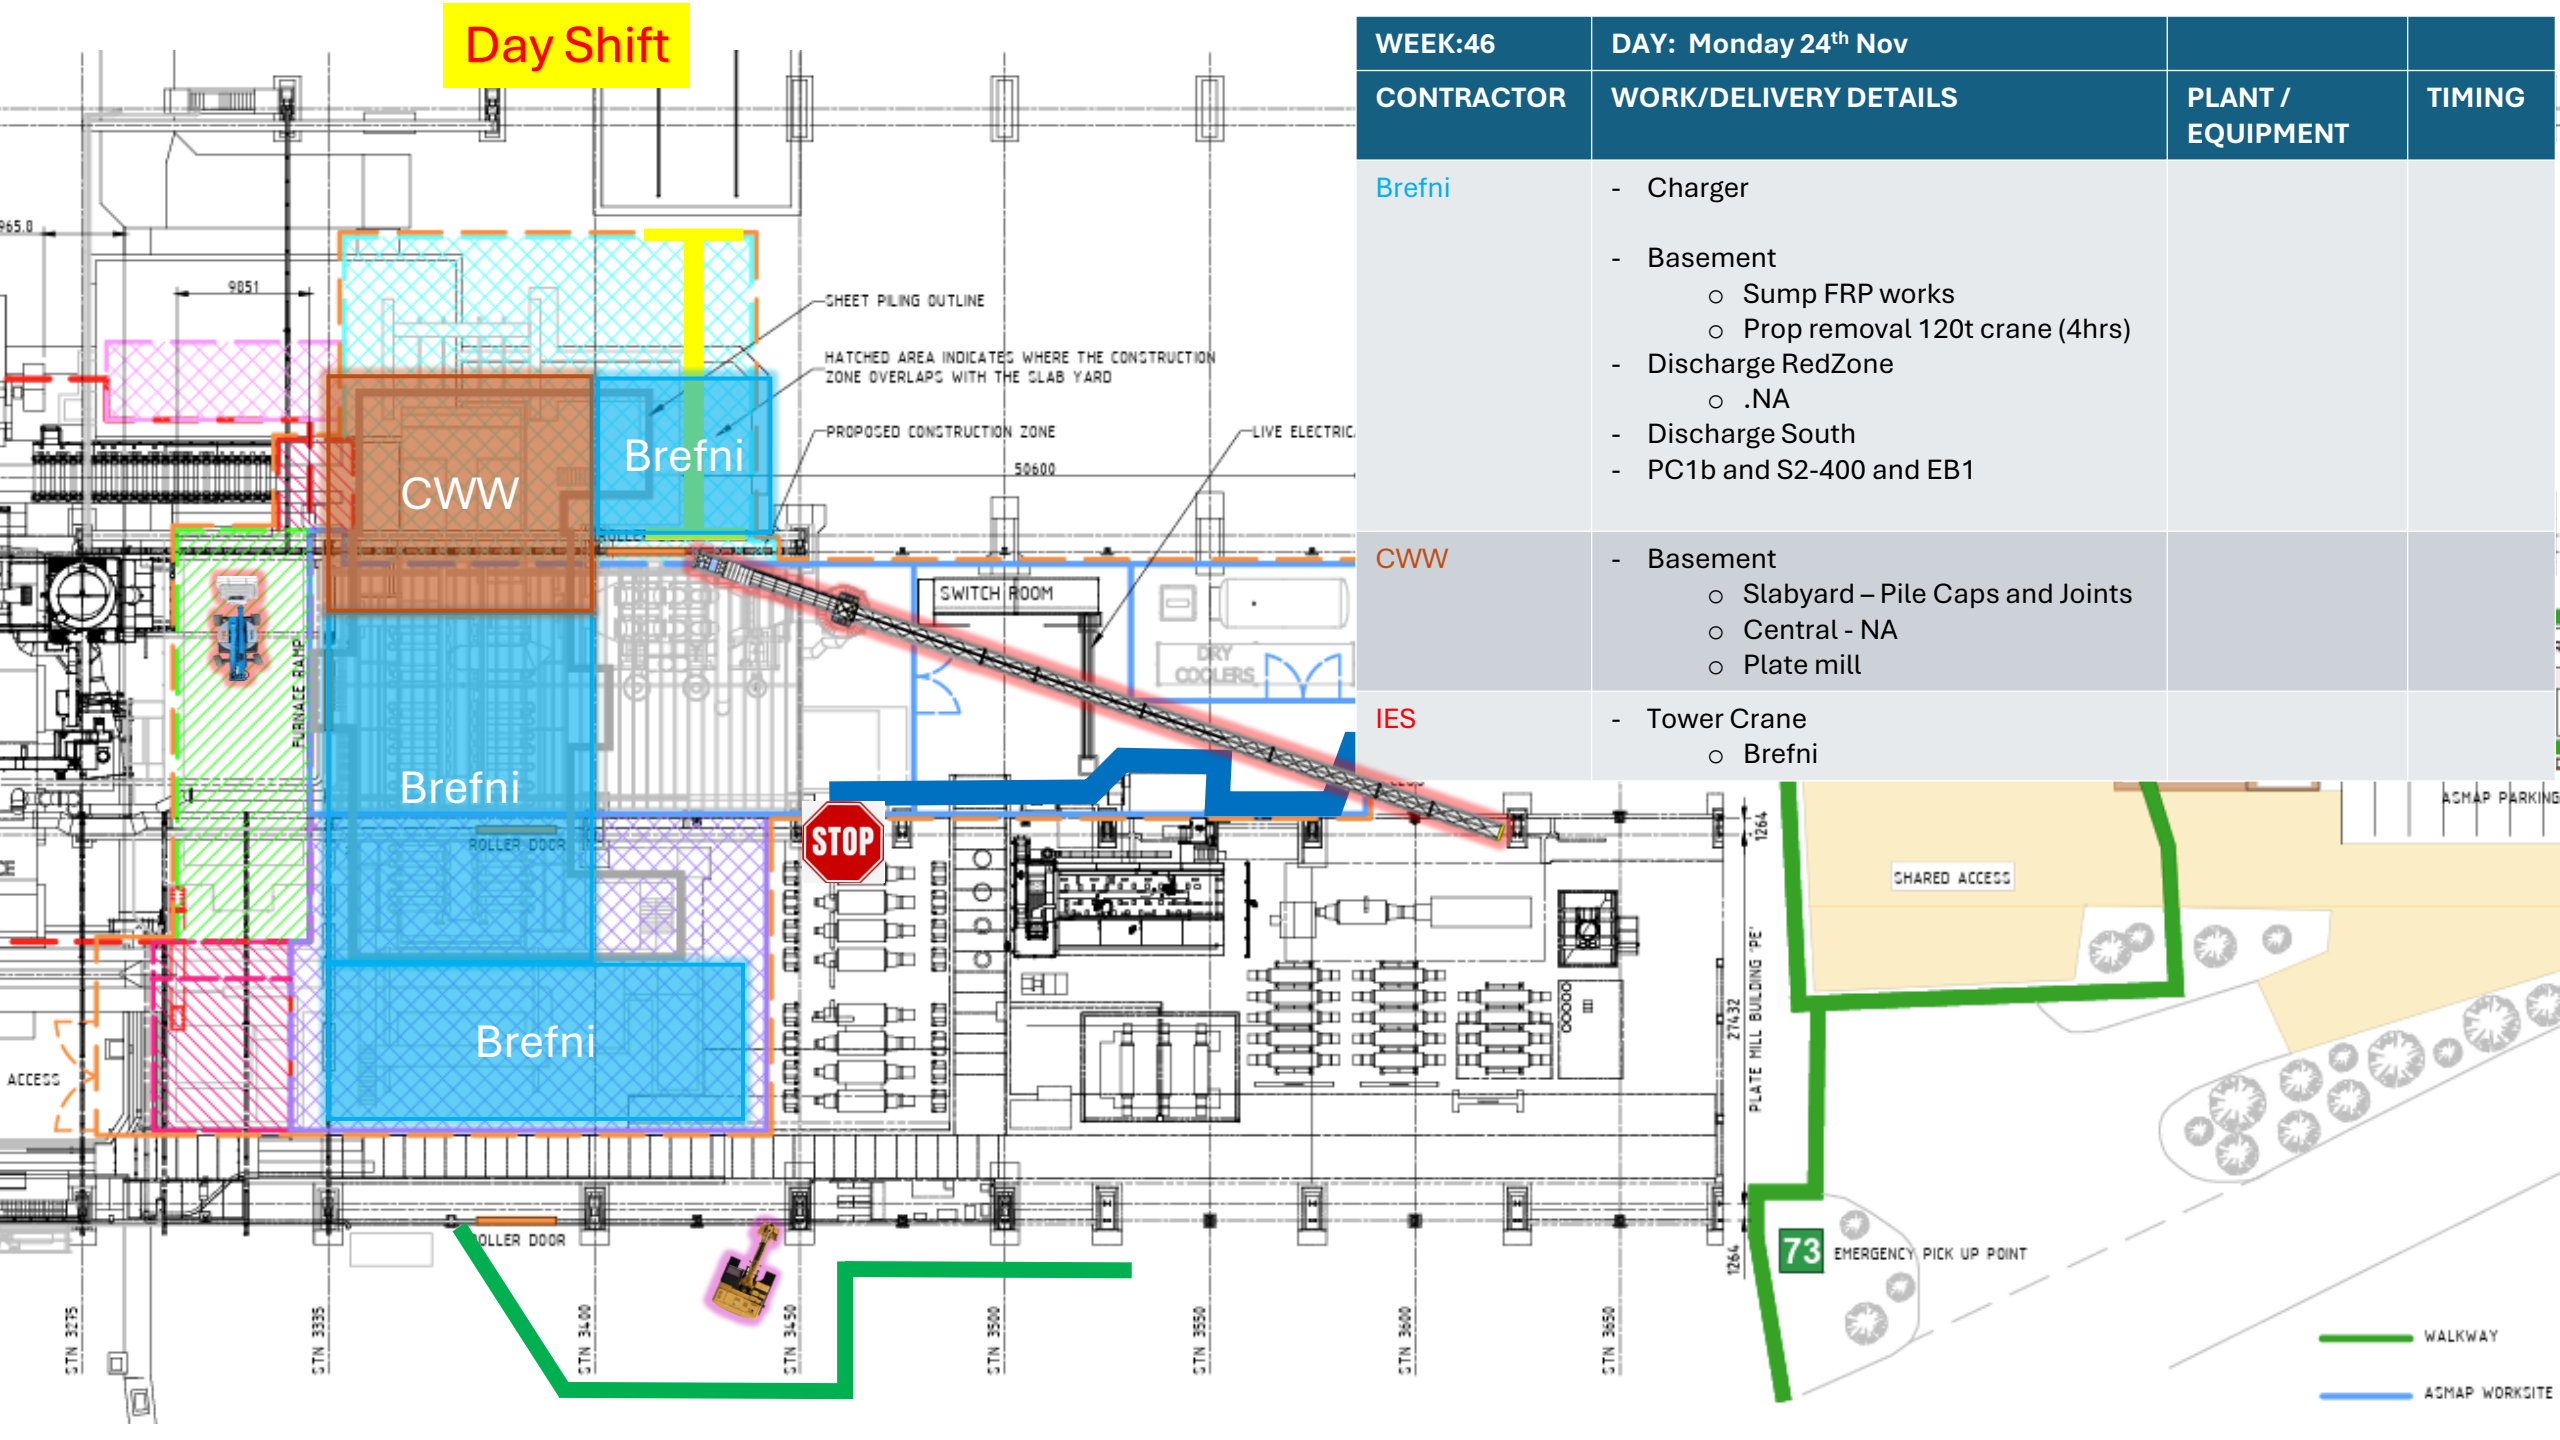


WEEK:46	DAY: Monday 24 th Nov		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	<ul style="list-style-type: none"> - Charger - Basement <ul style="list-style-type: none"> o Sump FRP works o Prop removal 120t crane (4hrs) - Discharge RedZone <ul style="list-style-type: none"> o .NA - Discharge South - PC1b and S2-400 and EB1 		
CWW	<ul style="list-style-type: none"> - Basement <ul style="list-style-type: none"> o Slabyard – Pile Caps and Joints o Central - NA o Plate mill 		
IES	<ul style="list-style-type: none"> - Tower Crane <ul style="list-style-type: none"> o Brefni 		


WALKWAY
ASMAP WORKSITE

Night Shift

WEEK:46	DAY: Monday 24 th Nov		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING

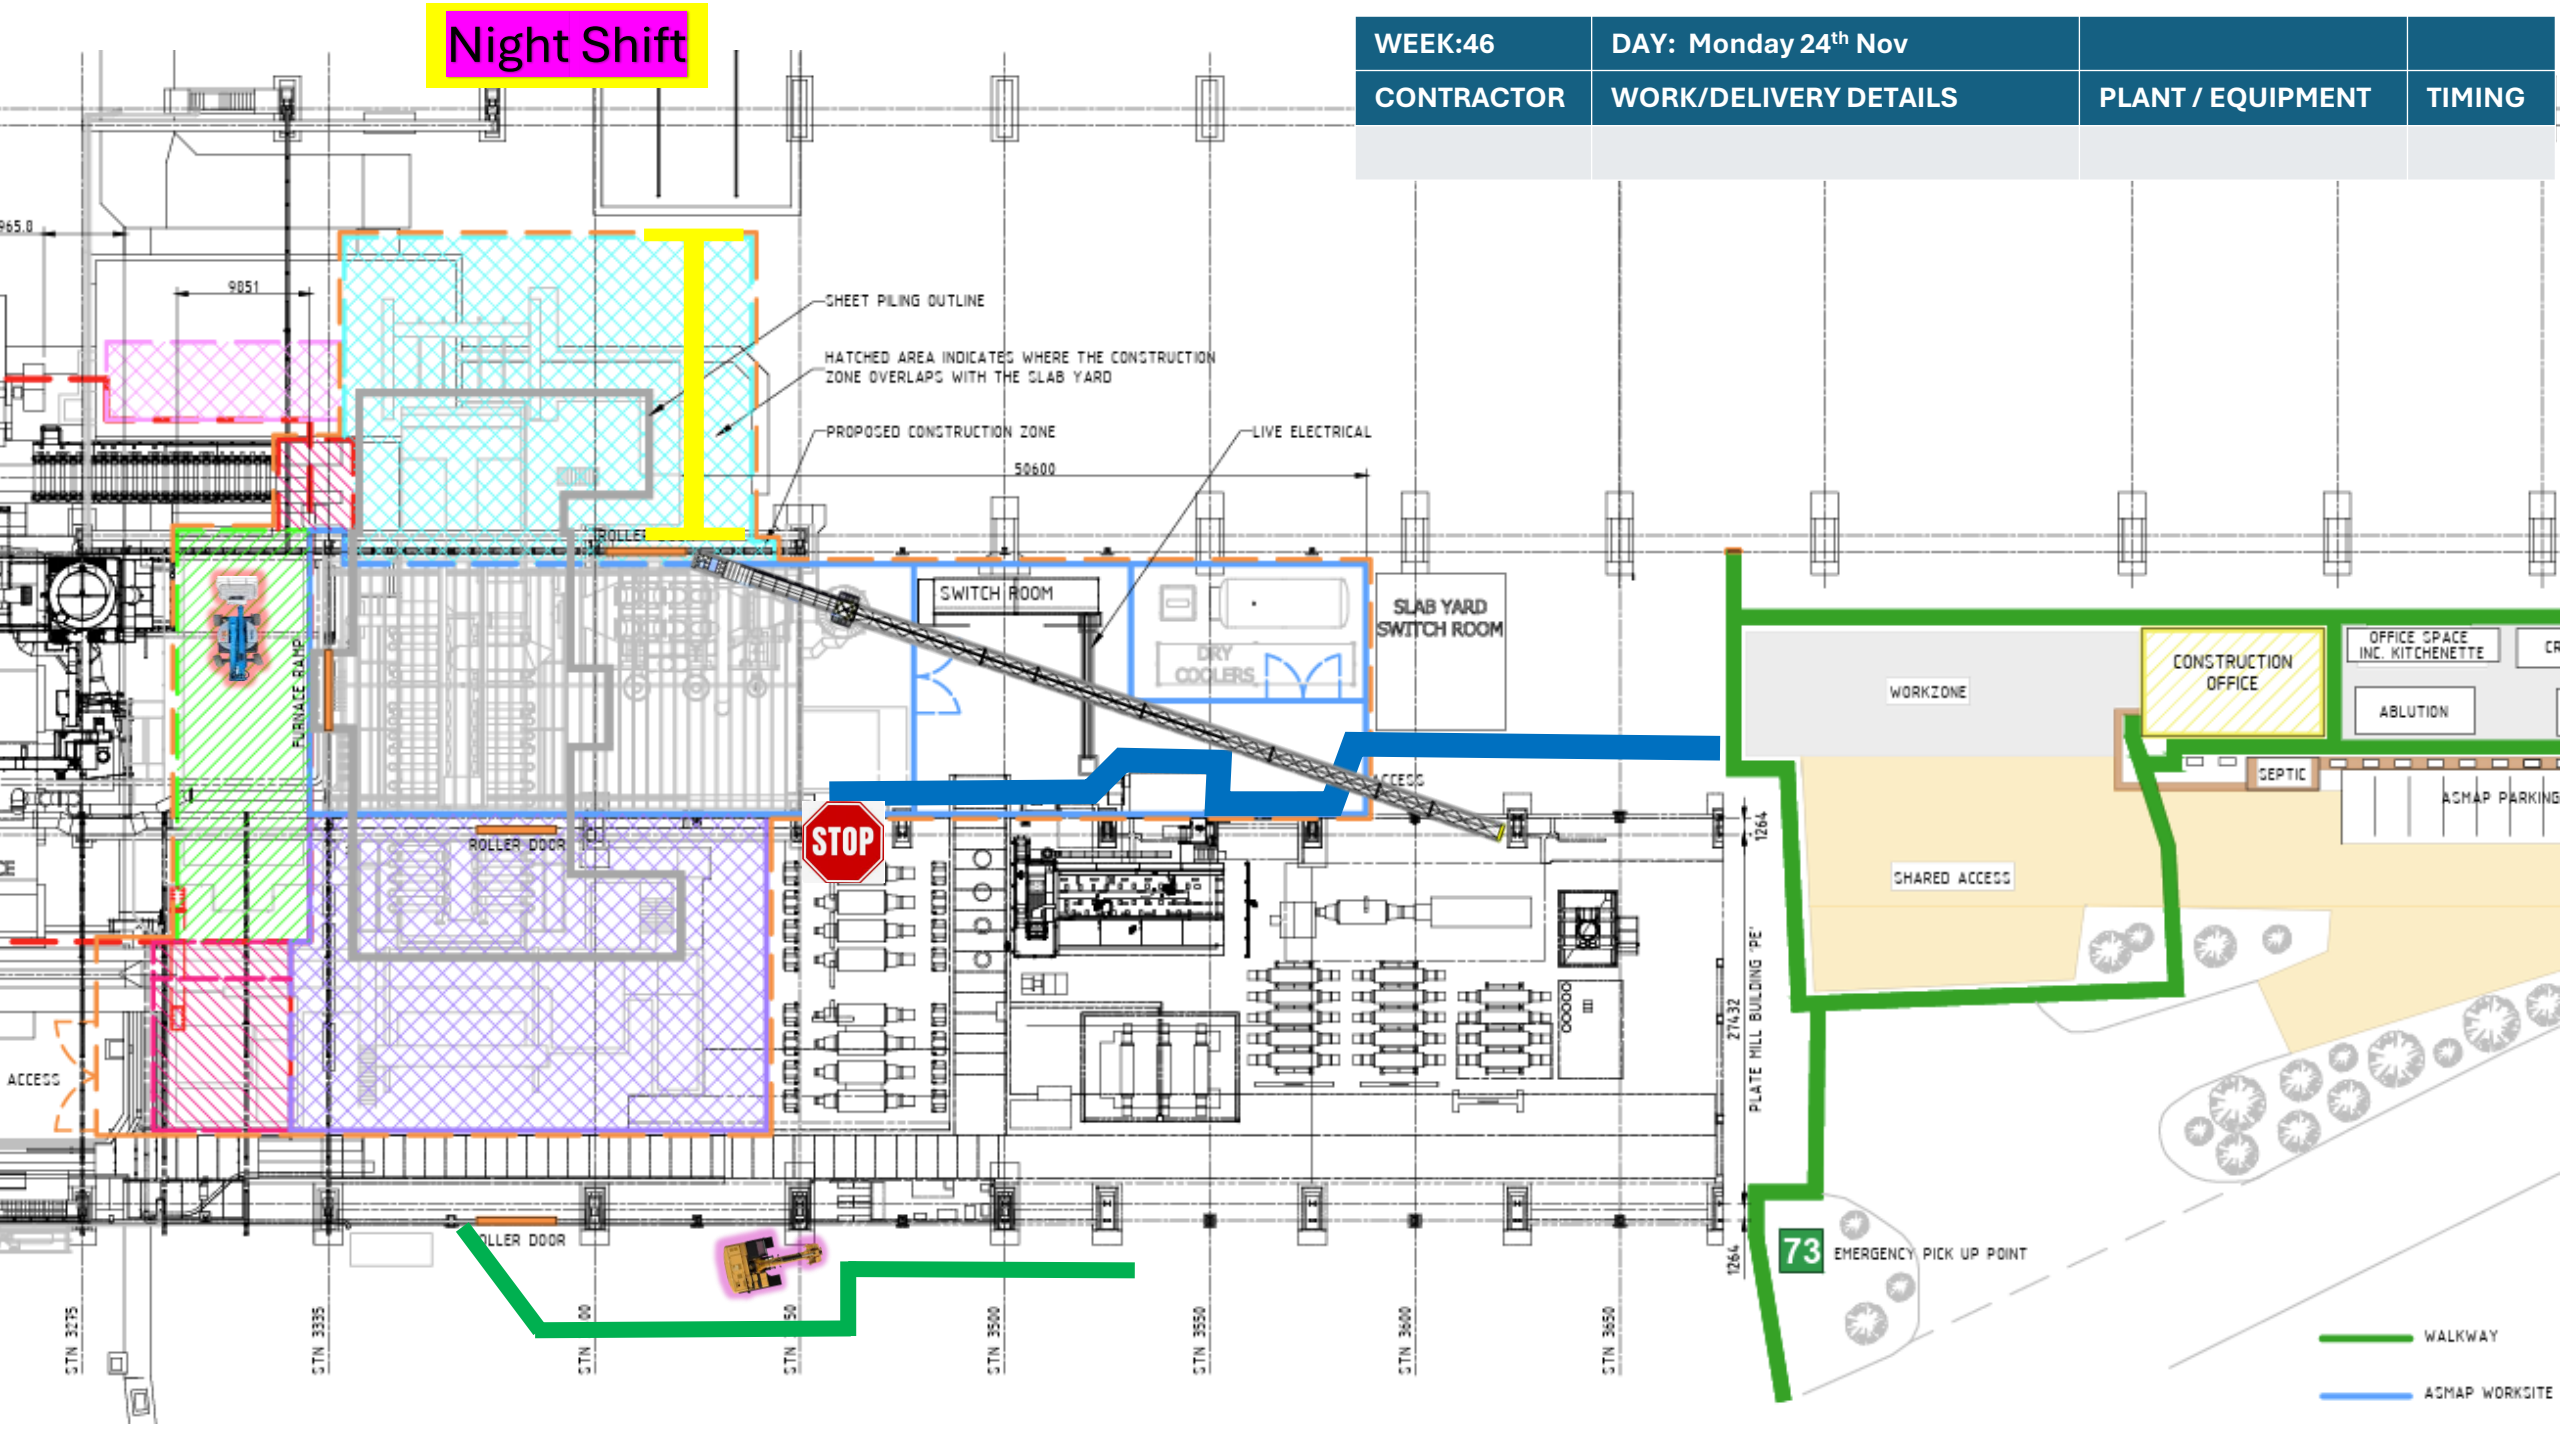


Day Shift

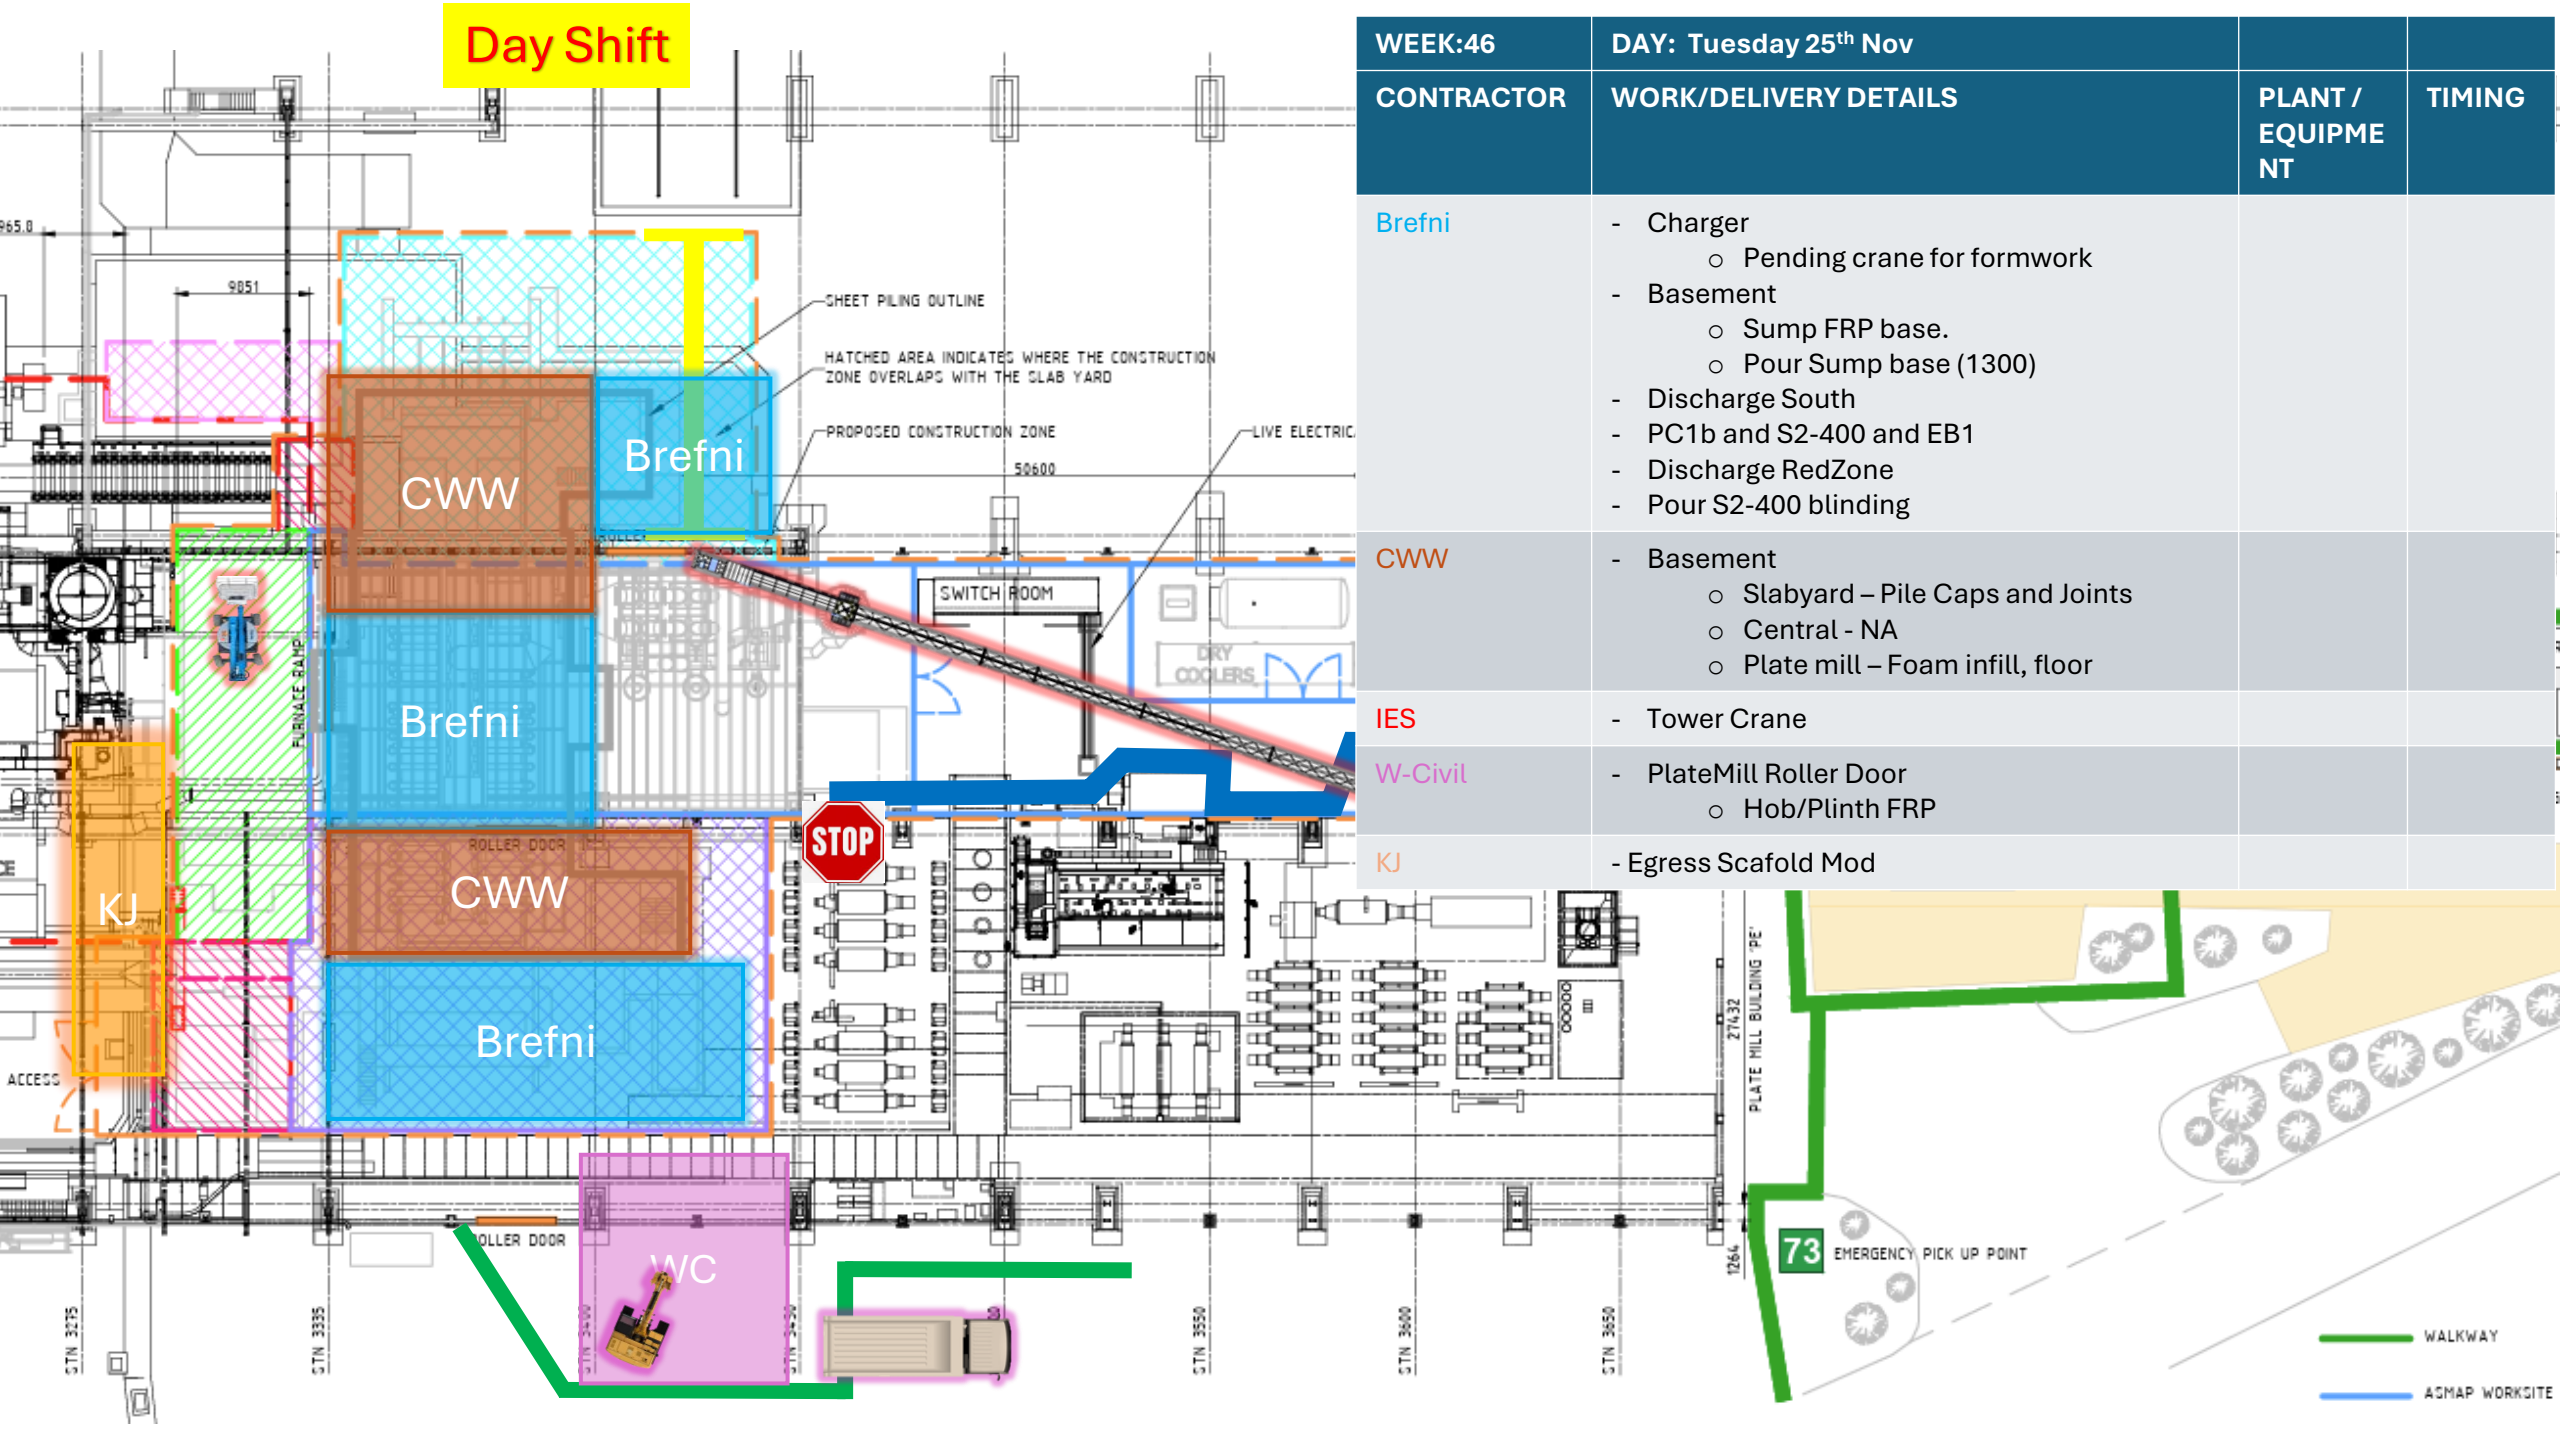


WEEK:46	DAY: Tuesday 25 th Nov		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPME NT	TIMING
Brefni	<ul style="list-style-type: none">- Charger<ul style="list-style-type: none">o Pending crane for formwork- Basement<ul style="list-style-type: none">o Sump FRP base.o Pour Sump base (1300)- Discharge South- PC1b and S2-400 and EB1- Discharge RedZone- Pour S2-400 blinding		
CWW	<ul style="list-style-type: none">- Basement<ul style="list-style-type: none">o Slabyard – Pile Caps and Jointso Central - NAo Plate mill – Foam infill, floor		
IES	<ul style="list-style-type: none">- Tower Crane		
W-Civil	<ul style="list-style-type: none">- PlateMill Roller Door<ul style="list-style-type: none">o Hob/Plinth FRP		
KJ	<ul style="list-style-type: none">- Egress Scaffold Mod		

Night Shift

WEEK:46	DAY: Tuesday 25 th Nov		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	<ul style="list-style-type: none">- Basement<ul style="list-style-type: none">o Load in reo central		NS 1600 – 0200
IES	<ul style="list-style-type: none">- Tower Crane<ul style="list-style-type: none">o Brefni		2000 finish

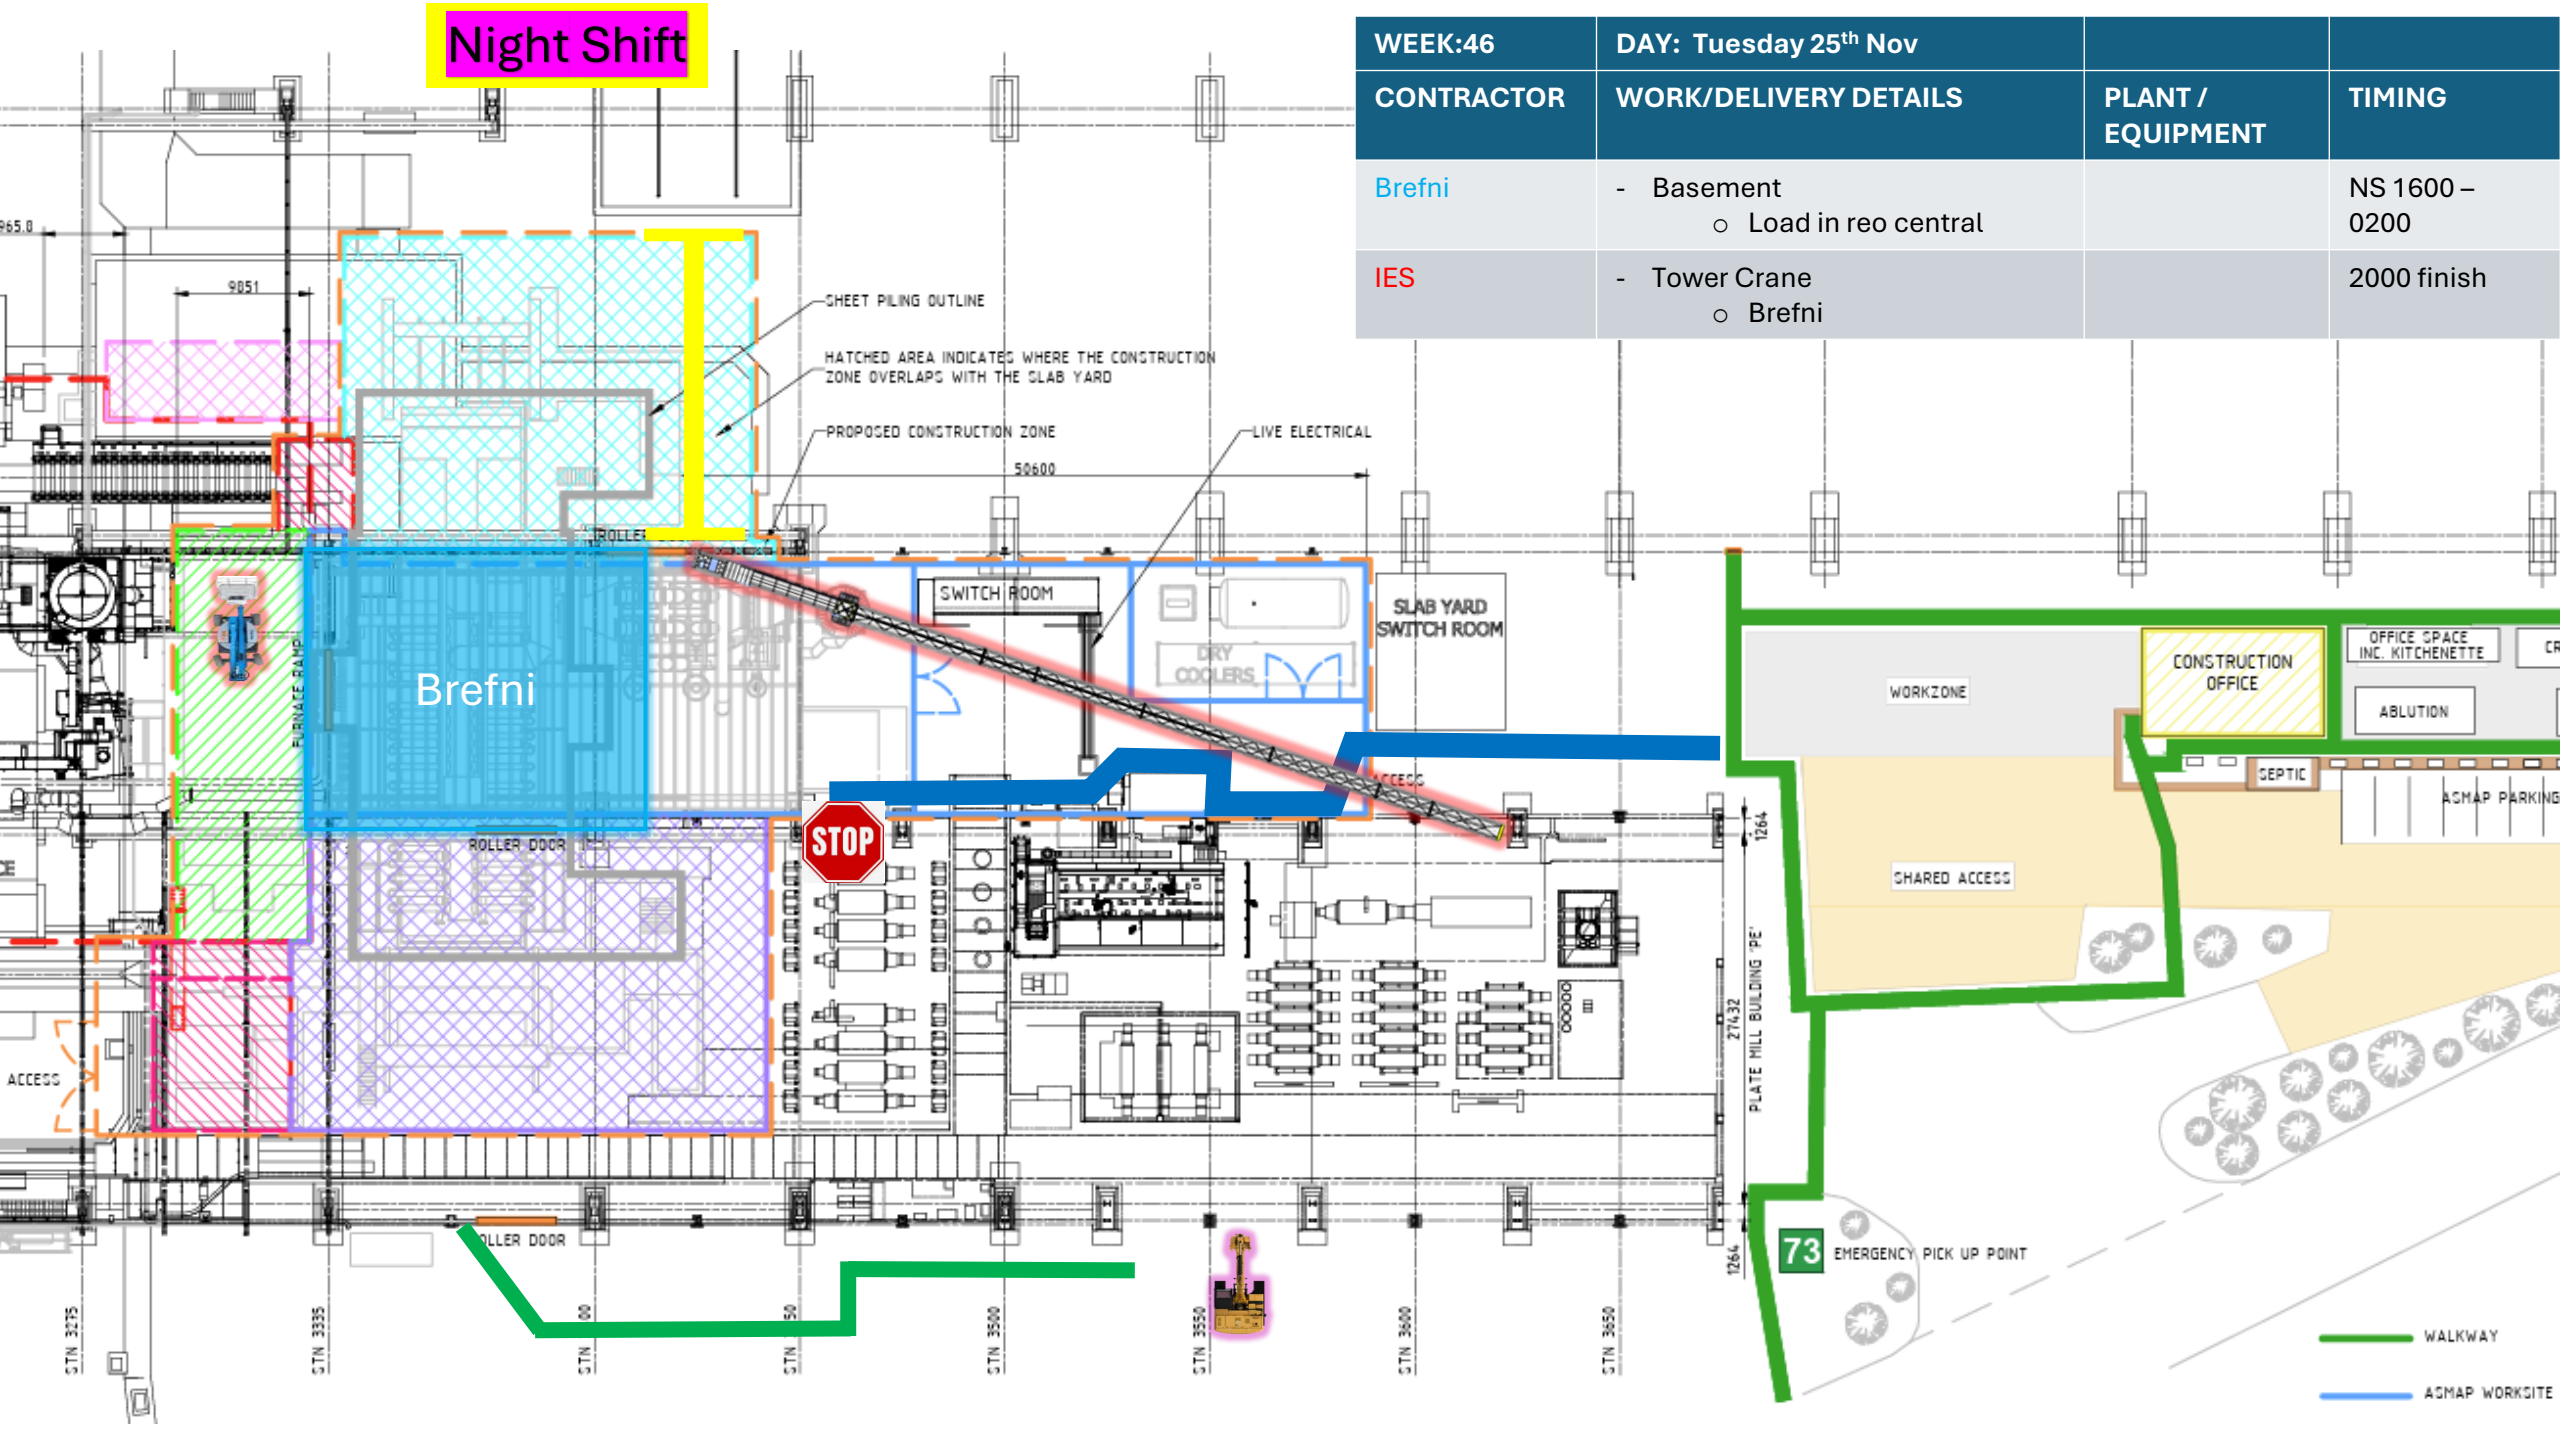


Day Shift

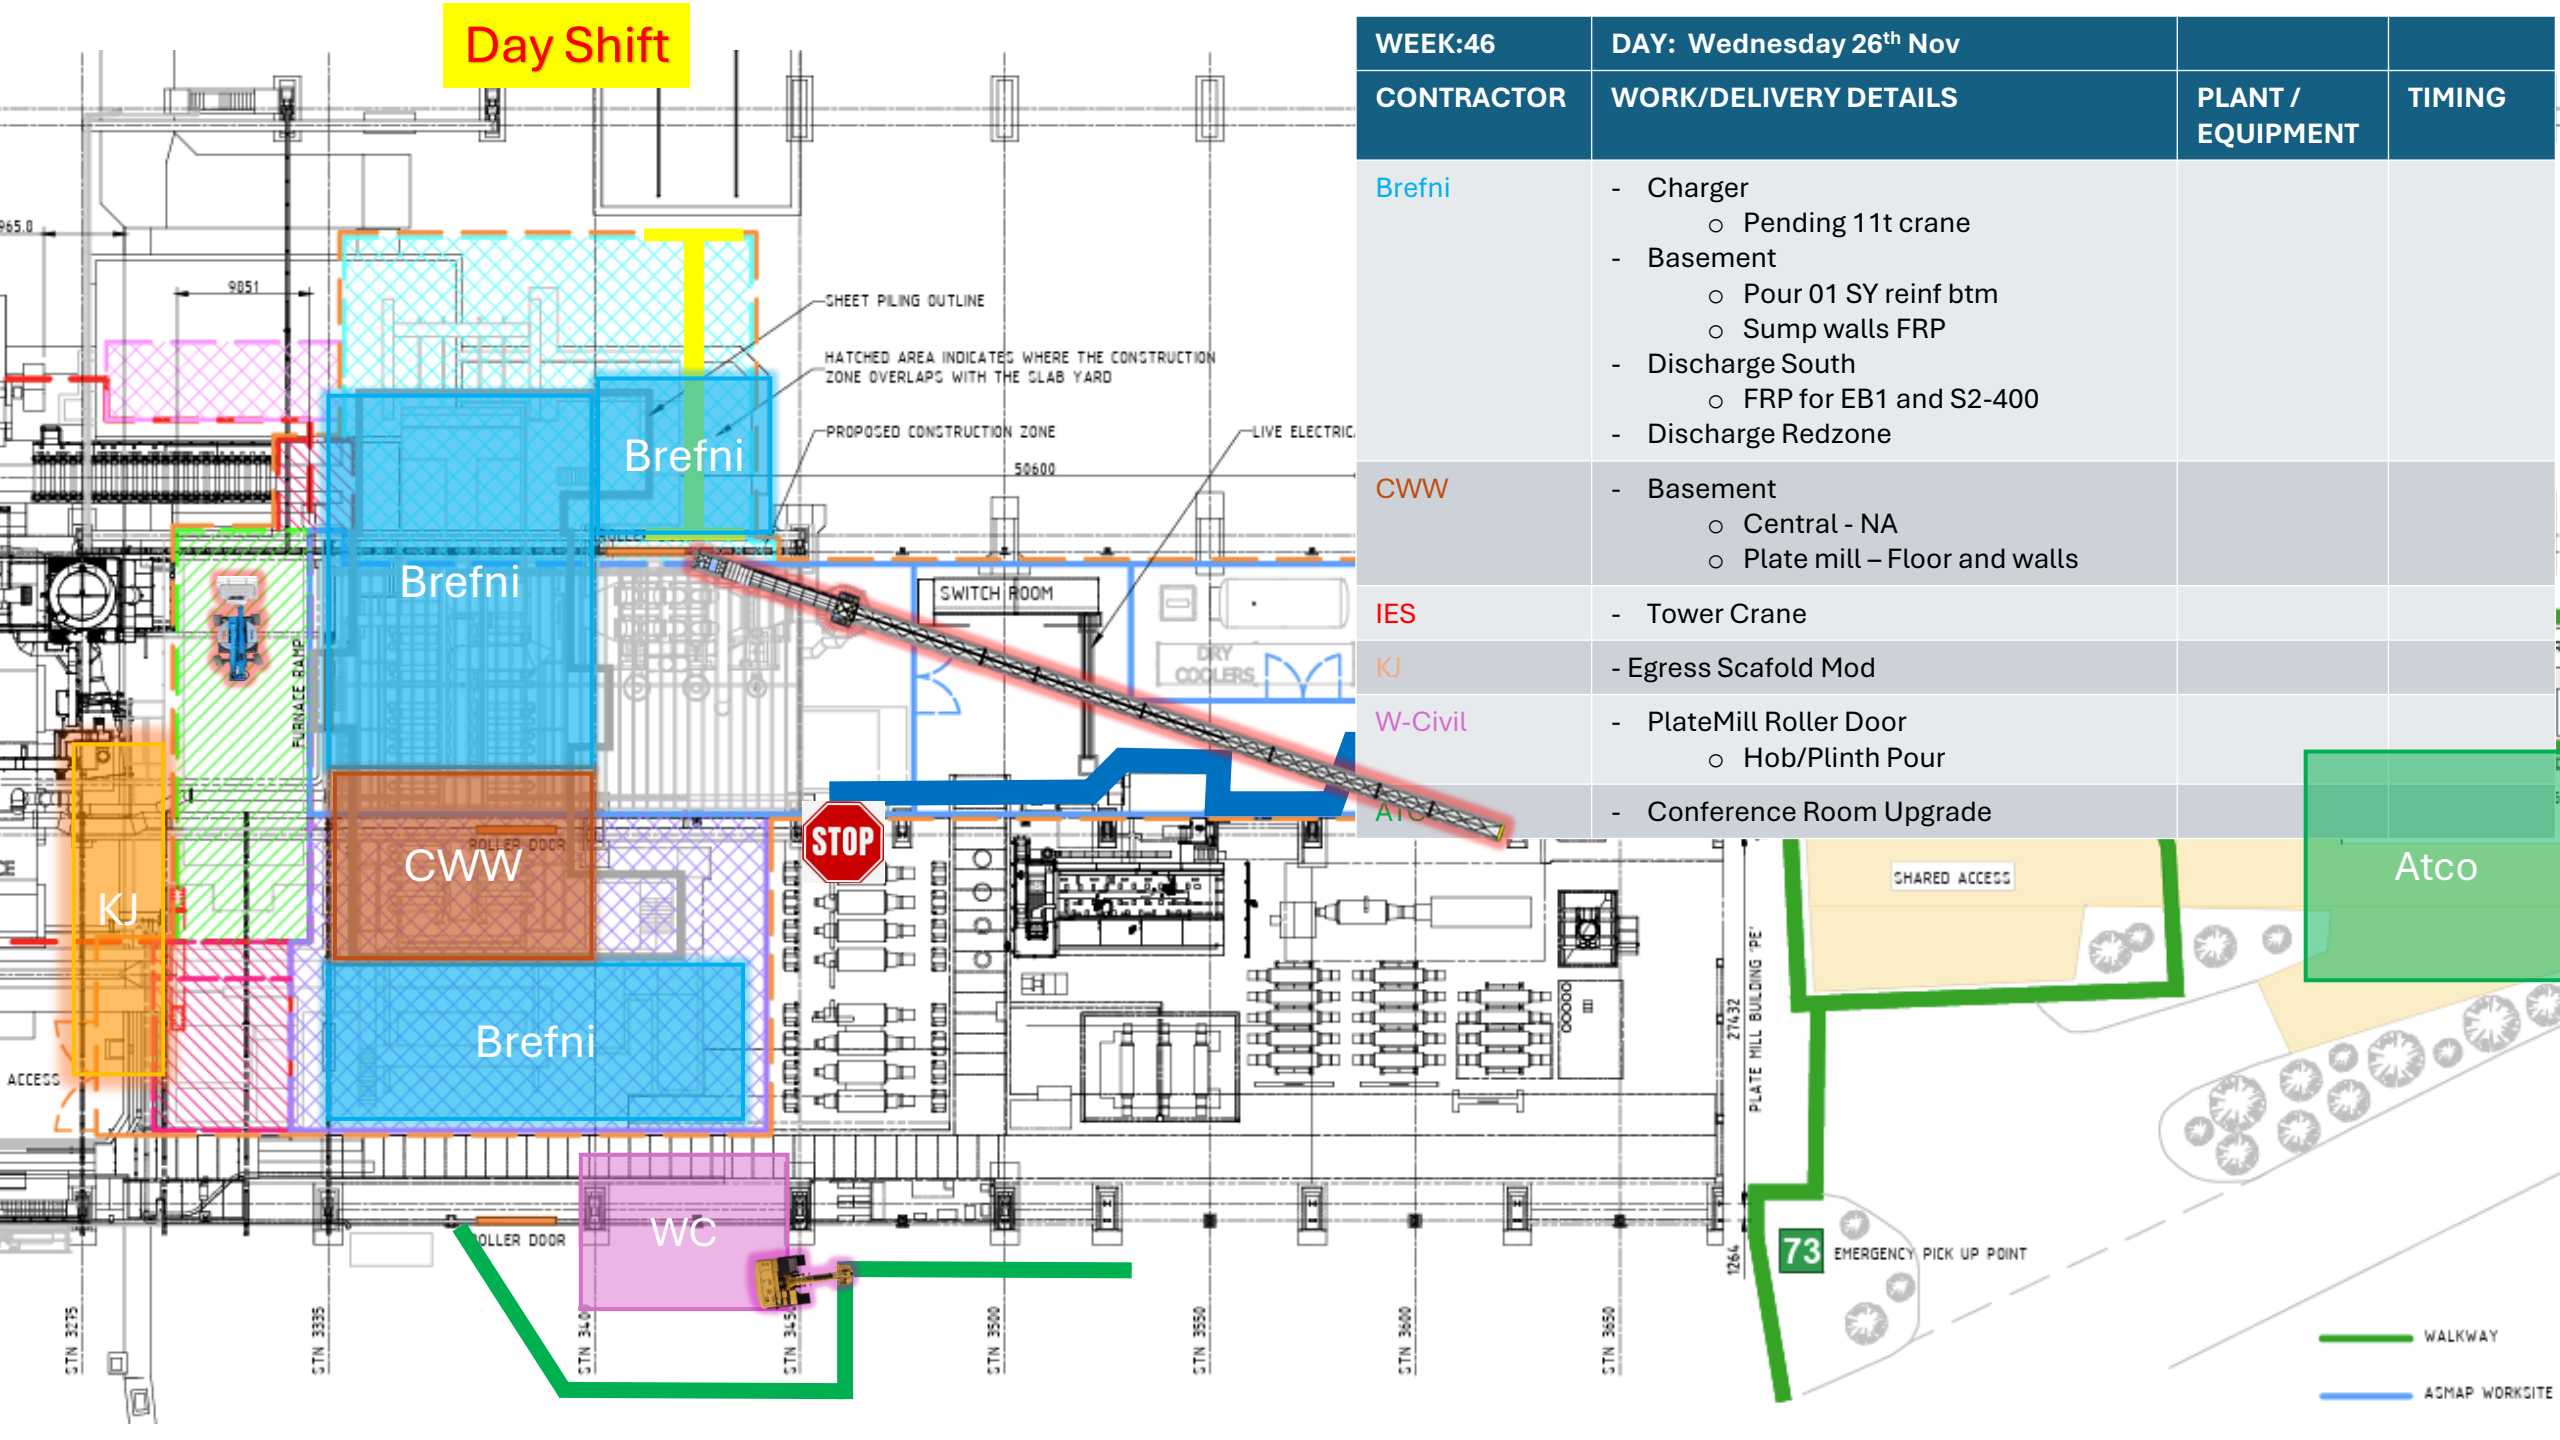

WEEK:46	DAY: Wednesday 26 th Nov		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	<ul style="list-style-type: none"> - Charger <ul style="list-style-type: none"> o Pending 11t crane - Basement <ul style="list-style-type: none"> o Pour 01 SY reinf btm o Sump walls FRP - Discharge South <ul style="list-style-type: none"> o FRP for EB1 and S2-400 - Discharge Redzone 		
CWW	<ul style="list-style-type: none"> - Basement <ul style="list-style-type: none"> o Central - NA o Plate mill – Floor and walls 		
IES	<ul style="list-style-type: none"> - Tower Crane 		
KJ	<ul style="list-style-type: none"> - Egress Scaffold Mod 		
W-Civil	<ul style="list-style-type: none"> - PlateMill Roller Door <ul style="list-style-type: none"> o Hob/Plinth Pour 		
Atco	<ul style="list-style-type: none"> - Conference Room Upgrade 		


Night Shift

WEEK:46	DAY: Wednesday 26 th Nov		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	<ul style="list-style-type: none">- Basement<ul style="list-style-type: none">o Sump Workso FRP Slabyard		1600 – 0200 shift
IES	<ul style="list-style-type: none">- Tower Crane<ul style="list-style-type: none">o Brefni		2000 finish

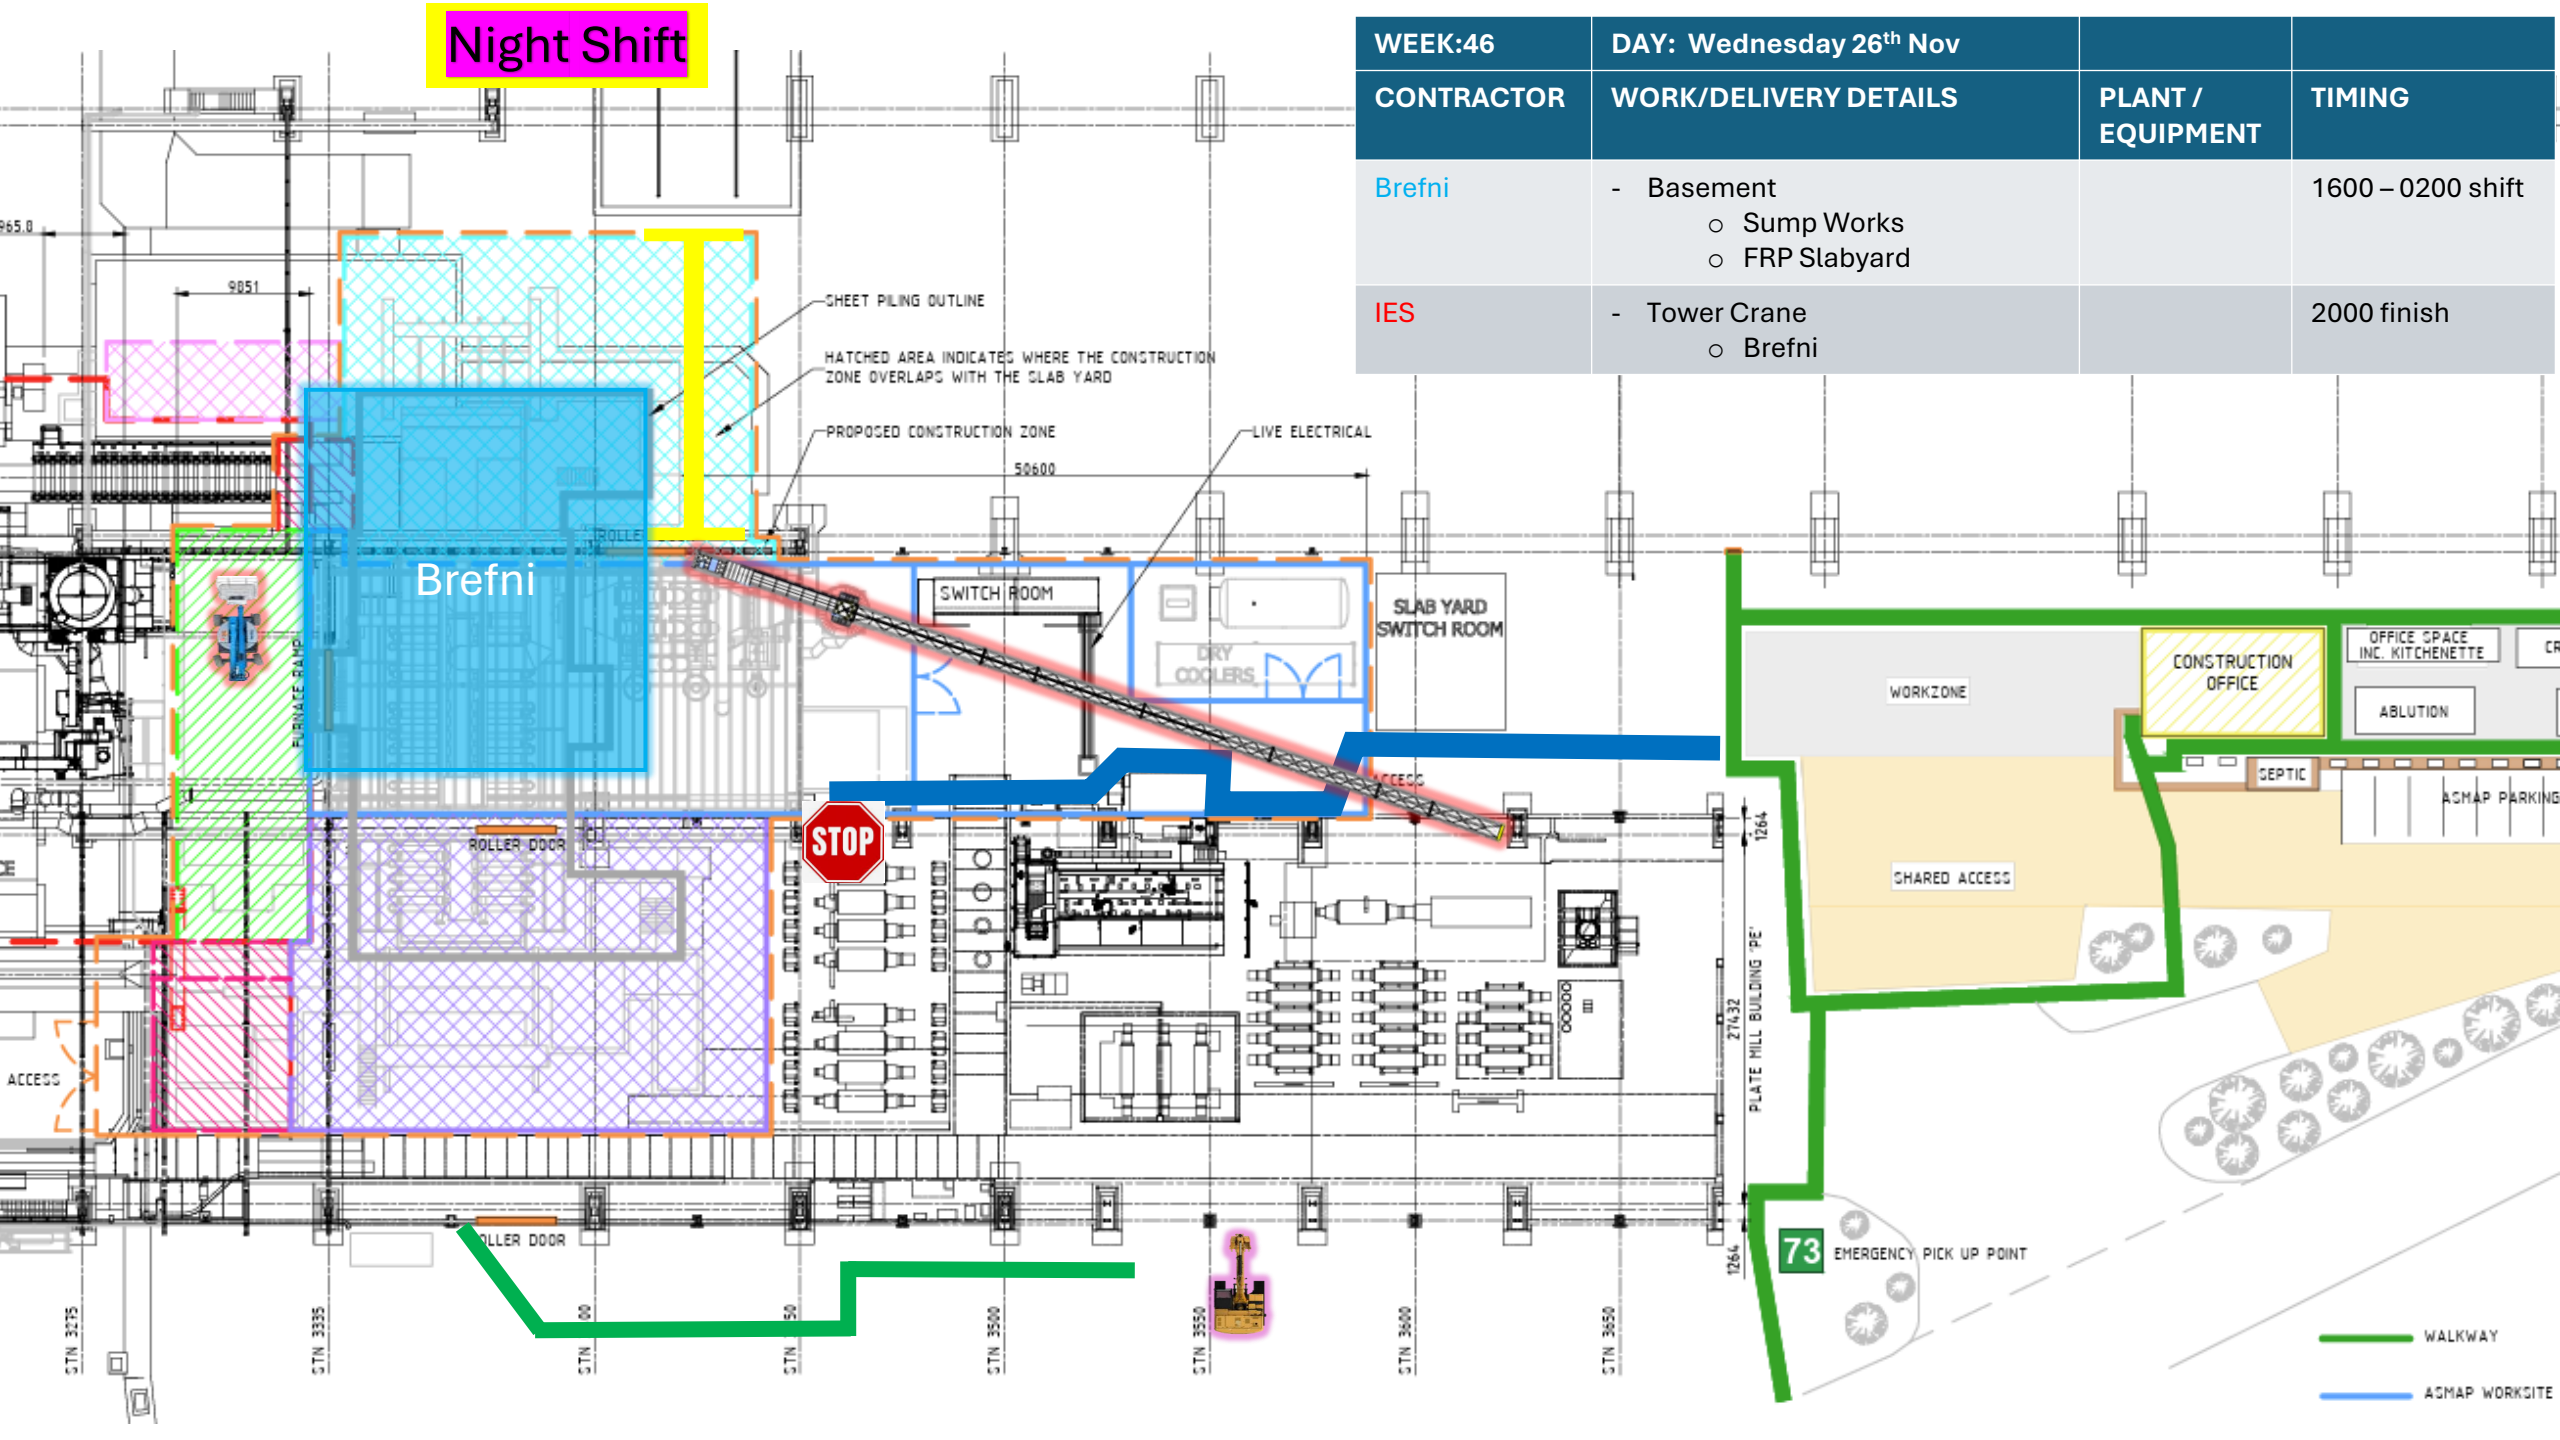


Night Shift

WEEK:46	DAY: Friday 28 th Nov		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
Brefni	- Basement o FRP Slabyard		

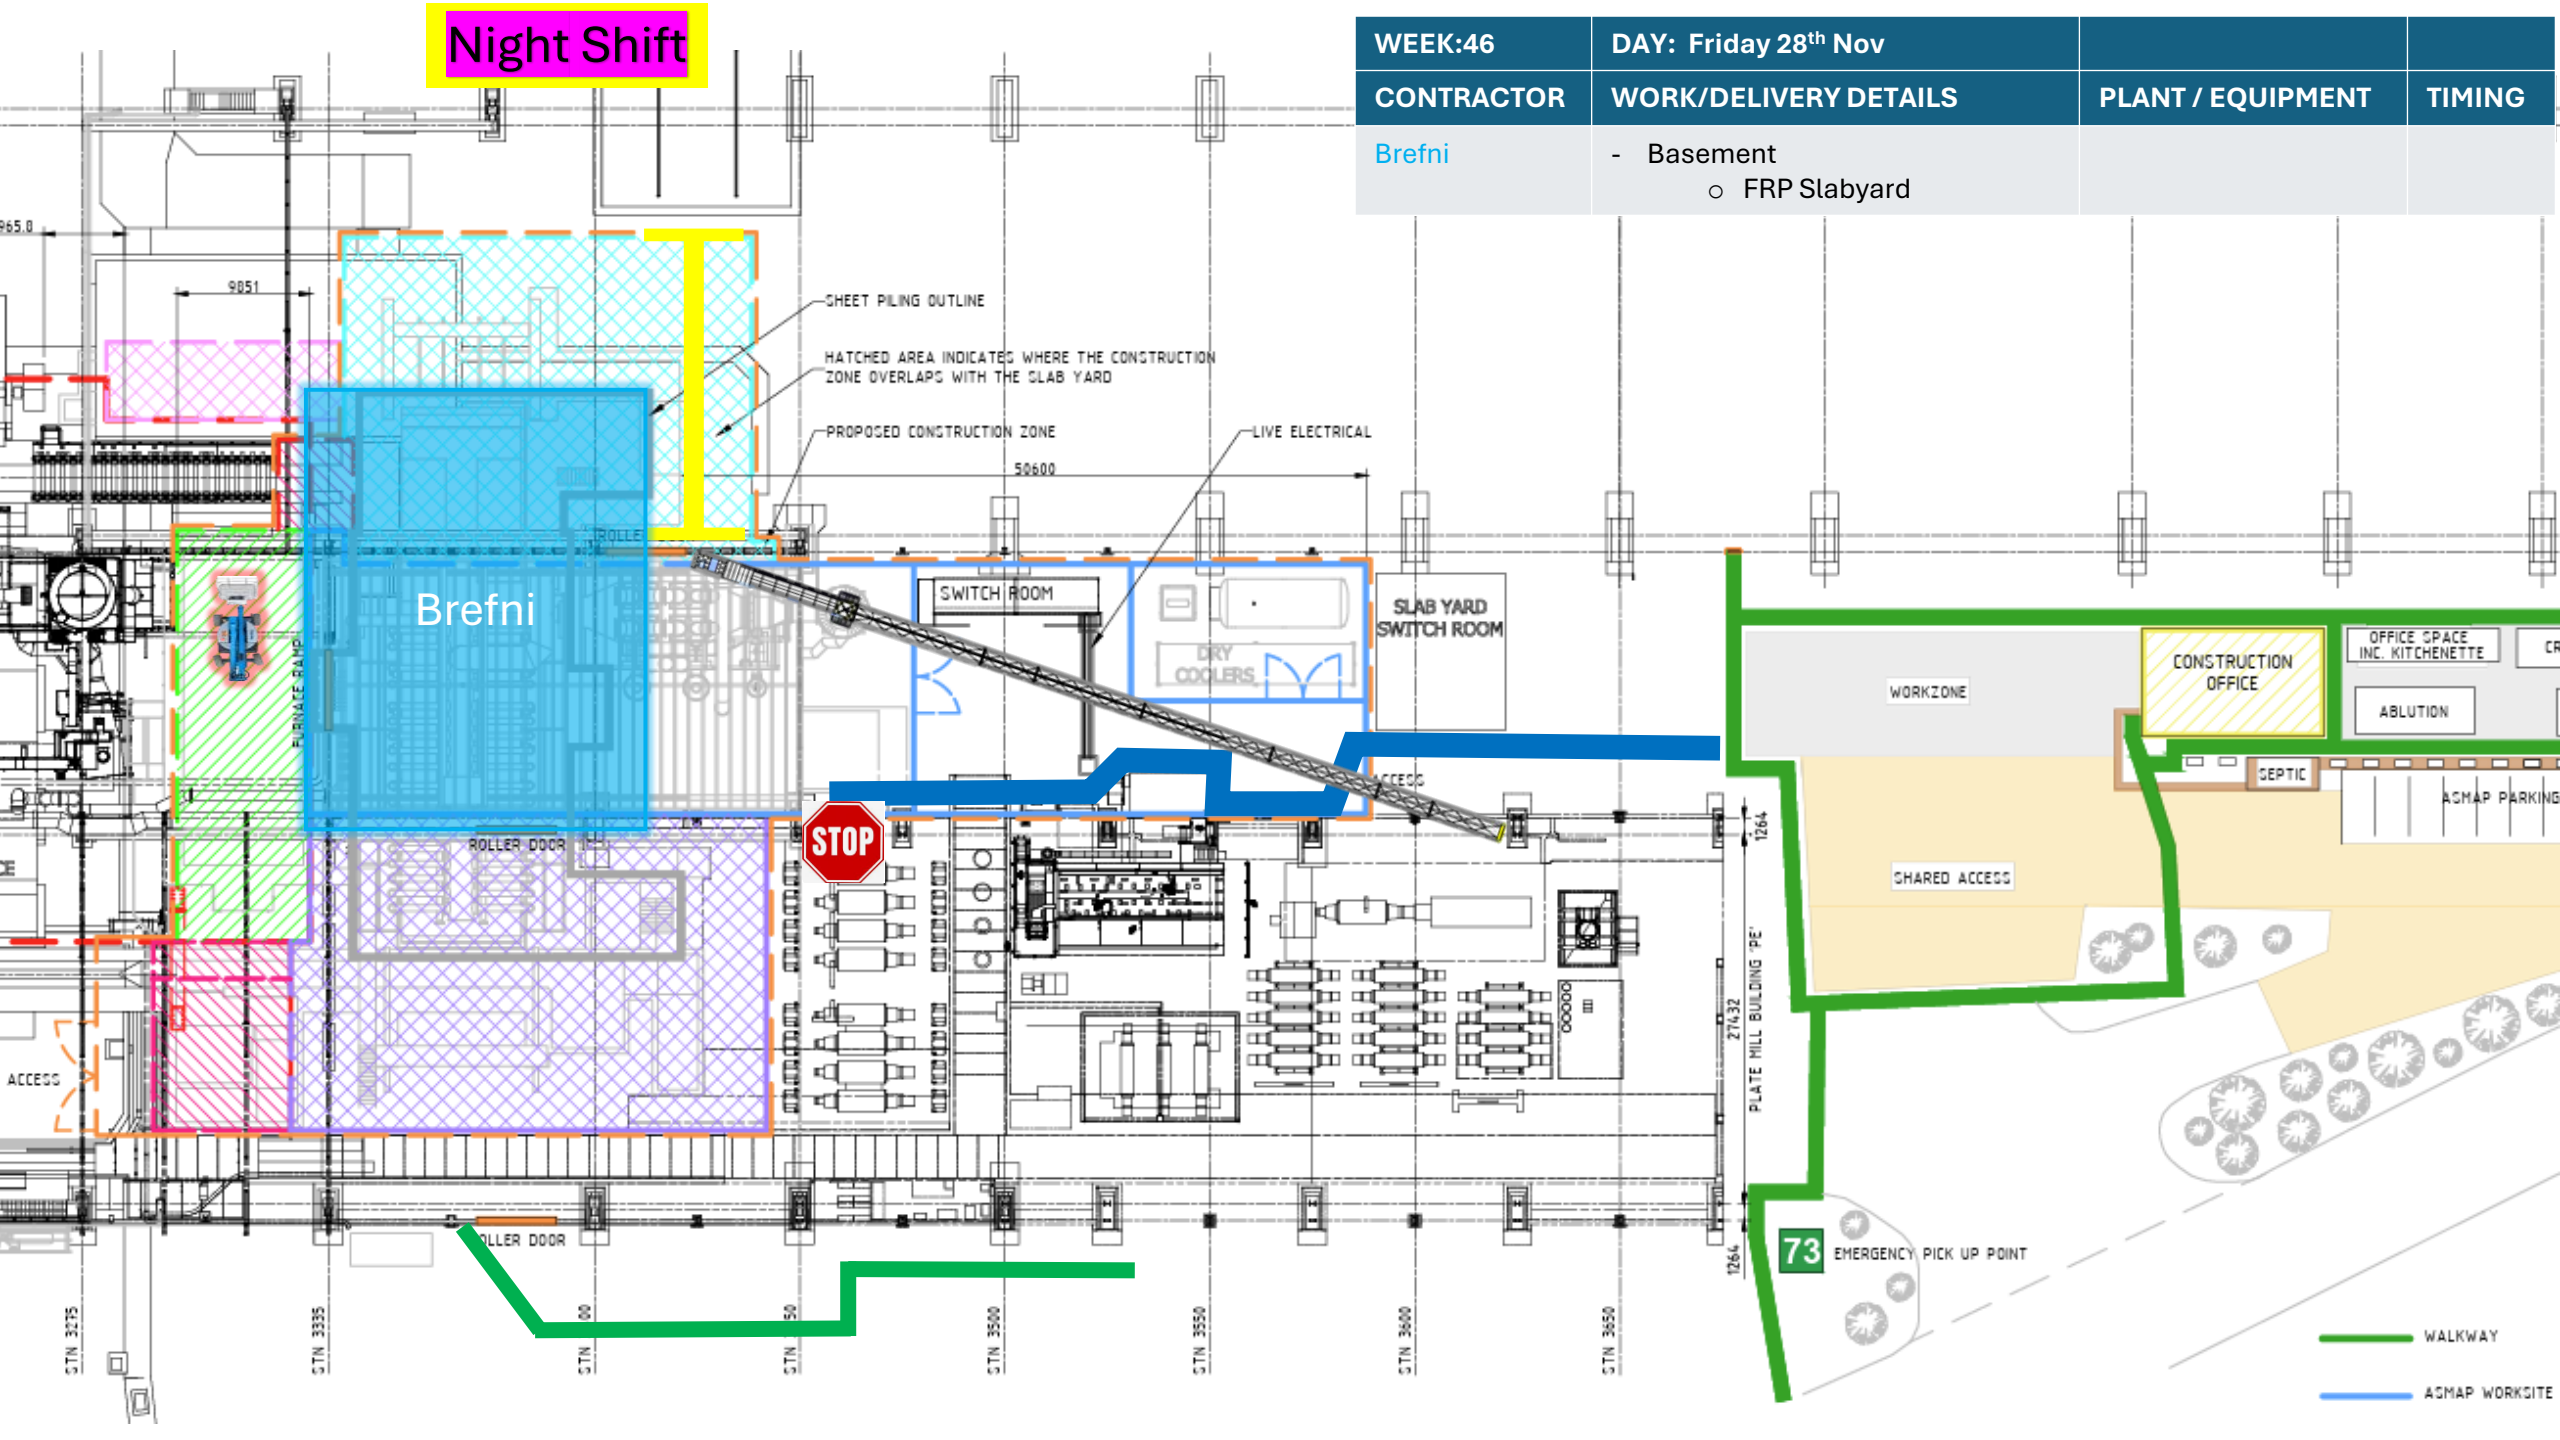


Day Shift

WEEK:46	DAY: Saturday 29 th Nov		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING
IES	<ul style="list-style-type: none">- Building extension<ul style="list-style-type: none">- Survey link beams- Drill link beams- Punch list items		
Programmed	<ul style="list-style-type: none">- PlateMill Roller Door<ul style="list-style-type: none">o Down Pipe install	EWP Mobile	

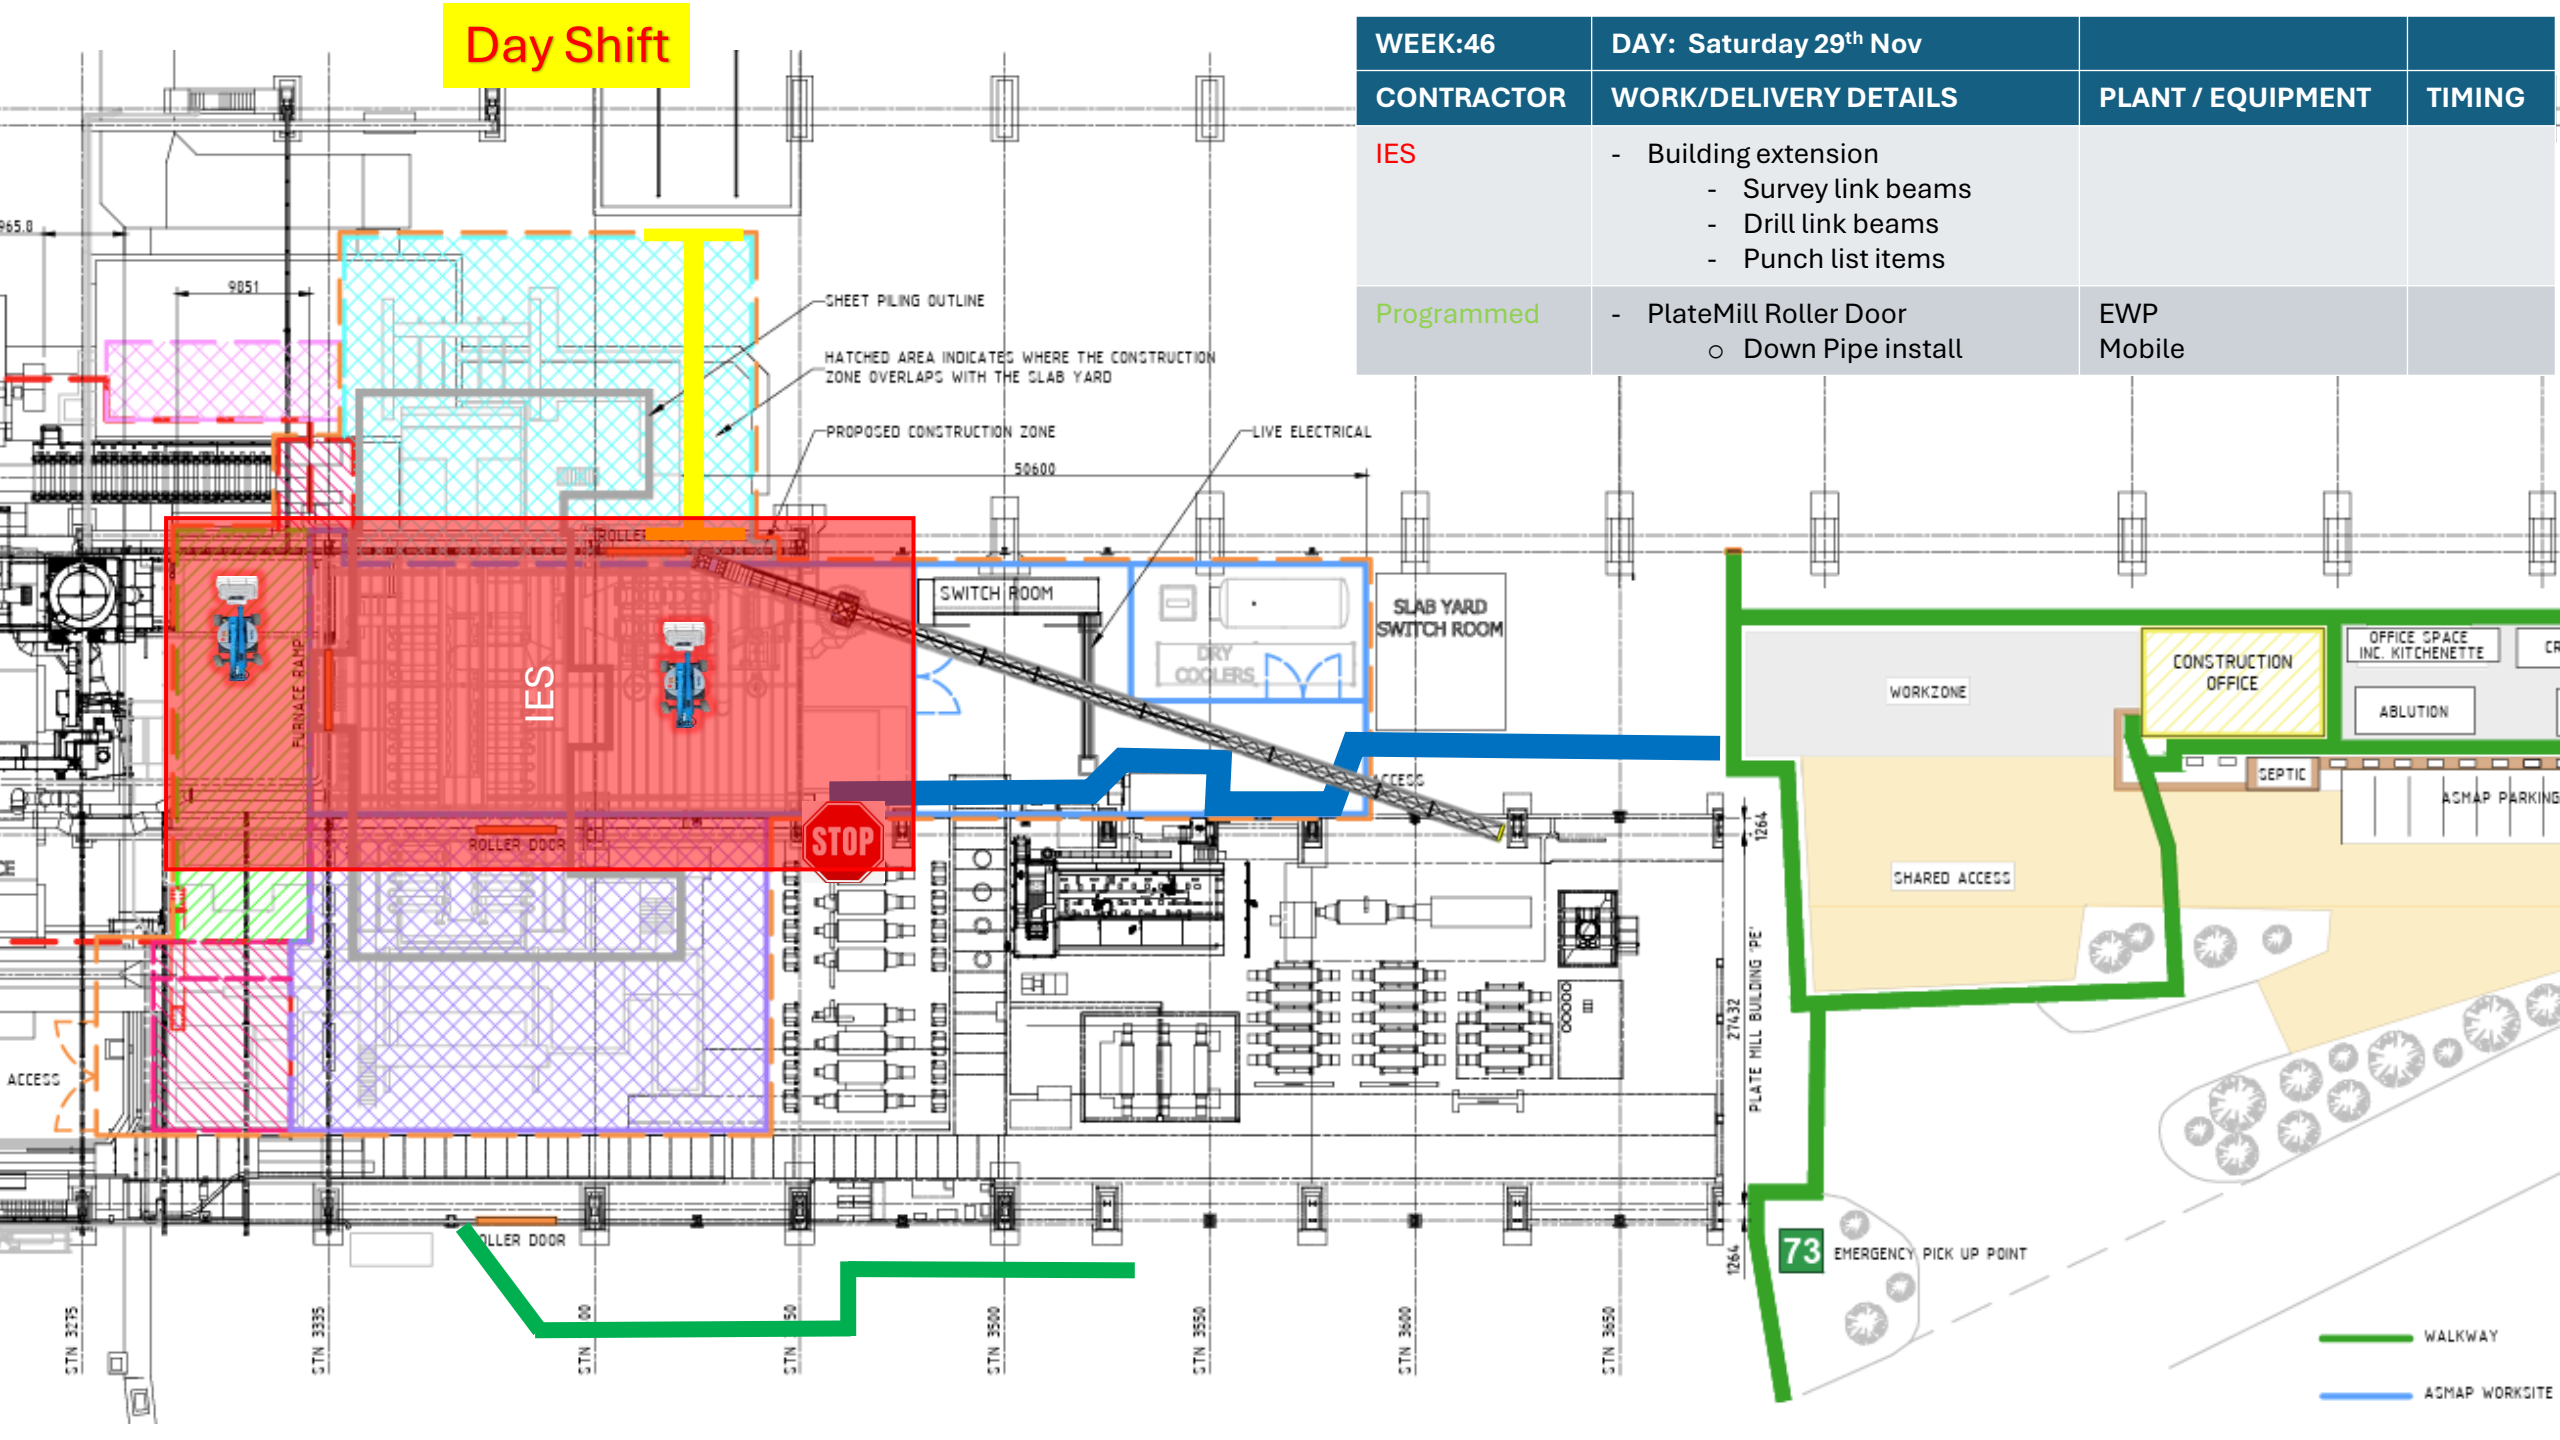


Night Shift

WEEK:46	DAY: Saturday 29 th Nov		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING

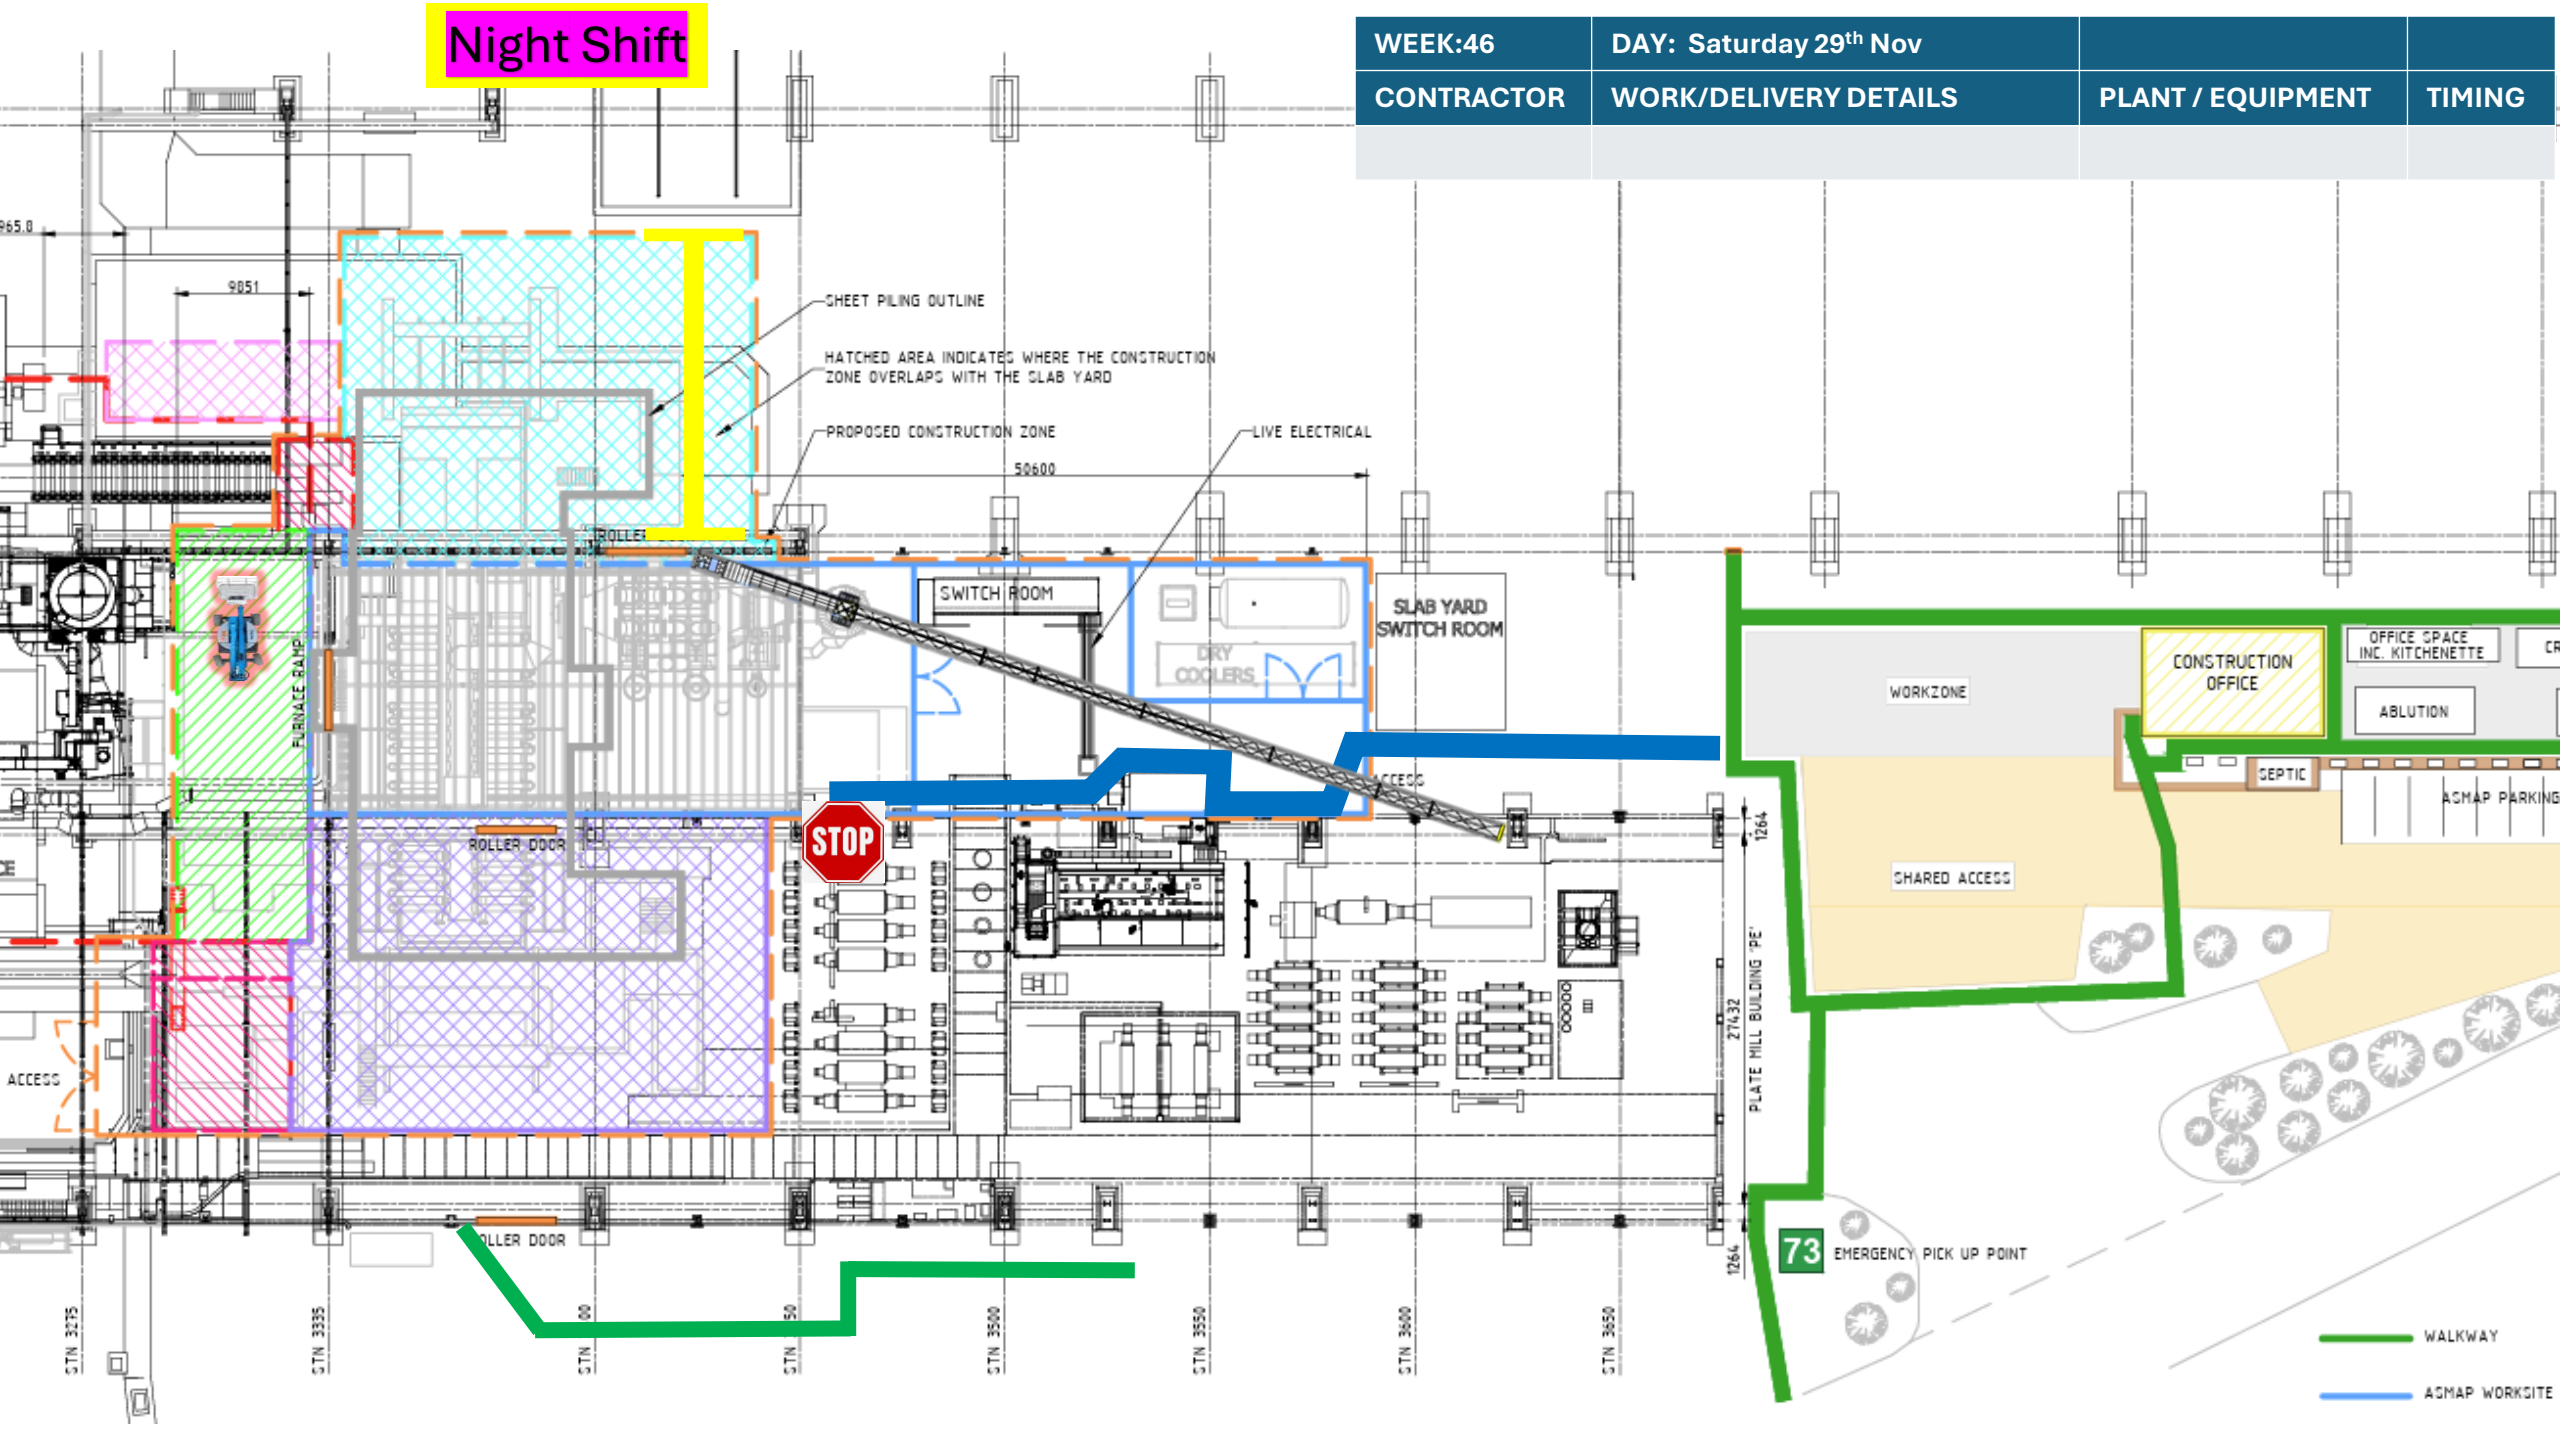

Night Shift

WEEK:46	DAY: Sunday 30 th Nov		
CONTRACTOR	WORK/DELIVERY DETAILS	PLANT / EQUIPMENT	TIMING

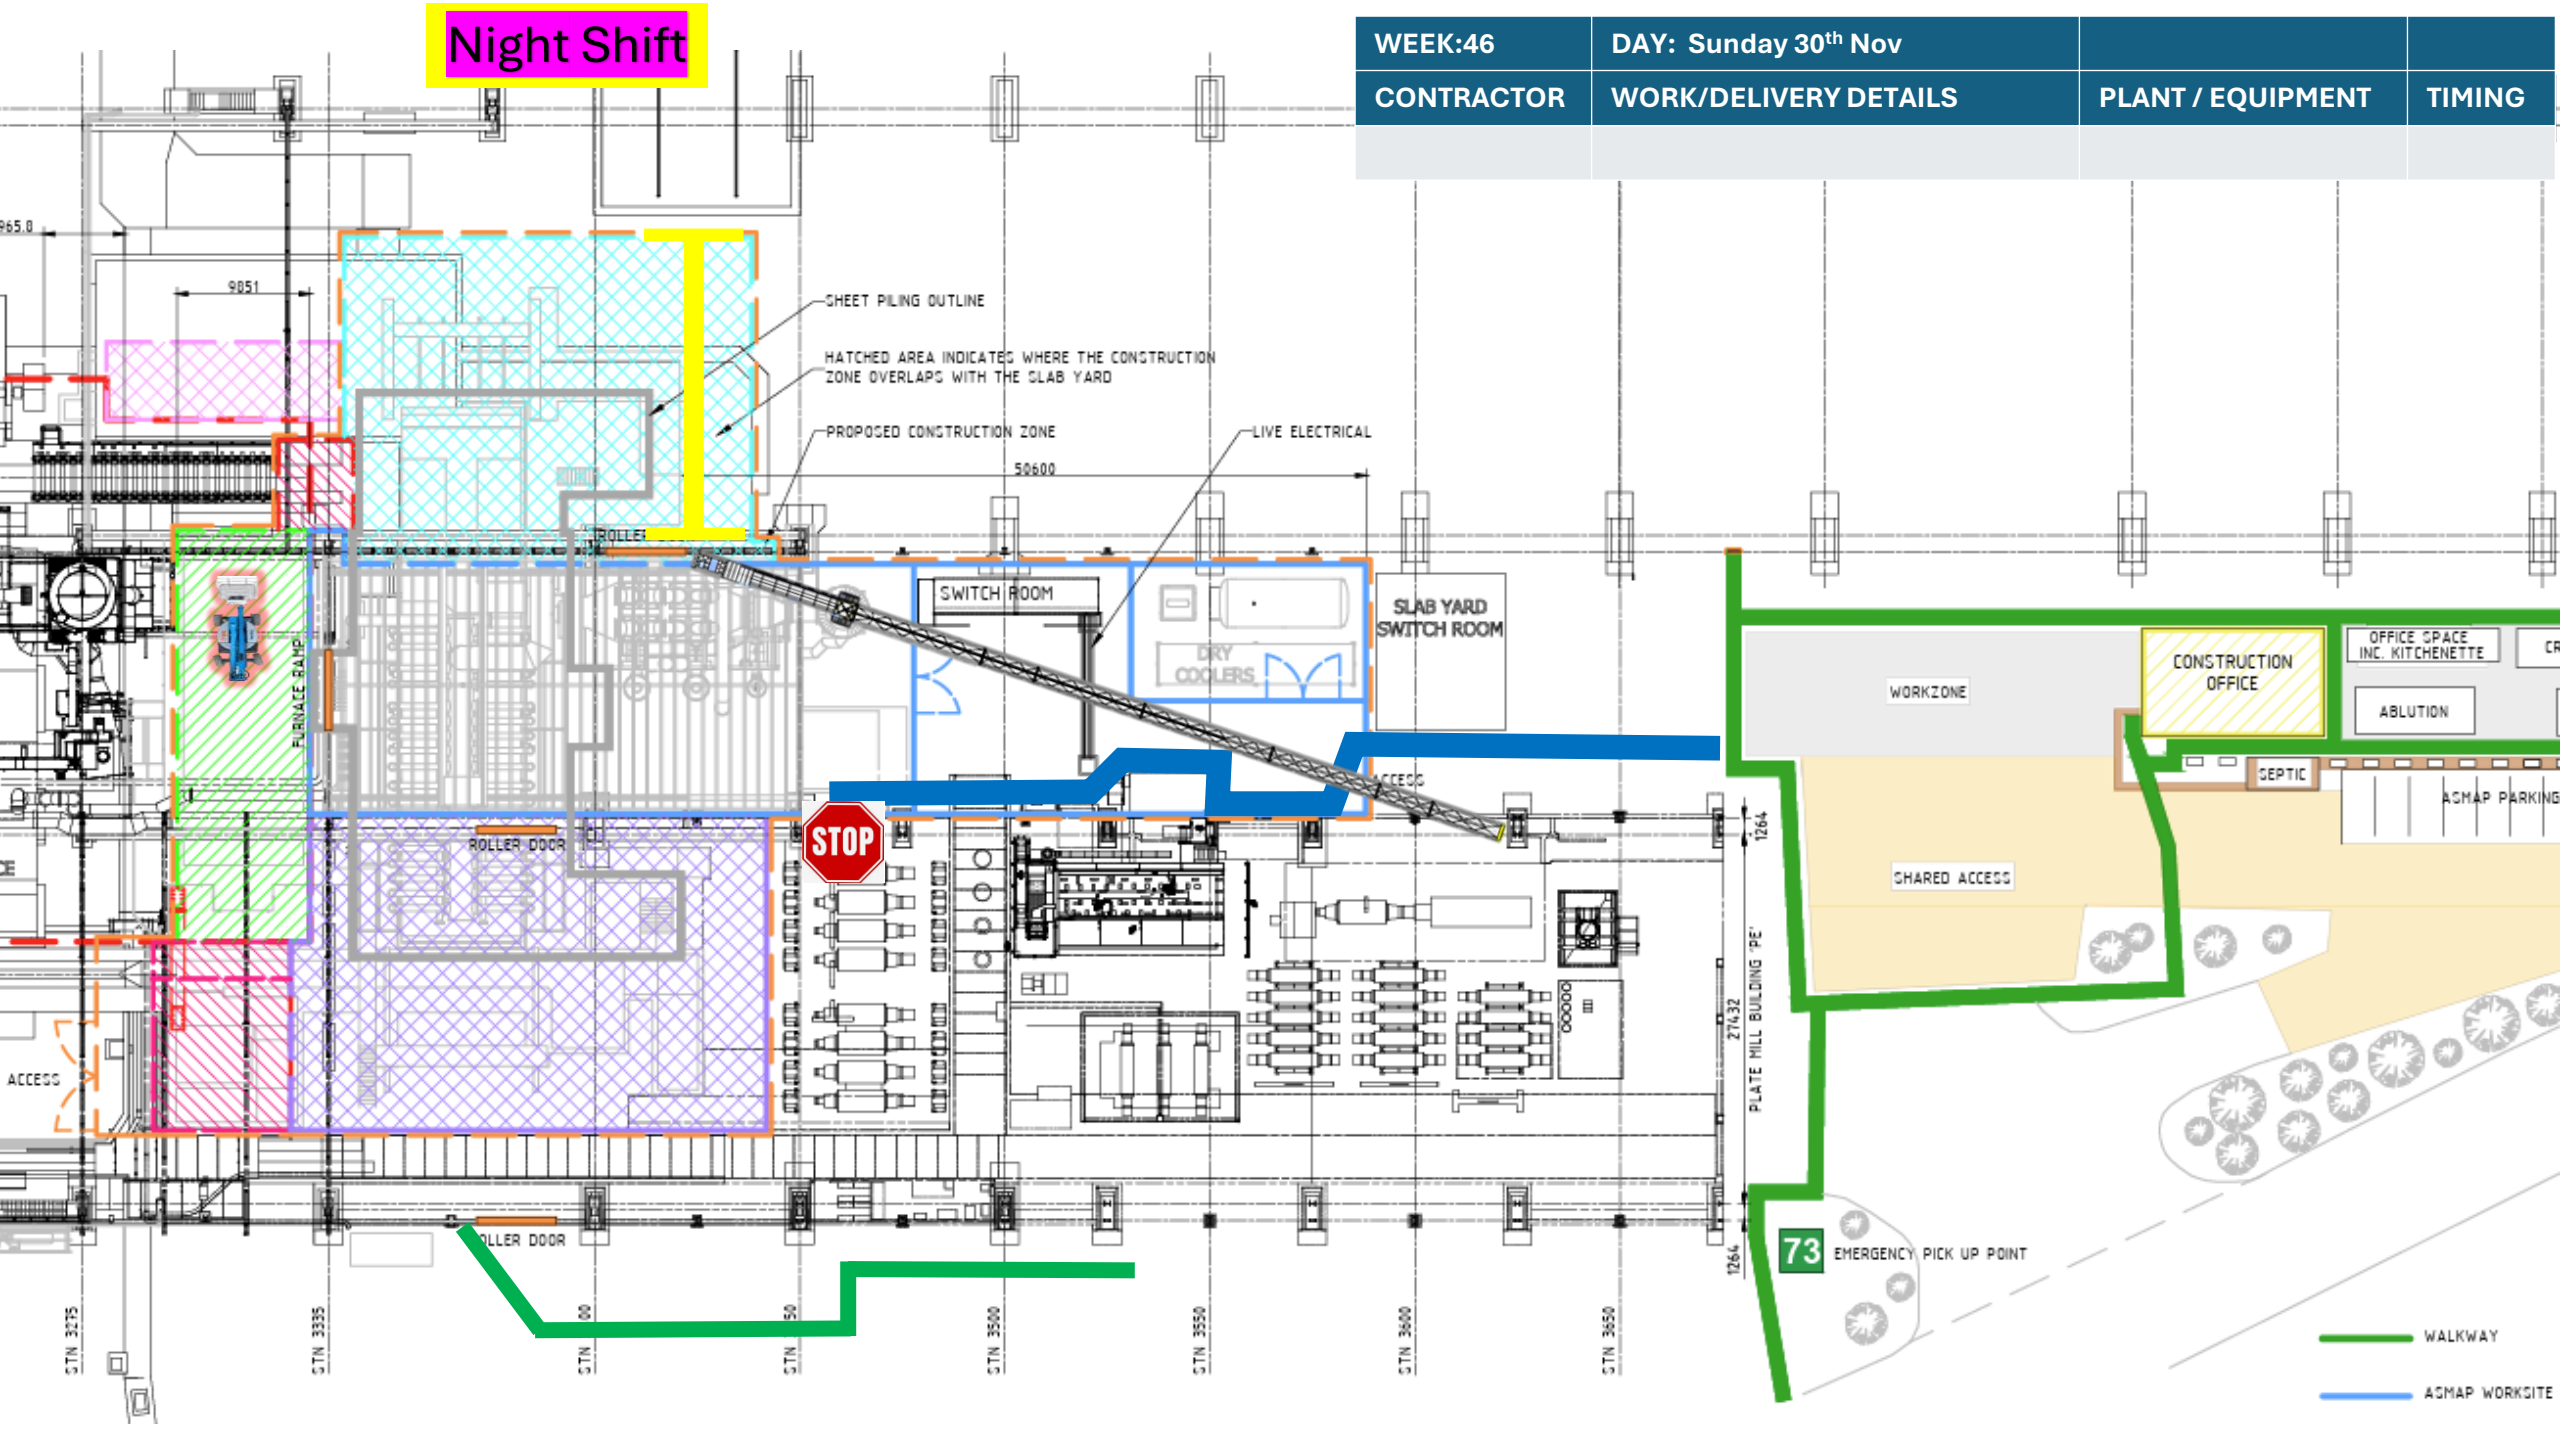

PLANT AND VEHICLES

Copy into drawings. Not to scale



30T Excavator



80T Mobile
Crane




Bogie



Semi




Agi

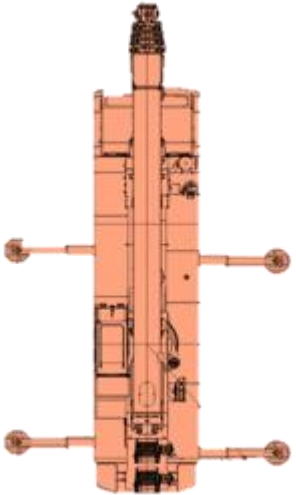

80T Mobile
Crane



Mobile Crane

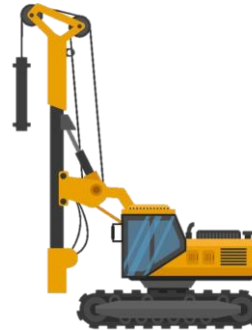

Piling Rig



Franna



Low loader trailer

PLANT AND VEHICLES

These images are approximately to scale, please copy into the interaction drawing.




80 ft EWP



5T Excavator



Bogie




Agi



Front
Dumper



Forklift



80T Crane



14T Excavator



Semi Trailer



30T Excavator



SITE INTERACTIONS

- Add to the site map:
 - The Plant/Vehicle/Equipment that the contractor will be using predominately for that week.
 - Storage of materials.
- Add details of work into the table for each contractor.
- Locks on – 07 October - 0600
- Locks off – 26 October - 1700
